



19 April 2021

Ridgeland High School | Football Field Turf & Track Replacement
WBA Project No. 5620



ADDENDUM NO. 01

NOTICE TO ALL DOCUMENT HOLDERS:

The following additions, deletions, changes and clarifications to the drawings and specifications are to be included as part of the Contract Documents.

GENERAL

ITEM NO. 1

NOTICE FOR PRE-BID

An optional Pre-Bid meeting will be held on Thursday, April 21, 2021 at the Office of the Madison County School District at 10:30 am.

SPECIFICATIONS

ITEM NO. 2

SECTION 00.5000 – Contracting Forms and Supplements

Part 1, Paragraph 2

CLARIFICATION: The Owner has developed standard versions of the AIA A101 (including Exhibits A & B) and the AIA A201. These form forms will constitute the basis of the Contract for Construction and draft versions are attached for the bidders' reference.

DRAWINGS

ITEM NO. 3

EARTHWORK, SUBGRADE REPAIR and OTHER CIVIL ITEMS

CLARIFICATION

Additional site demolition, over excavation, backfill, storm repair and replacement, field and track base repair and replacement and other civil items are to be included in the scope of the work, in addition to the Track and Turf removal and replacement scope of work, issued in the Bid Documents dated April 8, 2021.

ADD sheets C001, C101, C111, C112, C121, C131, C201, C202 and C203.

Encl: Draft of AIA A101, including Exhibits A & B
Draft of AIA A201
Sheets C001, C101, C111, C112, C121, C131, C201, C202 and C203

cc: All Document Holders
File 0120.C2

DRAFT AIA® Document A101™ – 2017

Standard Form of Agreement Between Owner and Contractor where the basis of payment is a Stipulated Sum

AGREEMENT made as of the date set forth on **Exhibit B**.

BETWEEN the Owner:

(Name, legal status, address and other information)

Madison County Schools
476 Highland Colony Parkway
Ridgeland, Mississippi 39157
(601) 499-0800

and the Contractor identified on **Exhibit B**.

for the following Project identified on **Exhibit B**.

The Architect is identified on **Exhibit B**.

The Owner and Contractor agree as follows.

ADDITIONS AND DELETIONS: The author of this document has added information needed for its completion. The author may also have revised the text of the original AIA standard form. An *Additions and Deletions Report* that notes added information as well as revisions to the standard form text is available from the author and should be reviewed.

This document has important legal consequences. Consultation with an attorney is encouraged with respect to its completion or modification.

The parties should complete A101™-2017, Exhibit A, Insurance and Bonds, contemporaneously with this Agreement. AIA Document A201™-2017, General Conditions of the Contract for Construction, is adopted in this document by reference. Do not use with other general conditions unless this document is modified.

ELECTRONIC COPYING of any portion of this AIA® Document to another electronic file is prohibited and constitutes a violation of copyright laws as set forth in the footer of this document.

TABLE OF ARTICLES

- 1 THE CONTRACT DOCUMENTS
- 2 THE WORK OF THIS CONTRACT
- 3 DATE OF COMMENCEMENT AND SUBSTANTIAL COMPLETION
- 4 CONTRACT SUM
- 5 PAYMENTS
- 6 DISPUTE RESOLUTION
- 7 TERMINATION OR SUSPENSION
- 8 MISCELLANEOUS PROVISIONS
- 9 ENUMERATION OF CONTRACT DOCUMENTS

EXHIBIT A INSURANCE AND BONDS

EXHIBIT B PROJECT DETAILS AND OTHER INFORMATION

ARTICLE 1 THE CONTRACT DOCUMENTS

§ 1.1 The Contract Documents consist of this Agreement, Conditions of the Contract (General, Supplementary, and other Conditions), all sections of the Project Manual, including Drawings, Specifications, and Addenda issued prior to execution of this Agreement, other documents listed in this Agreement, and Modifications issued after execution of this Agreement, all as amended and all of which form the Contract, and are as fully a part of the Contract as if attached to this Agreement or repeated herein. The Contract represents the entire and integrated agreement between the parties hereto and supersedes prior negotiations, representations, or agreements, either written or oral. An enumeration of the Contract Documents, other than a Modification, appears in Article 9. Contract Documents also include the Advertisement for Bid and Instructions to Bidders.

§ 1.2 This Agreement, as amended, represents the entire and integrated agreement between the Owner and the Contractor and supersedes all prior negotiations, representations or agreements, either written or oral. In the event of conflict, terms and conditions contained in the Agreement, as amended, shall take precedence over terms and conditions contained in the General Conditions, as amended, and the terms and conditions in the General Conditions, as amended, shall take precedence over all other terms and conditions contained in the other Contract Documents. The Advertisement for Bid and Instructions to Bidders shall take precedence over the Contractor's bid or proposal, unless specifically agreed otherwise herein.

§ 1.3 The Madison County School District board of trustees (the "School Board"), by a majority vote, is the only representative of the Owner, an independent school district, having the power and authority to enter into or amend this Agreement, to approve and execute a Change Order or Construction Change Directive modifying the Contract Sum, or to agree to an extension to the date of Substantial or Final Completion.

§ 1.4 The School Board designates the authorized representatives identified in Paragraph 8.3 to act on its behalf in all other respects.

ARTICLE 2 THE WORK OF THIS CONTRACT

§ 2.1 The Contractor shall fully execute the Work described in the Contract Documents, except as specifically indicated in the Contract Documents to be the responsibility of others.

§ 2.2 Contractor shall, at its own expense as part of the Contract Sum, secure all licenses, furnish all labor, material, plant, office space, tools, equipment, machinery, scaffolding, cartage, electric current for power purposes and provide all other things and personnel necessary for the full and diligent prosecution of the Work, all in compliance with applicable statutes, building codes, ordinances and regulations and in a first class workmanlike

manner in strict accordance with the requirements of the Project as well as the directions of the Project Architect and to the reasonable satisfaction of the Owner. Contractor shall be responsible for supervision, coordination of its sub-trades, and for the performance of all actions reasonably required to complete the Work even if not specifically shown in the plans and specifications but can be reasonably inferred.

§ 2.3 The Contractor is required to furnish a payment and performance bond. Such bonds shall be executed by it with a fidelity or surety company authorized to transact business in Mississippi in form and amount satisfactory to the Owner. The Performance Bond shall guarantee the faithful performance of all contract obligations of this Contract. The Payment Bond shall comply with the requirements of Mississippi regarding unconditional payment bonds and assure the prompt payment of all claims of lienors and laborers. The cost of the bond shall be included within the Contract Sum.

ARTICLE 3 DATE OF COMMENCEMENT AND SUBSTANTIAL COMPLETION

§ 3.1 The date of commencement of the Work shall be set forth on Exhibit B.

§ 3.2 The Contract Time shall be measured from the date of commencement of the Work through Final Completion.

§ 3.3 Substantial Completion

§ 3.3.1 Subject to adjustments of the Contract Time as provided in the Contract Documents, the Contractor shall achieve Substantial Completion of the entire Work by the date set forth on Exhibit B.

§ 3.3.2 Subject to adjustments of the Contract Time as provided in the Contract Documents, if portions of the Work are to be completed prior to Substantial Completion of the entire Work, the Contractor shall achieve Substantial Completion of such portions by the date set forth in Exhibit B.

§ 3.4 Time is of the essence and a material consideration of the Contract. The Contractor acknowledges and recognizes that the Owner is entitled to full and beneficial occupancy and use of the completed Work following expiration of the Contract Time. The Contractor further acknowledges and agrees that if the Contractor fails to complete substantially or cause the Substantial Completion of any portion of the Work in either of the specified phases within the Contract Time, the Owner will sustain extensive damages and serious loss as a result of such failure. The exact amount of such damages will be extremely difficult to ascertain. Therefore, the Owner and the Contractor agree to liquidated damages as set forth below in this Paragraph 3.4. The term substantial completion is as defined in Article 9.8.1 of the General Conditions.

§ 3.4.1 Subject to the requirements of Article 8.3 of the General Conditions, if the Contractor fails to achieve Substantial Completion of the Work within the Contract Time, the Owner shall be entitled to retain or recover from the Contractor, as liquidated damages and not as a penalty, the per diem amount of \$500.00 commencing upon the first day following expiration of the Contract Time and continuing until the actual Date of Substantial Completion.

§ 3.4.2 These Liquidated Damages are agreed to be a good faith and reasonable pre-estimate of the Owner's actual damages and are not considered to be a penalty. Contractor and Owner hereby acknowledge and agree that Owner's right to Liquidated Damages hereunder is not intended to be exclusive of any other right, power, or remedy of Owner hereunder or under any other Contract Documents for other defaults by Contractor (i.e., defaults not arising under this Subsection 3.4), but each and every such right, power and remedy shall be cumulative and concurrent and shall be in addition to the right to Liquidated Damages provided for in this Paragraph 3.4.

§ 3.4.3 The Owner may deduct liquidated damages described in this Paragraph 3.4 from any unpaid amounts then or thereafter due the Contractor under this Agreement. Any liquidated damages not so deducted from any unpaid amounts due the Contractor shall be payable to the Owner at the demand of the Owner, together with interest from the date of the demand at a rate equal to the highest lawful rate of interest payable by the Contractor.

ARTICLE 4 CONTRACT SUM

§ 4.1 The Owner shall pay the Contractor the Contract Sum in current funds for the Contractor's performance of the Contract. The Contract Sum is set forth in Exhibit B and is subject to additions and deductions as provided in the Contract Documents. To the extent the Cost of the Work exceeds the Contract Sum, the Contractor shall bear such costs in excess of the Contract Sum without reimbursement or additional compensation from the Owner.

§ 4.1.1 The Contract Sum contains an Owner's Contingency in the amount set forth on Exhibit B. This contingency is for the sole use of the Owner to be used for changes in the scope of Work, if any, or for the betterment of the Project. Owner's authorized representative may approve any expenditure from Owner's Contingency without further School Board approval. If the Owner's Contingency is not expended or not fully expended, then any unused portion shall belong to the Owner and shall be credited to the Owner in calculating final payment.

§ 4.2 Alternates, if any, are set forth on Exhibit B.

ARTICLE 5 PAYMENTS

§ 5.1 Progress Payments

§ 5.1.1 Based upon Applications for Payment submitted to the Architect and Owner by the Contractor and Certificates for Payment issued by the Architect, the Owner shall make progress payments on account of the Contract Sum to the Contractor as provided below and elsewhere in the Contract Documents.

§ 5.1.2 The period covered by each Application for Payment shall be one calendar month ending on the last day of the month. The Contractor shall submit monthly Applications for Payment for approval to both the Architect and Owner on AIA Form G702, or such other form agreed to in writing by Owner and Contractor. Continuation sheets shall be submitted on AIA Form G703. If the Architect and Owner approve the application, then the Architect shall submit a Certificate for Payment to the Owner. The Architect and Owner may require any additional information deemed necessary and appropriate to substantiate the Application for Payment. Materials that are verified to be on the jobsite or other approved location for use in the Project may also be incorporated into the Application for Payment

§ 5.1.3 Provided that an Application for Payment is received by the Architect and Owner not later than the « 1st » day of a month, the Owner shall make payment of the amount certified to the Contractor not later than the « 15th » day of the following month. If an Application for Payment is received by the Architect and Owner after the application date fixed above, payment of the amount certified shall be made by the Owner not later than « sixty » (« 60 ») days after the Architect receives the Application for Payment.

(Federal, state or local laws may require payment within a certain period of time.)

§ 5.1.4 Each Application for Payment shall be based on the most recent schedule of values submitted by the Contractor in accordance with the Contract Documents. The schedule of values shall allocate the entire Contract Sum, less any unused Owner's Contingency, among the various portions of the Work. The schedule of values shall be prepared in such form, and supported by such data to substantiate its accuracy, as the Architect and Owner may require. This schedule of values shall be used as a basis for reviewing the Contractor's Applications for Payment.

§ 5.1.5 Applications for Payment shall show the percentage of completion of each portion of the Work as of the end of the period covered by the Application for Payment.

§ 5.1.6 Subject to other provisions of the Contract Documents, the amount of each progress payment shall be computed as follows:

§ 5.1.6.1 The amount of each progress payment shall first include:

- .1 That portion of the Contract Sum properly allocable to completed Work;
- .2 That portion of the Contract Sum properly allocable to materials and equipment delivered and suitably stored at the site for subsequent incorporation in the completed construction, or, if approved in advance by the Owner, suitably stored off the site at a location agreed upon in writing; and
- .3 That portion of Construction Change Directives that the Architect determines, in the Architect's professional judgment, to be reasonably justified.

§ 5.1.6.2 The amount of each progress payment shall then be reduced by:

- .1 The aggregate of any amounts previously paid by the Owner;
- .2 The amount, if any, for Work that remains uncorrected and for which the Architect or Owner has previously withheld or nullified a Certificate for Payment as provided in Article 9 of AIA Document A201-2017;
- .3 Any amount for which the Contractor does not intend to pay a Subcontractor or material supplier, unless the Work has been performed by others the Contractor intends to pay;

- .4 For Work performed or defects discovered since the last payment application, any amount for which the Architect may withhold payment, or nullify a Certificate of Payment in whole or in part, as provided in Article 9 of AIA Document A201–2017;
- .5 Retainage withheld pursuant to Section 5.1.7; and
- .6 If Owner is entitled to deduct liquidated damages, or any other damages or amounts provided in the Contract Documents, including clean-up fees, then Owner shall be entitled to deduct such liquidated damages, amounts and fees at any time.

§ 5.1.7 Retainage

§ 5.1.7.1 For each progress payment made prior to Substantial Completion of the Work, the Owner may withhold the amount set forth in Exhibit B, as retainage, from the payment otherwise due.

§ 5.1.7.1.1 To the extent any items are not subject to retainage, they shall be set forth on Exhibit B.

§ 5.1.7.2 There shall be no reduction or limitation of retainage, unless agreed to in writing by Owner.

§ 5.1.8 If final completion of the Work is materially delayed through no fault of the Contractor, the Owner shall pay the Contractor any additional amounts in accordance with Article 9 of AIA Document A201–2017.

§ 5.1.9 Except with the Owner's prior approval, the Contractor shall not make advance payments to suppliers for materials or equipment which have not been delivered and stored at the site.

§ 5.2 Final Payment

§ 5.2.1 Final payment, constituting the entire unpaid balance of the Contract Sum minus disputed sums, authorized deductions and liquidated damages, shall be made by the Owner to the Contractor when

- .1 the Contractor has fully performed the Contract except for the Contractor's responsibility to correct nonconforming Work as provided in Article 12 of AIA Document A201–2017, and to satisfy other requirements, if any, which extend beyond final payment;
- .2 the Contractor has provided all documents required by Sections 3.5 et seq. and 9.10.2 of the General Conditions; and
- .3 a final Certificate for Payment has been issued by the Architect and approved by the Owner.

§ 5.2.2 The Owner's final payment to the Contractor shall be made no later than 45 days after the issuance of the Architect's final Certificate for Payment, and Owner's School Board vote.

§ 5.3 Payment Procedures

§ 5.3.1. Subject to the provisions of Article 9 of the General Conditions, the following payment procedures shall also apply to both progress and final payments.

1. At the time of the submission of an Application for Payment the Contractor shall furnish to the Contractor: (1) a certification of work performed on a form approved by the Owner; (2) waivers of lien for all work done by Contractor, all lienors giving notice and any such other persons, firms or corporations performing work in accordance with the Contract Documents to the date of the application for payment; and (3) evidence of payment to all laborers working directly or indirectly for the Contractor through the date of the application for payment. The Owner shall have the right at any time and in its sole discretion to make payments directly to laborers and/or material men and/or sub-contractors of the Contractor, or to make any such payments jointly to such payees and the Contractor.

2. Payments made to the Contractor are received by it in trust to be applied first to the amount owing to any person who has performed labor or furnished materials to the Contractor for the performance and work under this agreement and before the Contractor shall use any monies received for any other purposes.

3. Partial or final payment will not be payable or due at the option of the Owner in the event that any of the following conditions exist: (1) Defective or damaged work is not remedied by Contractor; (2) Claims have been filed by laborers, material men and/or subcontractors under this agreement; (3) Contractor fails to make the proper application for payment or fails to comply with Mississippi's mechanics lien law; (4) Contractor becomes bankrupt or insolvent; (5) This agreement or any other agreement between Owner and Contractor is in breach; and (6) Any insurance required of Contractor ceases to be effective and in force.

4. Acceptance of final payment by Contractor operates as a release to the Owner of all claims and liability to the Contractor for all construction work performed by Contractor.

§ 5.3.2 The compensation payable to the Contractor hereunder shall not be increased because of the imposition of any taxes, or of increases in the price of any labor, material or services.

§ 5.3.3 No payment made hereunder shall operate as an admission on the part of the Owner that this Agreement, or any part thereof has been complied with, or preclude any action for damages against the Contractor should this Agreement not be faithfully executed in every respect or should the Work furnished and installed by the Contractor not meet with the approval of the Owner

§ 5.4 Payments due and unpaid under the Contract shall bear interest from the date payment is due at the legal rate prevailing from time to time at the place where the Project is located.

ARTICLE 6 DISPUTE RESOLUTION

§ 6.1 Mediation

Any claim, dispute, or other matter in question arising out of or related to this Agreement, if not resolved within 14 days following the notice of claim through discussions among the parties' officers having authority to resolve the claim, dispute, or other matter, shall be subject to mediation as a condition precedent to litigation. The parties shall work in good faith to select and agree upon a mediator within thirty (30) days after a demand for mediation is made by either party. If the parties cannot agree upon a mediator, then each party shall designate their preferred mediator as a representative. Each party's mediator representative shall then select a mediator that will conduct the mediation between the parties. If such matter relates to or is the subject of a lien arising out of the Contractor's services, the Contractor may proceed in accordance with applicable law to comply with the lien notice or filing deadlines prior to resolution of the matter by mediation or litigation.

§ 6.2 Binding Dispute Resolution

For any Claim subject to, but not resolved by, mediation pursuant to Article 15 of AIA Document A201-2017, the method of binding dispute resolution shall be litigation in a court of competent jurisdiction.

ARTICLE 7 TERMINATION OR SUSPENSION

§ 7.1 The Contract may be terminated by the Owner for cause or for convenience after ten (10) calendar days' written notice to Contractor. Further, Owner or the Contractor may terminate this Agreement as provided in Article 14 of AIA Document A201-2017.

§ 7.2 The Work may be suspended by the Owner as provided in Article 14 of AIA Document A201-2017.

ARTICLE 8 MISCELLANEOUS PROVISIONS

§ 8.1 Where reference is made in this Agreement to a provision of AIA Document A201-2017 or another Contract Document, the reference refers to that provision as amended or supplemented by other provisions of the Contract Documents.

§ 8.2 The Owner's representative is set forth on Exhibit B.

§ 8.3 The Contractor's representative is set forth on Exhibit B.

§ 8.4 Neither the Owner's nor the Contractor's representative shall be changed without ten days' prior notice to the other party.

§ 8.5 Insurance and Bonds

§ 8.5.1 The Owner and the Contractor shall purchase and maintain insurance as set forth in AIA Document A101™-2017, Standard Form of Agreement Between Owner and Contractor where the basis of payment is a Stipulated Sum, Exhibit A, Insurance and Bonds, and elsewhere in the Contract Documents.

§ 8.5.2 The Contractor shall provide bonds as set forth in AIA Document A101™-2017 Exhibit A, and elsewhere in the Contract Documents.

§ 8.6 Notice in electronic format, pursuant to Article 1 of AIA Document A201–2017, may be given in accordance with AIA Document E203™–2013, Building Information Modeling and Digital Data Exhibit, if completed, or as otherwise set forth in Exhibit B.

§ 8.7 Other provisions:

§ 8.7.1 The Agreement shall be governed by the laws of the State of Mississippi, and the mandatory and exclusive venue of any and all litigation shall be in Madison County, Mississippi.

§ 8.7.2 As a material consideration of the making of this Agreement, the modifications to this Agreement shall not be construed against the maker of said modifications.

§ 8.7.3 Notwithstanding anything to the contrary in this Agreement, or in any document forming a part hereof, there shall be no mandatory arbitration for any dispute arising hereunder.

§ 8.7.4 Article 1 of the General Conditions shall govern Contractor's use of the Construction Documents.

§ 8.7.5 The Contractor shall be responsible to the Owner for acts and omissions of the Contractor's employees, Subcontractors and their agents and employees, and other persons or entities performing portions of the Work for, or on behalf of, the Contractor or any of its Subcontractors. As part of that responsibility, Contractor shall enforce the Owner's alcohol-free, drug-free, tobacco-free, harassment-free and weapon-free policies and zones, which will require compliance with those policies and zones by Contractor's employees, subcontractors, and all other persons carrying out the Contract. Further, Contractor shall use commercially reasonable efforts to perform background checks on all Contractor's employees, Subcontractors and their agents and employees, and other persons or entities performing portions of the Work for, or on behalf of, the Contractor or any of its Subcontractors and for which will be present at the jobsite for the Project.

§ 8.7.6 Contractor shall require all construction workers, whether Contractor's own forces or the forces of Contractor's subcontractors, to wear identification tags on the front of their persons during all times that they are on Owner's property. Such identification tags shall contain a current photograph and the worker's full name in a typeface large enough to be seen from a reasonable distance.

§ 8.7.7 Contractor shall require all construction workers, whether Contractor's own forces or the forces of Contractor's subcontractors, to park their personal motor vehicles on Owner's property only in the parking places designated by the Owner's campus principal. Any vehicles not parked in the appropriate locations shall be towed at the vehicle owner's sole expense.

§ 8.7.8 Contractor shall follow, and shall require all employees, agents or subcontractors to follow applicable ordinances of the municipality in which the Project is located.

§ 8.7.9 Contractor shall institute a theft deterrence program designed to restrict construction worker access to properties of Owner that are currently in use, to maintain supervision of Contractor's and Contractor's subcontractor's forces, and to reimburse the Owner or those persons suffering a theft loss which results from Contractor's forces or Contractor's subcontractor's forces' actions, omissions, or failure to secure the Work or adjoining property.

§ 8.7.10 The Contractor may not assign its responsibilities, duties, obligations and rights under this Agreement, without the express written consent of the Owner. This does not prevent Contractor from engaging subcontractors to perform various phases of the Project, but Contractor shall be fully responsible to Owner for the work, actions and omissions of all such subcontractors.

§ 8.7.11 This Agreement, in its entirety, shall be binding upon all the parties hereto, their respective successors, heirs, executors, administrators or assigns.

§ 8.7.12 Execution of this Agreement shall constitute approval and acceptance of all terms, covenants and conditions as modified and contained in the Contract Documents.

§ 8.7.13 This Agreement is subject to all applicable federal and state laws, rules, and regulations. Invalidity of any portion of this Agreement under the laws of the State of Mississippi or of the United States shall not affect the validity of the remainder of this Agreement.

§ 8.7.14 By signing this Agreement, Contractor represents and warrants the following to the Owner (in addition to any other representations and warranties contained in the Contract Documents), as a material inducement to the Owner to execute this Agreement, which representations and warranties shall survive the execution and delivery of this Agreement, any termination of this Agreement, and the final completion of the Work

- .1 The Contractor is authorized to do business in Mississippi under Mississippi Code §31-3-1 et seq. and is otherwise properly licensed by all necessary governmental and public and quasi-public authorities having jurisdiction over the Contractor and over the Work and the Project.
- .2 Contractor is financially solvent, able to pay all debts as they mature, and possessed of sufficient working capital to complete the Work and perform all obligations hereunder and that it has no reasonable belief that any of its subcontractors are not are financially solvent, able to pay all debts as they mature, and possessed of sufficient working capital to complete their respective portion of the Work.
- .3 The Contractor is able to furnish the plant, tools, materials, supplies, equipment, and labor required to complete the Work and perform its obligations hereunder and has sufficient experience and competence to do so.
- .4 The Contractor's execution of this Agreement and performance thereof is within the Contractor's duly authorized powers.
- .5 The Contractor's duly authorized representative has visited the site of the Project, is familiar with the local conditions under which the Work is to be performed, and has correlated observations with the requirements of the Contract Documents.
- .6 The Contractor possesses a high level of experience and expertise in the business administration, construction, construction management, and superintendence of projects of the size, complexity, and nature of this particular Project and will perform the Work with the care, skill, and diligence of such a contractor.

§ 8.7.15 No delay or omission by Owner in exercising any right or power accruing upon the noncompliance or failure of performance by Contractor of any of the provisions of this Agreement shall impair any such right or power or be construed to be a waiver thereof. A waiver by Owner of any of the covenants, conditions or agreements hereof to be performed by Contractor shall not be construed to be a waiver of any subsequent breach thereof or of any other covenant, condition or agreement herein contained.

§ 8.7.16 Contractor stipulates that Owner is a political subdivision of the State of Mississippi, and as such, enjoys immunities from suit and liability as provided by the Constitution and laws of the State of Mississippi. By entering into this Agreement, Owner does not waive any of its immunities from suit and/or liability, except as otherwise specifically provided herein and as specifically authorized by law.

ARTICLE 9 ENUMERATION OF CONTRACT DOCUMENTS

§ 9.1 This Agreement is comprised of the documents set forth on Exhibit B.

[signature page to follow]

This Agreement entered into as of the day and year first written above.

OWNER (Signature)

« »« »

(Printed name and title)

CONTRACTOR (Signature)

« »« »

(Printed name and title)



DRAFT AIA® Document A101™ – 2017

Exhibit A

Insurance and Bonds

TABLE OF ARTICLES

- A.1 GENERAL
- A.2 OWNER'S INSURANCE
- A.3 CONTRACTOR'S INSURANCE AND BONDS
- A.4 SPECIAL TERMS AND CONDITIONS

ARTICLE A.1 GENERAL

The Owner and Contractor shall purchase and maintain insurance, and provide bonds, as set forth in this Exhibit. As used in this Exhibit, the term General Conditions refers to AIA Document A201™–2017, General Conditions of the Contract for Construction.

ARTICLE A.2 OWNER'S INSURANCE

§ A.2.1 General

Prior to commencement of the Work, the Owner shall secure the insurance, and provide evidence of the coverage, required under this Article A.2 and, upon the Contractor's request, provide a copy of the property insurance policy or policies required by Section A.2.3. The copy of the policy or policies provided shall contain all applicable conditions, definitions, exclusions, and endorsements.

§ A.2.2 Liability Insurance

The Owner shall be responsible for purchasing and maintaining the Owner's usual general liability insurance.

§ A.2.3 Required Property Insurance

§ A.2.3.1 Unless this obligation is placed on the Contractor pursuant to Section A.3.3.2.1, the Owner shall purchase and maintain, from an insurance company or insurance companies lawfully authorized to issue insurance in the jurisdiction where the Project is located, property insurance written on a builder's risk "all-risks" completed value or equivalent policy form and sufficient to cover the total value of the entire Project on a replacement cost basis. The Owner's property insurance coverage shall be no less than the amount of the initial Contract Sum, plus the value of subsequent Modifications and labor performed and materials or equipment supplied by others. The property insurance shall be maintained until Substantial Completion and thereafter as provided in Section A.2.3.1.3, unless otherwise provided in the Contract Documents or otherwise agreed in writing by the parties to this Agreement. This insurance shall include the interests of the Owner, Contractor, Subcontractors, and Sub-subcontractors in the Project as insureds. This insurance shall include the interests of mortgagees as loss payees.

§ A.2.3.1.1 **Causes of Loss.** The insurance required by this Section A.2.3.1 shall provide coverage for direct physical loss or damage, and shall not exclude the risks of fire, explosion, theft, vandalism, malicious mischief, collapse, earthquake, flood, or windstorm. The insurance shall also provide coverage for ensuing loss or resulting damage from error, omission, or deficiency in construction methods, design, specifications, workmanship, or materials. Sub-limits, if any, are as follows:

ADDITIONS AND DELETIONS:

The author of this document has added information needed for its completion. The author may also have revised the text of the original AIA standard form. An *Additions and Deletions Report* that notes added information as well as revisions to the standard form text is available from the author and should be reviewed.

This document has important legal consequences. Consultation with an attorney is encouraged with respect to its completion or modification.

This document is intended to be used in conjunction with AIA Document A201™–2017, General Conditions of the Contract for Construction. Article 11 of A201™–2017 contains additional insurance provisions.

ELECTRONIC COPYING of any portion of this AIA® Document to another electronic file is prohibited and constitutes a violation of copyright laws as set forth in the footer of this document.

(Indicate below the cause of loss and any applicable sub-limit.)

Causes of Loss

Sub-Limit

§ A.2.3.1.2 Specific Required Coverages. The insurance required by this Section A.2.3.1 shall provide coverage for loss or damage to falsework and other temporary structures, and to building systems from testing and startup. The insurance shall also cover debris removal, including demolition occasioned by enforcement of any applicable legal requirements, and reasonable compensation for the Architect's and Contractor's services and expenses required as a result of such insured loss, including claim preparation expenses. Sub-limits, if any, are as follows:
(Indicate below type of coverage and any applicable sub-limit for specific required coverages.)

Coverage

Sub-Limit

§ A.2.3.1.3 Unless the parties agree otherwise, upon Substantial Completion, the Owner shall continue the insurance required by Section A.2.3.1 or, if necessary, replace the insurance policy required under Section A.2.3.1 with property insurance written for the total value of the Project that shall remain in effect until expiration of the period for correction of the Work set forth in Section 12.2.2 of the General Conditions.

§ A.2.3.1.4 Deductibles and Self-Insured Retentions. If the insurance required by this Section A.2.3 is subject to deductibles or self-insured retentions, the Owner shall be responsible for all loss not covered because of such deductibles or retentions.

§ A.2.3.2 Occupancy or Use Prior to Substantial Completion. The Owner's occupancy or use of any completed or partially completed portion of the Work prior to Substantial Completion shall not commence until the insurance company or companies providing the insurance under Section A.2.3.1 have consented in writing to the continuance of coverage. The Owner and the Contractor shall take no action with respect to partial occupancy or use that would cause cancellation, lapse, or reduction of insurance, unless they agree otherwise in writing.

§ A.2.3.3 Insurance for Existing Structures

If the Work involves remodeling an existing structure or constructing an addition to an existing structure, the Owner shall purchase and maintain, until the expiration of the period for correction of Work as set forth in Section 12.2.2 of the General Conditions, "all-risks" property insurance, on a replacement cost basis, protecting the existing structure against direct physical loss or damage from the causes of loss identified in Section A.2.3.1, notwithstanding the undertaking of the Work. The Owner shall be responsible for all co-insurance penalties.

§ A.2.4 Optional Extended Property Insurance.

The Owner shall purchase and maintain the insurance selected and described below.

(Select the types of insurance the Owner is required to purchase and maintain by placing an X in the box(es) next to the description(s) of selected insurance. For each type of insurance selected, indicate applicable limits of coverage or other conditions in the fill point below the selected item.)

[☐] **§ A.2.4.1 Loss of Use, Business Interruption, and Delay in Completion Insurance,** to reimburse the Owner for loss of use of the Owner's property, or the inability to conduct normal operations due to a covered cause of loss.

<< >>

[☐] **§ A.2.4.2 Ordinance or Law Insurance,** for the reasonable and necessary costs to satisfy the minimum requirements of the enforcement of any law or ordinance regulating the demolition, construction, repair, replacement or use of the Project.

<< >>

[☐] **§ A.2.4.3 Expediting Cost Insurance,** for the reasonable and necessary costs for the temporary repair of

damage to insured property, and to expedite the permanent repair or replacement of the damaged property.

« »

- [« »] **§ A.2.4.4 Extra Expense Insurance**, to provide reimbursement of the reasonable and necessary excess costs incurred during the period of restoration or repair of the damaged property that are over and above the total costs that would normally have been incurred during the same period of time had no loss or damage occurred.

« »

- [« »] **§ A.2.4.5 Civil Authority Insurance**, for losses or costs arising from an order of a civil authority prohibiting access to the Project, provided such order is the direct result of physical damage covered under the required property insurance.

« »

- [« »] **§ A.2.4.6 Ingress/Egress Insurance**, for loss due to the necessary interruption of the insured's business due to physical prevention of ingress to, or egress from, the Project as a direct result of physical damage.

« »

- [« »] **§ A.2.4.7 Soft Costs Insurance**, to reimburse the Owner for costs due to the delay of completion of the Work, arising out of physical loss or damage covered by the required property insurance: including construction loan fees; leasing and marketing expenses; additional fees, including those of architects, engineers, consultants, attorneys and accountants, needed for the completion of the construction, repairs, or reconstruction; and carrying costs such as property taxes, building permits, additional interest on loans, realty taxes, and insurance premiums over and above normal expenses.

« »

§ A.2.5 Other Optional Insurance.

The Owner shall purchase and maintain the insurance selected below.

(Select the types of insurance the Owner is required to purchase and maintain by placing an X in the box(es) next to the description(s) of selected insurance.)

- [« »] **§ A.2.5.1 Cyber Security Insurance** for loss to the Owner due to data security and privacy breach, including costs of investigating a potential or actual breach of confidential or private information.
(Indicate applicable limits of coverage or other conditions in the fill point below.)

« »

- [« »] **§ A.2.5.2 Other Insurance**
(List below any other insurance coverage to be provided by the Owner and any applicable limits.)

Coverage

Limits

ARTICLE A.3 CONTRACTOR'S INSURANCE AND BONDS

§ A.3.1 General

§ A.3.1.1 Certificates of Insurance. The Contractor shall provide certificates of insurance acceptable to the Owner evidencing compliance with the requirements in this Article A.3 at the following times: (1) prior to commencement of the Work; (2) upon renewal or replacement of each required policy of insurance; and (3) upon the Owner's

written request. An additional certificate evidencing continuation of commercial liability coverage, including coverage for completed operations, shall be submitted with the final Application for Payment and thereafter upon renewal or replacement of such coverage until the expiration of the periods required by Section A.3.2.1 and Section A.3.3.1. The certificates will show the Owner as an additional insured on the Contractor's Commercial General Liability and excess or umbrella liability policy or policies.

§ A.3.1.2 Deductibles and Self-Insured Retentions. The Contractor shall disclose to the Owner any deductible or self-insured retentions applicable to any insurance required to be provided by the Contractor.

§ A.3.1.3 Additional Insured Obligations. To the fullest extent permitted by law, the Contractor shall cause the commercial general liability coverage to include (1) the Owner, the Architect, and the Architect's consultants as additional insureds for claims caused in whole or in part by the Contractor's negligent acts or omissions during the Contractor's operations; and (2) the Owner as an additional insured for claims caused in whole or in part by the Contractor's negligent acts or omissions for which loss occurs during completed operations. The additional insured coverage shall be primary and non-contributory to any of the Owner's general liability insurance policies and shall apply to both ongoing and completed operations. To the extent commercially available, the additional insured coverage shall be no less than that provided by Insurance Services Office, Inc. (ISO) forms CG 20 10 07 04, CG 20 37 07 04, and, with respect to the Architect and the Architect's consultants, CG 20 32 07 04.

§ A.3.2 Contractor's Required Insurance Coverage

§ A.3.2.1 The Contractor shall purchase and maintain the following types and limits of insurance from an insurance company or insurance companies lawfully authorized to issue insurance in the jurisdiction where the Project is located. The Contractor shall maintain the required insurance until the expiration of the period for correction of Work as set forth in Section 12.2.2 of the General Conditions, unless a different duration is stated below:

(If the Contractor is required to maintain insurance for a duration other than the expiration of the period for correction of Work, state the duration.)

« »

§ A.3.2.2 Commercial General Liability

§ A.3.2.2.1 Commercial General Liability insurance for the Project written on an occurrence form with policy limits of not less than one millions dollars (\$ 1,000,000) each occurrence, two million dollars (\$ 2,000,000) general aggregate, and two million dollars (\$ 2,000,000) aggregate for products-completed operations hazard, providing coverage for claims including

- .1 damages because of bodily injury, sickness or disease, including occupational sickness or disease, and death of any person;
- .2 personal injury and advertising injury;
- .3 damages because of physical damage to or destruction of tangible property, including the loss of use of such property;
- .4 bodily injury or property damage arising out of completed operations; and
- .5 the Contractor's indemnity obligations under Section 3.18 of the General Conditions.

§ A.3.2.2.2 The Contractor's Commercial General Liability policy under this Section A.3.2.2 shall not contain an exclusion or restriction of coverage for the following:

- .1 Claims by one insured against another insured, if the exclusion or restriction is based solely on the fact that the claimant is an insured, and there would otherwise be coverage for the claim.
- .2 Claims for property damage to the Contractor's Work arising out of the products-completed operations hazard where the damaged Work or the Work out of which the damage arises was performed by a Subcontractor.
- .3 Claims for bodily injury other than to employees of the insured.
- .4 Claims for indemnity under Section 3.18 of the General Conditions arising out of injury to employees of the insured.
- .5 Claims or loss excluded under a prior work endorsement or other similar exclusionary language.
- .6 Claims or loss due to physical damage under a prior injury endorsement or similar exclusionary language.

- .7 Claims related to residential, multi-family, or other habitational projects, if the Work is to be performed on such a project.
- .8 Claims related to roofing, if the Work involves roofing.
- .9 Claims related to exterior insulation finish systems (EIFS), synthetic stucco or similar exterior coatings or surfaces, if the Work involves such coatings or surfaces.
- .10 Claims related to earth subsidence or movement, where the Work involves such hazards.
- .11 Claims related to explosion, collapse and underground hazards, where the Work involves such hazards.

§ A.3.2.3 Automobile Liability covering vehicles owned, and non-owned vehicles used, by the Contractor, with policy limits of not less than one hundred thousand dollars (\$ 100,000) per accident, for bodily injury, death of any person, and property damage arising out of the ownership, maintenance and use of those motor vehicles along with any other statutorily required automobile coverage.

§ A.3.2.4 The Contractor may achieve the required limits and coverage for Commercial General Liability and Automobile Liability through a combination of primary and excess or umbrella liability insurance, provided such primary and excess or umbrella insurance policies result in the same or greater coverage as the coverages required under Section A.3.2.2 and A.3.2.3, and in no event shall any excess or umbrella liability insurance provide narrower coverage than the primary policy. The excess policy shall not require the exhaustion of the underlying limits only through the actual payment by the underlying insurers.

§ A.3.2.5 Workers' Compensation at statutory limits.

§ A.3.2.6 Employers' Liability with policy limits not less than one million dollars (\$ 1,000,000) each accident, one million dollars (\$ 1,000,000) each employee, and one million dollars (\$ 1,000,000) policy limit.

§ A.3.2.7 Jones Act, and the Longshore & Harbor Workers' Compensation Act, as required, if the Work involves hazards arising from work on or near navigable waterways, including vessels and docks

§ A.3.2.8 If the Contractor is required to furnish professional services as part of the Work, the Contractor shall procure Professional Liability insurance covering performance of the professional services, with policy limits of not less than one million dollars (\$ 1,000,000) per claim and one million dollars (\$ 1,000,000) in the aggregate.

§ A.3.2.9 If the Work involves the transport, dissemination, use, or release of pollutants, the Contractor shall procure Pollution Liability insurance, with policy limits of not less than one million dollars (\$ 1,000,000) per claim and one million dollars (\$ 1,000,000) in the aggregate.

§ A.3.2.10 Coverage under Sections A.3.2.8 and A.3.2.9 may be procured through a Combined Professional Liability and Pollution Liability insurance policy, with combined policy limits of not less than one millions dollars (\$ 1,000,000) per claim and one millions dollars (\$ 1,000,000) in the aggregate.

§ A.3.2.11 Insurance for maritime liability risks associated with the operation of a vessel is not required.

§ A.3.2.12 Insurance for the use or operation of manned or unmanned aircraft, if the Work requires such activities, with policy limits of not less than one millions dollars (\$ 1,000,000) per claim and one million dollars (\$ 1,000,000) in the aggregate.

§ A.3.3 Contractor's Other Insurance Coverage

§ A.3.3.1 Insurance selected and described in this Section A.3.3 shall be purchased from an insurance company or insurance companies lawfully authorized to issue insurance in the jurisdiction where the Project is located. The Contractor shall maintain the required insurance through Final Completion and until the expiration of the period for correction of Work as set forth in Section 12.2.2 of the General Conditions.

§ A.3.3.2 The Contractor shall purchase and maintain the following types and limits of insurance in accordance with Section A.3.3.1.

(Select the types of insurance the Contractor is required to purchase and maintain by placing an X in the box(es) next to the description(s) of selected insurance. Where policy limits are provided, include the policy limit in the appropriate fill point.)

- [☒] § **A.3.3.2.1** Property insurance of the same type and scope satisfying the requirements identified in Section A.2.3, which, if selected in this section A.3.3.2.1, relieves the Owner of the responsibility to purchase and maintain such insurance except insurance required by Section A.2.3.1.3 and Section A.2.3.3. The Contractor shall comply with all obligations of the Owner under Section A.2.3 except to the extent provided below. The Contractor shall disclose to the Owner the amount of any deductible, and the Owner shall be responsible for losses within the deductible. Upon request, the Contractor shall provide the Owner with a copy of the property insurance policy or policies required. The Owner shall adjust and settle the loss with the insurer and be the trustee of the proceeds of the property insurance in accordance with Article 11 of the General Conditions unless otherwise set forth below: *(Where the Contractor's obligation to provide property insurance differs from the Owner's obligations as described under Section A.2.3, indicate such differences in the space below. Additionally, if a party other than the Owner will be responsible for adjusting and settling a loss with the insurer and acting as the trustee of the proceeds of property insurance in accordance with Article 11 of the General Conditions, indicate the responsible party below.)*

« »

- [☐] § **A.3.3.2.2 Railroad Protective Liability Insurance**, with policy limits of not less than « » (\$ « ») per claim and « » (\$ « ») in the aggregate, for Work within fifty (50) feet of railroad property.
- [☐] § **A.3.3.2.3 Asbestos Abatement Liability Insurance**, with policy limits of not less than « » (\$ « ») per claim and « » (\$ « ») in the aggregate, for liability arising from the encapsulation, removal, handling, storage, transportation, and disposal of asbestos-containing materials.
- [☐] § **A.3.3.2.4** Insurance for physical damage to property while it is in storage and in transit to the construction site on an "all-risks" completed value form.
- [☐] § **A.3.3.2.5** Property insurance on an "all-risks" completed value form, covering property owned by the Contractor and used on the Project, including scaffolding and other equipment.
- [☐] § **A.3.3.2.6 Other Insurance**
(List below any other insurance coverage to be provided by the Contractor and any applicable limits.)

Coverage

Limits

§ A.3.4 Performance Bond and Payment Bond

The Contractor shall provide surety bonds, from a company or companies lawfully authorized to issue surety bonds in the jurisdiction where the Project is located, as follows:

(Specify type and penal sum of bonds.)

Type

Penal Sum (\$0.00)

Payment Bond

100% of the Contract Sum

Performance Bond

100% of the Contract Sum

Payment and Performance Bonds shall be AIA Document A312™, Payment Bond and Performance Bond, or contain provisions identical to AIA Document A312™, current as of the date of this Agreement and ensure that, among other requirements, Owner is entitled to recovery of legal, design and delay costs resulting from default thereunder.

ARTICLE A.4 SPECIAL TERMS AND CONDITIONS

Special terms and conditions that modify this Insurance and Bonds Exhibit, if any, are as follows:

Not applicable.



**Exhibit B to
AIA A101 - 2017
Standard Form Agreement Between Owner and Contractor
where basis of payment is a Stipulated Sum
For Madison County School District**

This Exhibit B supplements the AIA A101-2017 Standard Form Agreement Between Owner and Contractor, as amended by Owner (the "A101 Agreement"). This Exhibit B shall be completed by Contractor and approved by Owner prior to any work, services, rights or obligations under the A101 Agreement or this Exhibit B commence.

AGREEMENT made as of the ____ day of ____ in the year 20__.

A. Project Description:

(Name, location and detailed description)

B. Contractor Contact Information:

(Name, Legal Status, address, telephone number, and other contact information)

C. Owner's Representative: The Owner identifies the following representative in accordance with Section 8.2:

(List name, address, telephone number, e-mail address, and other contact information.)

D. Contractor's Representative: The Contractor identifies the following representative in accordance with Section 8.3: (List name, address, telephone number, e-mail address, and other contact information.)

E. Architect Contact Information:

(Name, Legal Status, address, telephone number, and other contact information)

F. Date of Commencement and Substantial Completion.

1. The date of commencement of the Work shall be as referenced in Section 3.1 shall be:
(Check one of the following boxes.)

[☐] The date of this Agreement.

[☐] A date set forth in a notice to proceed issued by the Owner.

[☐] Established as follows:
(Insert a date or a means to determine the date of commencement of the Work.)

« »

2. Subject to Section 3.3, the Contractor shall achieve Substantial Completion of the entire Work:
(Check one of the following boxes and complete the necessary information.)

[☐] Not later than « » (« ») calendar days from the date of commencement of the Work.

[☐] By the following date: « »

3. Subject to §3.3.2, if portions of the Work are to be completed prior to Substantial Completion of the entire Work, the Contractor shall achieve Substantial Completion of such portions by the following dates:

Portion of Work

Substantial Completion Date

- G. Contract Sum:** The Contract Sum as defined Section 4.1 is « » (\$ « »). The Contract Sum is detailed on the Initial Schedule of Values attached as Exhibit C. The Contract Sum contains an Owner's Contingency as defined in Section 4.1.1 in the amount of _____ Dollars (\$ _____ .00).

- H. Alternates:** The following alternates, if any, apply to and are included in Section 4.2.

1. Alternates, if any, included in the Contract Sum:

Item

Price

2. Subject to the conditions noted below, the following alternates may be accepted by the Owner following execution of this Agreement. Upon acceptance, the Owner shall issue a Modification to this Agreement. (Insert below each alternate and the conditions that must be met for the Owner to accept the alternate.)

Item

Price

Conditions for Acceptance

3. Allowances, if any, included in the Contract Sum: (Identify each allowance.)

Item

Price

4. Unit prices, if any: (Identify the item and state the unit price and quantity limitations, if any, to which the unit price will be applicable.)

Item	Units and Limitations	Price per Unit (\$0.00)

5. Liquidated damages, if any:
(Insert terms and conditions for liquidated damages, if any.)

« »

6. Other: (Insert other provisions, if any, that might result in a change to the Contract Sum.)

« »

I. Retainage:

1. The Retainage amount defined in Section 5.1.7.1 is 5.0% to be withheld from each Application for Payment.
2. The following items are not subject to Retainage:
(Insert any items not subject to the withholding of retainage, such as general conditions, insurance, etc.)

« »

J. Insurance and Bonds (see Exhibit A):

If Owner and Contractor do not agree to give notice in electronic format, pursuant to Article 1 of AIA Document A201–2017, AIA Document E203™–2013, Building Information Modeling and Digital Data Exhibit, then Owner and Contractor agree to as follows:

(If other than in accordance with AIA Document E203–2013, insert requirements for delivering notice in electronic format such as name, title, and email address of the recipient and whether and how the system will be required to generate a read receipt for the transmission.)

« »

K. Enumeration of Contract Documents: The Agreement is comprised of the following documents as described in Section 9.1.

- .1 AIA Document A101™–2017, Standard Form of Agreement Between Owner and Contractor
- .2 AIA Document A101™–2017, Exhibit A, Insurance and Bonds
- .3 Exhibit B, Project Details and Other Information
- .4 AIA Document A201™–2017, General Conditions of the Contract for Construction
- .5 AIA Document E203™–2013, Building Information Modeling and Digital Data Exhibit, dated as indicated below:

(Insert the date of the E203-2013 incorporated into this Agreement.)

« »

- .6 Drawings

Number	Title	Date

- .7 Specifications

DRAFT AIA® Document A201® – 2017

General Conditions of the Contract for Construction

THE OWNER:

(Name, legal status and address)

«Madison County Schools
476 Highland Colony Parkway
Ridgeland, Mississippi 39157
(601) 499-0800»

TABLE OF ARTICLES

- 1 GENERAL PROVISIONS
- 2 OWNER
- 3 CONTRACTOR
- 4 ARCHITECT
- 5 SUBCONTRACTORS
- 6 CONSTRUCTION BY OWNER OR BY SEPARATE CONTRACTORS
- 7 CHANGES IN THE WORK
- 8 TIME
- 9 PAYMENTS AND COMPLETION
- 10 PROTECTION OF PERSONS AND PROPERTY
- 11 INSURANCE AND BONDS
- 12 UNCOVERING AND CORRECTION OF WORK
- 13 MISCELLANEOUS PROVISIONS
- 14 TERMINATION OR SUSPENSION OF THE CONTRACT
- 15 CLAIMS AND DISPUTES

ADDITIONS AND DELETIONS:

The author of this document has added information needed for its completion. The author may also have revised the text of the original AIA standard form. An *Additions and Deletions Report* that notes added information as well as revisions to the standard form text is available from the author and should be reviewed.

This document has important legal consequences. Consultation with an attorney is encouraged with respect to its completion or modification.

For guidance in modifying this document to include supplementary conditions, see AIA Document A503™, *Guide for Supplementary Conditions*.

ELECTRONIC COPYING of any portion of this AIA® Document to another electronic file is prohibited and constitutes a violation of copyright laws as set forth in the footer of this document.

INDEX

(Topics and numbers in bold are Section headings.)

Acceptance of Nonconforming Work

9.6.6, 9.9.3, **12.3**

Acceptance of Work

9.6.6, 9.8.2, 9.9.3, 9.10.1, 9.10.3, 12.3

Access to Work

3.16, 6.2.1, 12.1

Accident Prevention

10

Acts and Omissions

3.2, 3.3.2, 3.12.8, 3.18, 4.2.3, 8.3.1, 9.5.1, 10.2.5,
10.2.8, 13.3.2, 14.1, 15.1.2, 15.2

Addenda

1.1.1

Additional Costs, Claims for

3.7.4, 3.7.5, 10.3.2, 15.1.5

Additional Inspections and Testing

9.4.2, 9.8.3, 12.2.1, **13.4**

Additional Time, Claims for

3.2.4, 3.7.4, 3.7.5, 3.10.2, 8.3.2, **15.1.6**

Administration of the Contract

3.1.3, **4.2**, 9.4, 9.5

Advertisement or Invitation to Bid

1.1.1

Aesthetic Effect

4.2.13

Allowances

3.8

Applications for Payment

4.2.5, 7.3.9, 9.2, **9.3**, 9.4, 9.5.1, 9.5.4, 9.6.3, 9.7, 9.10

Approvals

2.1.1, 2.3.1, 2.5, 3.1.3, 3.10.2, 3.12.8, 3.12.9,

3.12.10.1, 4.2.7, 9.3.2, 13.4.1

Arbitration

8.3.1, 15.3.2, **15.4**

ARCHITECT

4

Architect, Definition of

4.1.1

Architect, Extent of Authority

2.5, 3.12.7, 4.1.2, 4.2, 5.2, 6.3, 7.1.2, 7.3.4, 7.4, 9.2,
9.3.1, 9.4, 9.5, 9.6.3, 9.8, 9.10.1, 9.10.3, 12.1, 12.2.1,
13.4.1, 13.4.2, 14.2.2, 14.2.4, 15.1.4, 15.2.1

Architect, Limitations of Authority and

Responsibility

2.1.1, 3.12.4, 3.12.8, 3.12.10, 4.1.2, 4.2.1, 4.2.2,
4.2.3, 4.2.6, 4.2.7, 4.2.10, 4.2.12, 4.2.13, 5.2.1, 7.4,
9.4.2, 9.5.4, 9.6.4, 15.1.4, 15.2

Architect's Additional Services and Expenses

2.5, 12.2.1, 13.4.2, 13.4.3, 14.2.4

Architect's Administration of the Contract

3.1.3, 3.7.4, 15.2, 9.4.1, 9.5

Architect's Approvals

2.5, 3.1.3, 3.5, 3.10.2, 4.2.7

Architect's Authority to Reject Work

3.5, 4.2.6, 12.1.2, 12.2.1

Architect's Copyright

1.1.7, 1.5

Architect's Decisions

3.7.4, 4.2.6, 4.2.7, 4.2.11, 4.2.12, 4.2.13, 4.2.14, 6.3,
7.3.4, 7.3.9, 8.1.3, 8.3.1, 9.2, 9.4.1, 9.5, 9.8.4, 9.9.1,
13.4.2, 15.2

Architect's Inspections

3.7.4, 4.2.2, 4.2.9, 9.4.2, 9.8.3, 9.9.2, 9.10.1, 13.4

Architect's Instructions

3.2.4, 3.3.1, 4.2.6, 4.2.7, 13.4.2

Architect's Interpretations

4.2.11, 4.2.12

Architect's Project Representative

4.2.10

Architect's Relationship with Contractor

1.1.2, 1.5, 2.3.3, 3.1.3, 3.2.2, 3.2.3, 3.2.4, 3.3.1, 3.4.2,
3.5, 3.7.4, 3.7.5, 3.9.2, 3.9.3, 3.10, 3.11, 3.12, 3.16,
3.18, 4.1.2, 4.2, 5.2, 6.2.2, 7, 8.3.1, 9.2, 9.3, 9.4, 9.5,
9.7, 9.8, 9.9, 10.2.6, 10.3, 11.3, 12, 13.3.2, 13.4, 15.2

Architect's Relationship with Subcontractors

1.1.2, 4.2.3, 4.2.4, 4.2.6, 9.6.3, 9.6.4, 11.3

Architect's Representations

9.4.2, 9.5.1, 9.10.1

Architect's Site Visits

3.7.4, 4.2.2, 4.2.9, 9.4.2, 9.5.1, 9.9.2, 9.10.1, 13.4

Asbestos

10.3.1

Attorneys' Fees

3.18.1, 9.6.8, 9.10.2, 10.3.3

Award of Separate Contracts

6.1.1, 6.1.2

Award of Subcontracts and Other Contracts for Portions of the Work

5.2

Basic Definitions

1.1

Bidding Requirements

1.1.1

Binding Dispute Resolution

8.3.1, 9.7, 11.5, 13.1, 15.1.2, 15.1.3, 15.2.1, 15.2.5,
15.2.6.1, 15.3.1, 15.3.2, 15.3.3, 15.4.1

Bonds, Lien

7.3.4.4, 9.6.8, 9.10.2, 9.10.3

Bonds, Performance, and Payment

7.3.4.4, 9.6.7, 9.10.3, **11.1.2**, 11.1.3, **11.5**

Building Information Models Use and Reliance

1.8

Building Permit

3.7.1

Capitalization

1.3

Certificate of Substantial Completion

9.8.3, 9.8.4, 9.8.5

Certificates for Payment

4.2.1, 4.2.5, 4.2.9, 9.3.3, **9.4**, **9.5**, **9.6.1**, 9.6.6, 9.7,
9.10.1, 9.10.3, 14.1.1.3, 14.2.4, 15.1.4

Certificates of Inspection, Testing or Approval

13.4.4
Certificates of Insurance
9.10.2
Change Orders
1.1.1, 3.4.2, 3.7.4, 3.8.2.3, 3.11, 3.12.8, 4.2.8, 5.2.3,
7.1.2, 7.1.3, **7.2**, 7.3.2, 7.3.7, 7.3.9, 7.3.10, 8.3.1,
9.3.1.1, 9.10.3, 10.3.2, 11.2, 11.5, 12.1.2
Change Orders, Definition of
7.2.1
CHANGES IN THE WORK
2.2.2, 3.11, 4.2.8, **7**, 7.2.1, 7.3.1, 7.4, 8.3.1, 9.3.1.1,
11.5
Claims, Definition of
15.1.1
Claims, Notice of
1.6.2, 15.1.3
CLAIMS AND DISPUTES
3.2.4, 6.1.1, 6.3, 7.3.9, 9.3.3, 9.10.4, 10.3.3, **15**, 15.4
Claims and Timely Assertion of Claims
15.4.1
Claims for Additional Cost
3.2.4, 3.3.1, 3.7.4, 7.3.9, 9.5.2, 10.2.5, 10.3.2, **15.1.5**
Claims for Additional Time
3.2.4, 3.3.1, 3.7.4, 6.1.1, 8.3.2, 9.5.2, 10.3.2, **15.1.6**
Concealed or Unknown Conditions, Claims for
3.7.4
Claims for Damages
3.2.4, 3.18, 8.3.3, 9.5.1, 9.6.7, 10.2.5, 10.3.3, 11.3,
11.3.2, 14.2.4, 15.1.7
Claims Subject to Arbitration
15.4.1
Cleaning Up
3.15, 6.3
Commencement of the Work, Conditions Relating to
2.2.1, 3.2.2, 3.4.1, 3.7.1, 3.10.1, 3.12.6, 5.2.1, 5.2.3,
6.2.2, 8.1.2, 8.2.2, 8.3.1, 11.1, 11.2, **15.1.5**
Commencement of the Work, Definition of
8.1.2
Communications
3.9.1, **4.2.4**
Completion, Conditions Relating to
3.4.1, 3.11, 3.15, 4.2.2, 4.2.9, 8.2, 9.4.2, 9.8, 9.9.1,
9.10, 12.2, 14.1.2, 15.1.2
COMPLETION, PAYMENTS AND
9
Completion, Substantial
3.10.1, 4.2.9, 8.1.1, 8.1.3, 8.2.3, 9.4.2, 9.8, 9.9.1,
9.10.3, 12.2, 15.1.2
Compliance with Laws
2.3.2, 3.2.3, 3.6, 3.7, 3.12.10, 3.13, 9.6.4, 10.2.2,
13.1, 13.3, 13.4.1, 13.4.2, 13.5, 14.1.1, 14.2.1.3,
15.2.8, 15.4.2, 15.4.3
Concealed or Unknown Conditions
3.7.4, 4.2.8, 8.3.1, 10.3
Conditions of the Contract
1.1.1, 6.1.1, 6.1.4
Consent, Written

3.4.2, 3.14.2, 4.1.2, 9.8.5, 9.9.1, 9.10.2, 9.10.3, 13.2,
15.4.4.2
Consolidation or Joinder
15.4.4
CONSTRUCTION BY OWNER OR BY
SEPARATE CONTRACTORS
1.1.4, **6**
Construction Change Directive, Definition of
7.3.1
Construction Change Directives
1.1.1, 3.4.2, 3.11, 3.12.8, 4.2.8, 7.1.1, 7.1.2, 7.1.3,
7.3, 9.3.1.1
Construction Schedules, Contractor's
3.10, 3.11, 3.12.1, 3.12.2, 6.1.3, 15.1.6.2
Contingent Assignment of Subcontracts
5.4, 14.2.2.2
Continuing Contract Performance
15.1.4
Contract, Definition of
1.1.2
CONTRACT, TERMINATION OR
SUSPENSION OF THE
5.4.1.1, 5.4.2, 11.5, **14**
Contract Administration
3.1.3, 4, 9.4, 9.5
Contract Award and Execution, Conditions Relating
to
3.7.1, 3.10, 5.2, 6.1
Contract Documents, Copies Furnished and Use of
1.5.2, 2.3.6, 5.3
Contract Documents, Definition of
1.1.1
Contract Sum
2.2.2, 2.2.4, 3.7.4, 3.7.5, 3.8, 3.10.2, 5.2.3, 7.3, 7.4,
9.1, 9.2, 9.4.2, 9.5.1.4, 9.6.7, 9.7, 10.3.2, 11.5, 12.1.2,
12.3, 14.2.4, 14.3.2, 15.1.4.2, **15.1.5**, **15.2.5**
Contract Sum, Definition of
9.1
Contract Time
1.1.4, 2.2.1, 2.2.2, 3.7.4, 3.7.5, 3.10.2, 5.2.3, 6.1.5,
7.2.1.3, 7.3.1, 7.3.5, 7.3.6, 7, 7, 7.3.10, 7.4, 8.1.1,
8.2.1, 8.2.3, 8.3.1, 9.5.1, 9.7, 10.3.2, 12.1.1, 12.1.2,
14.3.2, 15.1.4.2, 15.1.6.1, 15.2.5
Contract Time, Definition of
8.1.1
CONTRACTOR
3
Contractor, Definition of
3.1, **6.1.2**
Contractor's Construction and Submittal
Schedules
3.10, 3.12.1, 3.12.2, 4.2.3, 6.1.3, 15.1.6.2
Contractor's Employees
2.2.4, 3.3.2, 3.4.3, 3.8.1, 3.9, 3.18.2, 4.2.3, 4.2.6,
10.2, 10.3, 11.3, 14.1, 14.2.1.1
Contractor's Liability Insurance
11.1

Contractor's Relationship with Separate Contractors and Owner's Forces
3.12.5, 3.14.2, 4.2.4, 6, 11.3, 12.2.4

Contractor's Relationship with Subcontractors
1.2.2, 2.2.4, 3.3.2, 3.18.1, 3.18.2, 4.2.4, 5, 9.6.2, 9.6.7, 9.10.2, 11.2, 11.3, 11.4

Contractor's Relationship with the Architect
1.1.2, 1.5, 2.3.3, 3.1.3, 3.2.2, 3.2.3, 3.2.4, 3.3.1, 3.4.2, 3.5.1, 3.7.4, 3.10, 3.11, 3.12, 3.16, 3.18, 4.2, 5.2, 6.2.2, 7, 8.3.1, 9.2, 9.3, 9.4, 9.5, 9.7, 9.8, 9.9, 10.2.6, 10.3, 11.3, 12, 13.4, 15.1.3, 15.2.1

Contractor's Representations
3.2.1, 3.2.2, 3.5, 3.12.6, 6.2.2, 8.2.1, 9.3.3, 9.8.2

Contractor's Responsibility for Those Performing the Work
3.3.2, 3.18, 5.3, 6.1.3, 6.2, 9.5.1, 10.2.8

Contractor's Review of Contract Documents
3.2

Contractor's Right to Stop the Work
2.2.2, 9.7

Contractor's Right to Terminate the Contract
14.1

Contractor's Submittals
3.10, 3.11, 3.12, 4.2.7, 5.2.1, 5.2.3, 9.2, 9.3, 9.8.2, 9.8.3, 9.9.1, 9.10.2, 9.10.3

Contractor's Superintendent
3.9, 10.2.6

Contractor's Supervision and Construction Procedures
1.2.2, 3.3, 3.4, 3.12.10, 4.2.2, 4.2.7, 6.1.3, 6.2.4, 7.1.3, 7.3.4, 7.3.6, 8.2, 10, 12, 14, 15.1.4

Coordination and Correlation
1.2, 3.2.1, 3.3.1, 3.10, 3.12.6, 6.1.3, 6.2.1

Copies Furnished of Drawings and Specifications
1.5, 2.3.6, 3.11

Copyrights
1.5, **3.17**

Correction of Work
2.5, 3.7.3, 9.4.2, 9.8.2, 9.8.3, 9.9.1, 12.1.2, **12.2**, 12.3, 15.1.3.1, 15.1.3.2, 15.2.1

Correlation and Intent of the Contract Documents
1.2

Cost, Definition of
7.3.4

Costs
2.5, 3.2.4, 3.7.3, 3.8.2, 3.15.2, 5.4.2, 6.1.1, 6.2.3, 7.3.3.3, 7.3.4, 7.3.8, 7.3.9, 9.10.2, 10.3.2, 10.3.6, 11.2, 12.1.2, 12.2.1, 12.2.4, 13.4, 14

Cutting and Patching
3.14, 6.2.5

Damage to Construction of Owner or Separate Contractors
3.14.2, 6.2.4, 10.2.1.2, 10.2.5, 10.4, 12.2.4

Damage to the Work
3.14.2, 9.9.1, 10.2.1.2, 10.2.5, 10.4, 12.2.4

Damages, Claims for
3.2.4, 3.18, 6.1.1, 8.3.3, 9.5.1, 9.6.7, 10.3.3, 11.3.2, 11.3, 14.2.4, 15.1.7

Damages for Delay
6.2.3, 8.3.3, 9.5.1.6, 9.7, 10.3.2, 14.3.2

Date of Commencement of the Work, Definition of
8.1.2

Date of Substantial Completion, Definition of
8.1.3

Day, Definition of
8.1.4

Decisions of the Architect
3.7.4, 4.2.6, 4.2.7, 4.2.11, 4.2.12, 4.2.13, 6.3, 7.3.4, 7.3.9, 8.1.3, 8.3.1, 9.2, 9.4, 9.5.1, 9.8.4, 9.9.1, 13.4.2, 14.2.2, 14.2.4, 15.1, 15.2

Decisions to Withhold Certification
9.4.1, **9.5**, 9.7, 14.1.1.3

Defective or Nonconforming Work, Acceptance, Rejection and Correction of
2.5, 3.5, 4.2.6, 6.2.3, 9.5.1, 9.5.3, 9.6.6, 9.8.2, 9.9.3, 9.10.4, 12.2.1

Definitions
1.1, 2.1.1, 3.1.1, 3.5, 3.12.1, 3.12.2, 3.12.3, 4.1.1, 5.1, 6.1.2, 7.2.1, 7.3.1, 8.1, 9.1, 9.8.1, 15.1.1

Delays and Extensions of Time
3.2, **3.7.4**, 5.2.3, 7.2.1, 7.3.1, **7.4**, **8.3**, **9.5.1**, **9.7**, 10.3.2, **10.4**, 14.3.2, **15.1.6**, 15.2.5

Digital Data Use and Transmission
1.7

Disputes
6.3, 7.3.9, 15.1, 15.2

Documents and Samples at the Site
3.11

Drawings, Definition of
1.1.5

Drawings and Specifications, Use and Ownership of
3.11

Effective Date of Insurance
8.2.2

Emergencies
10.4, 14.1.1.2, **15.1.5**

Employees, Contractor's
3.3.2, 3.4.3, 3.8.1, 3.9, 3.18.2, 4.2.3, 4.2.6, 10.2, 10.3.3, 11.3, 14.1, 14.2.1.1

Equipment, Labor, or Materials
1.1.3, 1.1.6, 3.4, 3.5, 3.8.2, 3.8.3, 3.12, 3.13, 3.15.1, 4.2.6, 4.2.7, 5.2.1, 6.2.1, 7.3.4, 9.3.2, 9.3.3, 9.5.1.3, 9.10.2, 10.2.1, 10.2.4, 14.2.1.1, 14.2.1.2

Execution and Progress of the Work
1.1.3, 1.2.1, 1.2.2, 2.3.4, 2.3.6, 3.1, 3.3.1, 3.4.1, 3.7.1, 3.10.1, 3.12, 3.14, 4.2, 6.2.2, 7.1.3, 7.3.6, 8.2, 9.5.1, 9.9.1, 10.2, 10.3, 12.1, 12.2, 14.2, 14.3.1, 15.1.4

Extensions of Time
3.2.4, 3.7.4, 5.2.3, 7.2.1, 7.3, 7.4, 9.5.1, 9.7, 10.3.2, 10.4, 14.3, 15.1.6, **15.2.5**

Failure of Payment
9.5.1.3, **9.7**, 9.10.2, 13.5, 14.1.1.3, 14.2.1.2

Faulty Work
(See Defective or Nonconforming Work)

Final Completion and Final Payment
4.2.1, 4.2.9, 9.8.2, **9.10**, 12.3, 14.2.4, 14.4.3

Financial Arrangements, Owner's
2.2.1, 13.2.2, 14.1.1.4

GENERAL PROVISIONS

1

Governing Law

13.1

Guarantees (See Warranty)

Hazardous Materials and Substances

10.2.4, **10.3**

Identification of Subcontractors and Suppliers
5.2.1

Indemnification

3.1.7, **3.18**, 9.6.8, 9.10.2, 10.3.3, 11.3

Information and Services Required of the Owner

2.1.2, **2.2**, 2.3, 3.2.2, 3.12.10.1, 6.1.3, 6.1.4, 6.2.5,
9.6.1, 9.9.2, 9.10.3, 10.3.3, 11.2, 13.4.1, 13.4.2,
14.1.1.4, 14.1.4, 15.1.4

Initial Decision

15.2

Initial Decision Maker, Definition of

1.1.8

Initial Decision Maker, Decisions

14.2.4, 15.1.4.2, 15.2.1, 15.2.2, 15.2.3, 15.2.4, 15.2.5

Initial Decision Maker, Extent of Authority

14.2.4, 15.1.4.2, 15.2.1, 15.2.2, 15.2.3, 15.2.4, 15.2.5

Injury or Damage to Person or Property

10.2.8, 10.4

Inspections

3.1.3, 3.3.3, 3.7.1, 4.2.2, 4.2.6, 4.2.9, 9.4.2, 9.8.3,
9.9.2, 9.10.1, 12.2.1, 13.4

Instructions to Bidders

1.1.1

Instructions to the Contractor

3.2.4, 3.3.1, 3.8.1, 5.2.1, 7, 8.2.2, 12, 13.4.2

Instruments of Service, Definition of

1.1.7

Insurance

6.1.1, 7.3.4, 8.2.2, 9.3.2, 9.8.4, 9.9.1, 9.10.2, 10.2.5,

11

Insurance, Notice of Cancellation or Expiration

11.1.4, 11.2.3

Insurance, Contractor's Liability

11.1

Insurance, Effective Date of

8.2.2, 14.4.2

Insurance, Owner's Liability

11.2

Insurance, Property

10.2.5, 11.2, 11.4, 11.5

Insurance, Stored Materials

9.3.2

INSURANCE AND BONDS

11

Insurance Companies, Consent to Partial Occupancy

9.9.1

Insured loss, Adjustment and Settlement of

11.5

Intent of the Contract Documents

1.2.1, 4.2.7, 4.2.12, 4.2.13

Interest

13.5

Interpretation

1.1.8, 1.2.3, **1.4**, 4.1.1, 5.1, 6.1.2, 15.1.1

Interpretations, Written

4.2.11, 4.2.12

Judgment on Final Award

15.4.2

Labor and Materials, Equipment

1.1.3, 1.1.6, **3.4**, 3.5, 3.8.2, 3.8.3, 3.12, 3.13, 3.15.1,
5.2.1, 6.2.1, 7.3.4, 9.3.2, 9.3.3, 9.5.1.3, 9.10.2, 10.2.1,
10.2.4, 14.2.1.1, 14.2.1.2

Labor Disputes

8.3.1

Laws and Regulations

1.5, 2.3.2, 3.2.3, 3.2.4, 3.6, 3.7, 3.12.10, 3.13, 9.6.4,
9.9.1, 10.2.2, 13.1, 13.3.1, 13.4.2, 13.5, 14, 15.2.8,
15.4

Liens

2.1.2, 9.3.1, 9.3.3, 9.6.8, 9.10.2, 9.10.4, 15.2.8

Limitations, Statutes of

12.2.5, 15.1.2, 15.4.1.1

Limitations of Liability

3.2.2, 3.5, 3.12.10, 3.12.10.1, 3.17, 3.18.1, 4.2.6,
4.2.7, 6.2.2, 9.4.2, 9.6.4, 9.6.7, 9.6.8, 10.2.5, 10.3.3,
11.3, 12.2.5, 13.3.1

Limitations of Time

2.1.2, 2.2, 2.5, 3.2.2, 3.10, 3.11, 3.12.5, 3.15.1, 4.2.7,
5.2, 5.3, 5.4.1, 6.2.4, 7.3, 7.4, 8.2, 9.2, 9.3.1, 9.3.3,
9.4.1, 9.5, 9.6, 9.7, 9.8, 9.9, 9.10, 12.2, 13.4, 14, 15,
15.1.2, 15.1.3, 15.1.5

Materials, Hazardous

10.2.4, **10.3**

Materials, Labor, Equipment and

1.1.3, 1.1.6, 3.4.1, 3.5, 3.8.2, 3.8.3, 3.12, 3.13, 3.15.1,
5.2.1, 6.2.1, 7.3.4, 9.3.2, 9.3.3, 9.5.1.3, 9.10.2,
10.2.1.2, 10.2.4, 14.2.1.1, 14.2.1.2

Means, Methods, Techniques, Sequences and
Procedures of Construction

3.3.1, 3.12.10, 4.2.2, 4.2.7, 9.4.2

Mechanic's Lien

2.1.2, 9.3.1, 9.3.3, 9.6.8, 9.10.2, 9.10.4, 15.2.8

Mediation

8.3.1, 15.1.3.2, 15.2.1, 15.2.5, 15.2.6, **15.3**, 15.4.1,
15.4.1.1

Minor Changes in the Work

1.1.1, 3.4.2, 3.12.8, 4.2.8, 7.1, **7.4**

MISCELLANEOUS PROVISIONS

13

Modifications, Definition of

1.1.1

Modifications to the Contract

1.1.1, 1.1.2, 2.5, 3.11, 4.1.2, 4.2.1, 5.2.3, 7, 8.3.1, 9.7,
10.3.2

Mutual Responsibility

6.2

Nonconforming Work, Acceptance of

9.6.6, 9.9.3, **12.3**

Nonconforming Work, Rejection and Correction of
2.4, 2.5, 3.5, 4.2.6, 6.2.4, 9.5.1, 9.8.2, 9.9.3, 9.10.4,
12.2

Notice

1.6, 1.6.1, 1.6.2, 2.1.2, 2.2.2., 2.2.3, 2.2.4, 2.5, 3.2.4,
3.3.1, 3.7.4, 3.7.5, 3.9.2, 3.12.9, 3.12.10, 5.2.1, 7.4,
8.2.2 9.6.8, 9.7, 9.10.1, 10.2.8, 10.3.2, 11.5, 12.2.2.1,
13.4.1, 13.4.2, 14.1, 14.2.2, 14.4.2, 15.1.3, 15.1.5,
15.1.6, 15.4.1

Notice of Cancellation or Expiration of Insurance
11.1.4, 11.2.3

Notice of Claims

1.6.2, 2.1.2, 3.7.4, 9.6.8, 10.2.8, **15.1.3**, 15.1.5,
15.1.6, 15.2.8, 15.3.2, 15.4.1

Notice of Testing and Inspections
13.4.1, 13.4.2

Observations, Contractor's

3.2, 3.7.4

Occupancy

2.3.1, 9.6.6, 9.8

Orders, Written

1.1.1, 2.4, 3.9.2, 7, 8.2.2, 11.5, 12.1, 12.2.2.1, 13.4.2,
14.3.1

OWNER

2

Owner, Definition of

2.1.1

Owner, Evidence of Financial Arrangements

2.2, 13.2.2, 14.1.1.4

Owner, Information and Services Required of the

2.1.2, **2.2**, 2.3, 3.2.2, 3.12.10, 6.1.3, 6.1.4, 6.2.5,
9.3.2, 9.6.1, 9.6.4, 9.9.2, 9.10.3, 10.3.3, 11.2, 13.4.1,
13.4.2, 14.1.1.4, 14.1.4, 15.1.4

Owner's Authority

1.5, 2.1.1, 2.3.32.4, 2.5, 3.4.2, 3.8.1, 3.12.10, 3.14.2,
4.1.2, 4.2.4, 4.2.9, 5.2.1, 5.2.4, 5.4.1, 6.1, 6.3, 7.2.1,
7.3.1, 8.2.2, 8.3.1, 9.3.2, 9.5.1, 9.6.4, 9.9.1, 9.10.2,
10.3.2, 11.4, 11.5, 12.2.2, 12.3, 13.2.2, 14.3, 14.4,
15.2.7

Owner's Insurance

11.2

Owner's Relationship with Subcontractors

1.1.2, 5.2, 5.3, 5.4, 9.6.4, 9.10.2, 14.2.2

Owner's Right to Carry Out the Work

2.5, 14.2.2

Owner's Right to Clean Up

6.3

**Owner's Right to Perform Construction and to
Award Separate Contracts**

6.1

Owner's Right to Stop the Work

2.4

Owner's Right to Suspend the Work

14.3

Owner's Right to Terminate the Contract

14.2, 14.4

Ownership and Use of Drawings, Specifications

and Other Instruments of Service

1.1.1, 1.1.6, 1.1.7, **1.5**, 2.3.6, 3.2.2, 3.11, 3.17, 4.2.12,
5.3

Partial Occupancy or Use

9.6.6, **9.9**

Patching, Cutting and

3.14, 6.2.5

Patents

3.17

Payment, Applications for

4.2.5, 7.3.9, 9.2, **9.3**, 9.4, 9.5, 9.6.3, 9.7, 9.8.5, 9.10.1,
14.2.3, 14.2.4, 14.4.3

Payment, Certificates for

4.2.5, 4.2.9, 9.3.3, **9.4**, 9.5, 9.6.1, 9.6.6, 9.7, 9.10.1,
9.10.3, 14.1.1.3, 14.2.4

Payment, Failure of

9.5.1.3, **9.7**, 9.10.2, 13.5, 14.1.1.3, 14.2.1.2

Payment, Final

4.2.1, 4.2.9, **9.10**, 12.3, 14.2.4, 14.4.3

Payment Bond, Performance Bond and

7.3.4.4, 9.6.7, 9.10.3, **11.1.2**

Payments, Progress

9.3, **9.6**, 9.8.5, 9.10.3, 14.2.3, 15.1.4

PAYMENTS AND COMPLETION

9

Payments to Subcontractors

5.4.2, 9.5.1.3, 9.6.2, 9.6.3, 9.6.4, 9.6.7, 14.2.1.2

PCB

10.3.1

Performance Bond and Payment Bond

7.3.4.4, 9.6.7, 9.10.3, **11.1.2**

Permits, Fees, Notices and Compliance with Laws

2.3.1, **3.7**, 3.13, 7.3.4.4, 10.2.2

PERSONS AND PROPERTY, PROTECTION

OF

10

Polychlorinated Biphenyl

10.3.1

Product Data, Definition of

3.12.2

Product Data and Samples, Shop Drawings

3.11, **3.12**, 4.2.7

Progress and Completion

4.2.2, **8.2**, 9.8, 9.9.1, 14.1.4, 15.1.4

Progress Payments

9.3, **9.6**, 9.8.5, 9.10.3, 14.2.3, 15.1.4

Project, Definition of

1.1.4

Project Representatives

4.2.10

Property Insurance

10.2.5, **11.2**

Proposal Requirements

1.1.1

PROTECTION OF PERSONS AND PROPERTY

10

Regulations and Laws

1.5, 2.3.2, 3.2.3, 3.6, 3.7, 3.12.10, 3.13, 9.6.4, 9.9.1, 10.2.2, 13.1, 13.3, 13.4.1, 13.4.2, 13.5, 14, 15.2.8, 15.4
Rejection of Work
4.2.6, 12.2.1
Releases and Waivers of Liens
9.3.1, 9.10.2
Representations
3.2.1, 3.5, 3.12.6, 8.2.1, 9.3.3, 9.4.2, 9.5.1, 9.10.1
Representatives
2.1.1, 3.1.1, 3.9, 4.1.1, 4.2.10, 13.2.1
Responsibility for Those Performing the Work
3.3.2, 3.18, 4.2.2, 4.2.3, 5.3, 6.1.3, 6.2, 6.3, 9.5.1, 10
Retainage
9.3.1, 9.6.2, 9.8.5, 9.9.1, 9.10.2, 9.10.3
Review of Contract Documents and Field Conditions by Contractor
3.2, 3.12.7, 6.1.3
Review of Contractor's Submittals by Owner and Architect
3.10.1, 3.10.2, 3.11, 3.12, 4.2, 5.2, 6.1.3, 9.2, 9.8.2
Review of Shop Drawings, Product Data and Samples by Contractor
3.12
Rights and Remedies
1.1.2, 2.4, 2.5, 3.5, 3.7.4, 3.15.2, 4.2.6, 5.3, 5.4, 6.1, 6.3, 7.3.1, 8.3, 9.5.1, 9.7, 10.2.5, 10.3, 12.2.1, 12.2.2, 12.2.4, **13.3**, 14, 15.4
Royalties, Patents and Copyrights
3.17
Rules and Notices for Arbitration
15.4.1
Safety of Persons and Property
10.2, 10.4
Safety Precautions and Programs
3.3.1, 4.2.2, 4.2.7, 5.3, **10.1**, 10.2, 10.4
Samples, Definition of
3.12.3
Samples, Shop Drawings, Product Data and
3.11, **3.12**, 4.2.7
Samples at the Site, Documents and
3.11
Schedule of Values
9.2, 9.3.1
Schedules, Construction
3.10, 3.12.1, 3.12.2, 6.1.3, 15.1.6.2
Separate Contracts and Contractors
1.1.4, 3.12.5, 3.14.2, 4.2.4, 4.2.7, 6, 8.3.1, 12.1.2
Separate Contractors, Definition of
6.1.1
Shop Drawings, Definition of
3.12.1
Shop Drawings, Product Data and Samples
3.11, **3.12**, 4.2.7
Site, Use of
3.13, 6.1.1, 6.2.1
Site Inspections
3.2.2, 3.3.3, 3.7.1, 3.7.4, 4.2, 9.9.2, 9.4.2, 9.10.1, 13.4

Site Visits, Architect's
3.7.4, 4.2.2, 4.2.9, 9.4.2, 9.5.1, 9.9.2, 9.10.1, 13.4
Special Inspections and Testing
4.2.6, 12.2.1, 13.4
Specifications, Definition of
1.1.6
Specifications
1.1.1, **1.1.6**, 1.2.2, 1.5, 3.12.10, 3.17, 4.2.14
Statute of Limitations
15.1.2, 15.4.1.1
Stopping the Work
2.2.2, 2.4, 9.7, 10.3, 14.1
Stored Materials
6.2.1, 9.3.2, 10.2.1.2, 10.2.4
Subcontractor, Definition of
5.1.1
SUBCONTRACTORS
5
Subcontractors, Work by
1.2.2, 3.3.2, 3.12.1, 3.18, 4.2.3, 5.2.3, 5.3, 5.4, 9.3.1.2, 9.6.7
Subcontractual Relations
5.3, 5.4, 9.3.1.2, 9.6, 9.10, 10.2.1, 14.1, 14.2.1
Submittals
3.10, 3.11, 3.12, 4.2.7, 5.2.1, 5.2.3, 7.3.4, 9.2, 9.3, 9.8, 9.9.1, 9.10.2, 9.10.3
Submittal Schedule
3.10.2, 3.12.5, 4.2.7
Subrogation, Waivers of
6.1.1, **11.3**
Substances, Hazardous
10.3
Substantial Completion
4.2.9, 8.1.1, 8.1.3, 8.2.3, 9.4.2, **9.8**, 9.9.1, 9.10.3, 12.2, 15.1.2
Substantial Completion, Definition of
9.8.1
Substitution of Subcontractors
5.2.3, 5.2.4
Substitution of Architect
2.3.3
Substitutions of Materials
3.4.2, 3.5, 7.3.8
Sub-subcontractor, Definition of
5.1.2
Subsurface Conditions
3.7.4
Successors and Assigns
13.2
Superintendent
3.9, 10.2.6
Supervision and Construction Procedures
1.2.2, **3.3**, 3.4, 3.12.10, 4.2.2, 4.2.7, 6.1.3, 6.2.4, 7.1.3, 7.3.4, 8.2, 8.3.1, 9.4.2, 10, 12, 14, 15.1.4
Suppliers
1.5, 3.12.1, 4.2.4, 4.2.6, 5.2.1, 9.3, 9.4.2, 9.5.4, 9.6, 9.10.5, 14.2.1
Surety

5.4.1.2, 9.6.8, 9.8.5, 9.10.2, 9.10.3, 11.1.2, 14.2.2, 15.2.7

Surety, Consent of
9.8.5, 9.10.2, 9.10.3

Surveys
1.1.7, 2.3.4

Suspension by the Owner for Convenience 14.3

Suspension of the Work
3.7.5, 5.4.2, 14.3
Suspension or Termination of the Contract
5.4.1.1, 14

Taxes

3.6, 3.8.2.1, 7.3.4.4

Termination by the Contractor

14.1, 15.1.7

Termination by the Owner for Cause

5.4.1.1, 14.2, 15.1.7

Termination by the Owner for Convenience 14.4

Termination of the Architect
2.3.3
Termination of the Contractor Employment
14.2.2

TERMINATION OR SUSPENSION OF THE CONTRACT

14

Tests and Inspections

3.1.3, 3.3.3, 3.7.1, 4.2.2, 4.2.6, 4.2.9, 9.4.2, 9.8.3, 9.9.2, 9.10.1, 10.3.2, 12.2.1, 13.4

TIME

8

Time, Delays and Extensions of

3.2.4, 3.7.4, 5.2.3, 7.2.1, 7.3.1, 7.4, 8.3, 9.5.1, 9.7, 10.3.2, 10.4, 14.3.2, 15.1.6, 15.2.5

Time Limits

2.1.2, 2.2, 2.5, 3.2.2, 3.10, 3.11, 3.12.5, 3.15.1, 4.2, 5.2, 5.3, 5.4, 6.2.4, 7.3, 7.4, 8.2, 9.2, 9.3.1, 9.3.3, 9.4.1, 9.5, 9.6, 9.7, 9.8, 9.9, 9.10, 12.2, 13.4, 14, 15.1.2, 15.1.3, 15.4

Time Limits on Claims

3.7.4, 10.2.8, 15.1.2, 15.1.3

Title to Work

9.3.2, 9.3.3

UNCOVERING AND CORRECTION OF WORK

12

Uncovering of Work

12.1

Unforeseen Conditions, Concealed or Unknown

3.7.4, 8.3.1, 10.3

Unit Prices

7.3.3.2, 9.1.2

Use of Documents

1.1.1, 1.5, 2.3.6, 3.12.6, 5.3

Use of Site

3.13, 6.1.1, 6.2.1

Values, Schedule of

9.2, 9.3.1

Waiver of Claims by the Architect

13.3.2

Waiver of Claims by the Contractor

9.10.5, 13.3.2, 15.1.7

Waiver of Claims by the Owner

9.9.3, 9.10.3, 9.10.4, 12.2.2.1, 13.3.2, 14.2.4, 15.1.7

Waiver of Consequential Damages

14.2.4, 15.1.7

Waiver of Liens

9.3, 9.10.2, 9.10.4

Waivers of Subrogation

6.1.1, 11.3

Warranty

3.5, 4.2.9, 9.3.3, 9.8.4, 9.9.1, 9.10.2, 9.10.4, 12.2.2, 15.1.2

Weather Delays

8.3, 15.1.6.2

Work, Definition of

1.1.3

Written Consent

1.5.2, 3.4.2, 3.7.4, 3.12.8, 3.14.2, 4.1.2, 9.3.2, 9.10.3, 13.2, 13.3.2, 15.4.4.2

Written Interpretations

4.2.11, 4.2.12

Written Orders

1.1.1, 2.4, 3.9, 7, 8.2.2, 12.1, 12.2, 13.4.2, 14.3.1

ARTICLE 1 GENERAL PROVISIONS

§ 1.1 Basic Definitions

§ 1.1.1 The Contract Documents

The Contract Documents are enumerated in the Agreement between the Owner and Contractor (hereinafter the Agreement) and consist of the Agreement, Conditions of the Contract (General, Supplementary and other Conditions), Drawings, Specifications, Addenda issued prior to execution of the Contract, other documents listed in the Agreement, and Modifications issued after execution of the Contract. A Modification is (1) a written amendment to the Contract signed by both parties, (2) a Change Order, (3) a Construction Change Directive, or (4) a written order for a minor change in the Work issued by the Architect. The Contract Documents shall include the Instructions to Bidders, the plans, the specifications, the Project Manual, including Divisions 0 through 16, all Addenda and modifications to the plans and/or specifications, the Agreement between Owner and Contractor, the performance and payment bonds, the notice to proceed and any executed change orders. Information and documentation pertaining to soil investigation data, laboratory investigations, soil borings and related information included herein are not part of the Contract Documents. In the event of a conflict between the provisions of Division O and any other section of the Contract Documents, such other sections(s) shall govern.

§ 1.1.2 The Contract

The Contract Documents form the Contract for Construction. The Contract represents the entire and integrated agreement between the parties hereto and supersedes prior negotiations, representations, or agreements, either written or oral. The Contract may be amended or modified only by a Modification. The Contract Documents shall not be construed to create a contractual relationship of any kind (1) between the Contractor and the Architect or the Architect's consultants, (2) between the Owner and a Subcontractor or a Sub-subcontractor, (3) between the Owner and the Architect or the Architect's consultants, or (4) between any persons or entities other than the Owner and the Contractor. The Architect shall, however, be entitled to performance and enforcement of obligations under the Contract intended to facilitate performance of the Architect's duties. Large scale drawings shall govern over small scale drawings where there are differences or conflicts between such drawings. Where the word 'similar' appears on the plans, it shall not be interpreted to mean 'identical' and shall require the Contractor to coordinate the actual conditions and dimensions of the location where the 'similar' conditions are shown to occur.

§ 1.1.3 The Work

The term "Work" means the construction and services required by the Contract Documents, whether completed or partially completed, and includes all other labor, materials, equipment, and services provided or to be provided by the Contractor to fulfill the Contractor's obligations. The Work may constitute the whole or a part of the Project.

§ 1.1.4 The Project

The Project is the total construction of which the Work performed under the Contract Documents may be the whole or a part and which may include construction by the Owner and by Separate Contractors.

§ 1.1.5 The Drawings

The Drawings are the graphic and pictorial portions of the Contract Documents showing the design, location and dimensions of the Work, generally including plans, elevations, sections, details, schedules, and diagrams.

§ 1.1.6 The Specifications

The Specifications are that portion of the Contract Documents consisting of the written requirements for materials, equipment, systems, standards and workmanship for the Work, and performance of related services.

§ 1.1.7 Instruments of Service

Instruments of Service are representations, in any medium of expression now known or later developed, of the tangible and intangible creative work performed by the Architect and the Architect's consultants under their respective professional services agreements. Instruments of Service may include, without limitation, studies, surveys, models, sketches, drawings, specifications, and other similar materials.

§ 1.1.7.1 The Project Manual is a volume assembled for the Work which may include the bidding requirements, sample forms, Conditions of the Contract and Specifications.

§ 1.1.8 Initial Decision Maker

The Initial Decision Maker is the person identified in the Agreement to render initial decisions on Claims in accordance with Section 15.2. The Initial Decision Maker shall not show partiality to the Owner or Contractor and shall not be liable for results of interpretations or decisions rendered in good faith.

§ 1.1.9 Products

The term "products" as used in these Supplementary Conditions includes materials, systems, and equipment.

§ 1.2 Correlation and Intent of the Contract Documents

§ 1.2.1 The intent of the Contract Documents is to include all items necessary for the proper execution and completion of the Work by the Contractor. The Contract Documents are complementary, and what is required by one shall be as binding as if required by all; performance by the Contractor shall be required only to the extent consistent with the Contract Documents and reasonably inferable from them as being necessary to produce the indicated results. In the event of an inconsistency between Drawings and Specifications or within either Document not clarified by addendum, the better quality or greater quantity of Work shall be provided in accordance with the Architect's interpretation. Should the Contractor observe any inconsistency within the Contract Documents, he shall bring them to the Architect's attention for resolution as soon as possible after originally observed.

§ 1.2.1.1 The invalidity of any provision of the Contract Documents shall not invalidate the Contract or its remaining provisions. If it is determined that any provision of the Contract Documents violates any law, or is otherwise invalid or unenforceable, then that provision shall be revised to the extent necessary to make that provision legal and enforceable. In such case the Contract Documents shall be construed, to the fullest extent permitted by law, to give effect to the parties' intentions and purposes in executing the Contract.

§ 1.2.2 Organization of the Specifications into divisions, sections and articles, and arrangement of Drawings shall not control the Contractor in dividing the Work among Subcontractors or in establishing the extent of Work to be performed by any trade.

§ 1.2.3 Unless otherwise stated in the Contract Documents, words that have well-known technical or construction industry meanings are used in the Contract Documents in accordance with such recognized meanings.

§ 1.2.4 It is the intent of the Contract Documents that the Contractor shall properly execute and complete the Work described by the Contract Documents, and unless otherwise provided in the Contract, the Contractor shall provide all labor, materials, equipment, tools, construction equipment and machinery, water, heat, utilities, transportation, and other facilities and services, whether temporary or permanent and whether or not incorporated in the Work, in full accordance with the Contract Documents and reasonably inferable from them as necessary to produce the intended results.

§ 1.2.5 The Contract Documents shall be interpreted collectively, each part complementing the others and consistent with the intent of the Contract Documents. Unless an item shown or described in the Contract Documents is specifically identified to be furnished or installed by the Owner or others or is identified as "Not In Contract" ("N.I.C."), the Contractor's obligation relative to that item shall be interpreted to include furnishing, assembling, installing, finishing, and/or connecting the item at the Contractor's expense to produce a product or system that is complete, appropriately tested, and in operable condition ready for use or subsequent construction or operation by the Owner or separate contractors. The omission of words or phrases for brevity of the Contract Documents, the inadvertent omission of words or phrases, or obvious typographical or written errors shall not defeat such interpretation as long as it is reasonably inferable from the Contract Documents as a whole.

Words or phrases used in the Contract Documents which have well-known technical or construction industry meanings are to be interpreted consistent with such recognized meanings unless otherwise indicated.

Except as noted otherwise, references to standard specifications or publications of associations, bureaus, or organizations shall mean the latest edition of the referenced standard specification or publication as of the date of the Advertisement of Bids.

In the case of inconsistency between Drawings and Specifications or within either document not clarified by addendum, the better quality or greater quantity of Work shall be provided in accordance with the Architect's interpretation.

Generally, portions of the Contract Documents written in longhand take precedence over typed portions, and typed portions take precedence over printed portions.

Any doubt as to the meaning of the Contract Documents or any obscurity as to the wording of them, shall be promptly submitted in writing to the Architect for written interpretation, explanation, or clarification.

§ 1.3 Capitalization

Terms capitalized in these General Conditions include those that are (1) specifically defined, (2) the titles of numbered articles, or (3) the titles of other documents published by the American Institute of Architects.

§ 1.4 Interpretation

In the interest of brevity the Contract Documents frequently omit modifying words such as “all” and “any” and articles such as “the” and “an,” but the fact that a modifier or an article is absent from one statement and appears in another is not intended to affect the interpretation of either statement.

§ 1.5 Ownership and Use of Drawings, Specifications, and Other Instruments of Service

§ 1.5.1 The Architect and the Architect’s consultants shall be deemed the authors and owners of their respective Instruments of Service, including the Drawings and Specifications, and retain all common law, statutory, and other reserved rights in their Instruments of Service, including copyrights. The Contractor, Subcontractors, Sub-subcontractors, and suppliers shall not own or claim a copyright in the Instruments of Service. Submittal or distribution to meet official regulatory requirements or for other purposes in connection with the Project is not to be construed as publication in derogation of the Architect’s or Architect’s consultants’ reserved rights.

§ 1.5.2 The Contractor, Subcontractors, Sub-subcontractors, and suppliers are authorized to use and reproduce the Instruments of Service provided to them, subject to any protocols established pursuant to Sections 1.7 and 1.8, solely and exclusively for execution of the Work. All copies made under this authorization shall bear the copyright notice, if any, shown on the Instruments of Service. The Contractor, Subcontractors, Sub-subcontractors, and suppliers may not use the Instruments of Service on other projects or for additions to the Project outside the scope of the Work without the specific written consent of the Owner, Architect, and the Architect’s consultants.

§ 1.6 Notice

§ 1.6.1 Except as otherwise provided in Section 1.6.2, where the Contract Documents require one party to notify or give notice to the other party, such notice shall be provided in writing to the designated representative of the party to whom the notice is addressed and shall be deemed to have been duly served if delivered in person, by mail, by courier, or by electronic transmission if a method for electronic transmission is set forth in the Agreement.

§ 1.6.2 Notice of Claims as provided in Section 15.1.3 shall be provided in writing and shall be deemed to have been duly served only if delivered to the designated representative of the party to whom the notice is addressed by certified or registered mail, or by courier providing proof of delivery.

ARTICLE 2 OWNER

§ 2.1 General

§ 2.1.1 The Owner is the person or entity identified as such in the Agreement and is referred to throughout the Contract Documents as if singular in number. The Owner shall designate in writing a representative who shall have express authority to bind the Owner with respect to all matters requiring the Owner’s approval or authorization. Except as otherwise provided in Section 4.2.1, the Architect does not have such authority. The term “Owner” means the Owner or the Owner’s authorized representative.

§ 2.1.2 The Owner shall furnish to the Contractor, within fifteen days after receipt of a written request, information necessary and relevant for the Contractor to evaluate, give notice of, or enforce mechanic’s lien rights. Such information shall include a correct statement of the record legal title to the property on which the Project is located, usually referred to as the site, and the Owner’s interest therein.

§ 2.2 Evidence of the Owner’s Financial Arrangements

§ 2.2.1 If the Project is a private project, not funded by public funds, then prior to commencement of the Work and upon written request by the Contractor, the Owner shall furnish to the Contractor reasonable evidence that the Owner has made financial arrangements to fulfill the Owner’s obligations under the Contract. The Contractor shall

have no obligation to commence the Work until the Owner provides such evidence. If commencement of the Work is delayed under this Section 2.2.1, the Contract Time shall be extended appropriately.

§ 2.2.2 Intentionally Deleted

§ 2.2.3 After the Owner furnishes evidence of financial arrangements under this Section 2.2, the Owner shall not materially vary such financial arrangements without prior notice to the Contractor.

§ 2.2.4 Where the Owner has designated information furnished under this Section 2.2 as “confidential,” the Contractor shall keep the information confidential and shall not disclose it to any other person. However, the Contractor may disclose “confidential” information, after seven (7) days’ notice to the Owner, where disclosure is required by law, including a subpoena or other form of compulsory legal process issued by a court or governmental entity, or by court or arbitrator(s) order. The Contractor may also disclose “confidential” information to its employees, consultants, sureties, Subcontractors and their employees, Sub-subcontractors, and others who need to know the content of such information solely and exclusively for the Project and who agree to maintain the confidentiality of such information.

§ 2.3 Information and Services Required of the Owner

§ 2.3.1 Intentionally Deleted.

§ 2.3.2 The Owner shall retain an architect lawfully licensed to practice architecture, or an entity lawfully practicing architecture, in the jurisdiction where the Project is located. That person or entity is identified as the Architect in the Agreement and is referred to throughout the Contract Documents as if singular in number.

§ 2.3.3 If the employment of the Architect terminates, the Owner shall employ a successor to whom the Contractor has no reasonable objection and whose status under the Contract Documents shall be that of the Architect.

§ 2.3.4 Intentionally Deleted

§ 2.3.5 The Owner shall furnish information or services required of the Owner by the Contract Documents with reasonable promptness. The Owner shall also furnish any other information or services under the Owner’s control and relevant to the Contractor’s performance of the Work with reasonable promptness after receiving the Contractor’s written request for such information or services.

§ 2.3.6 Intentionally Deleted

§ 2.4 Owner’s Right to Stop the Work

If the Contractor fails to correct Work which is not in accordance with the requirements of the Contract Documents as required by Article 12.2 or fails to carry out Work in accordance with the Contract Documents or fails to perform any of its obligations under the Contract Documents, the Owner may issue a written order to the Contractor to stop the Work, or any portion thereof, until the cause for such order has been eliminated. However, the right of the Owner to stop the Work shall not give rise to a duty on the part of the Owner to exercise this right for the benefit of the Contractor or any other person or entity, except to the extent required by Article 6.1.3.

The rights and remedies under this Article 2.4 are in addition to and do not in any respect limit any other rights of the Owner, including its termination rights under Article 14.

If the Contractor fails to correct Work that is not in accordance with the requirements of the Contract Documents as required by Section 12.2 or repeatedly fails to carry out Work in accordance with the Contract Documents, the Owner may issue a written order to the Contractor to stop the Work, or any portion thereof, until the cause for such order has been eliminated; however, the right of the Owner to stop the Work shall not give rise to a duty on the part of the Owner to exercise this right for the benefit of the Contractor or any other person or entity, except to the extent required by Section 6.1.3.

§ 2.5 Owner’s Right to Carry Out the Work

If the Contractor defaults or neglects to carry out the Work in accordance with the Contract Documents and fails within a ten-day period after receipt of notice from the Owner to commence and continue correction of such default or neglect with diligence and promptness, the Owner may, without prejudice to other remedies the Owner may have,

correct such default or neglect. Such action by the Owner and amounts charged to the Contractor are both subject to prior approval of the Architect and the Architect may, pursuant to Section 9.5.1, withhold or nullify a Certificate for Payment in whole or in part, to the extent reasonably necessary to reimburse the Owner for the reasonable cost of correcting such deficiencies, including Owner's expenses and compensation for the Architect's additional services made necessary by such default, neglect, or failure. If current and future payments are not sufficient to cover such amounts, the Contractor shall pay the difference to the Owner. If the Contractor disagrees with the actions of the Owner or the Architect, or the amounts claimed as costs to the Owner, the Contractor may file a Claim pursuant to Article 15.

ARTICLE 3 CONTRACTOR

§ 3.1 General

§ 3.1.1 The Contractor is the person or entity identified as such in the Agreement and is referred to throughout the Contract Documents as if singular in number. The Contractor shall be lawfully licensed, if required in the jurisdiction where the Project is located. The Contractor shall designate in writing a representative who shall have express authority to bind the Contractor with respect to all matters under this Contract. The term "Contractor" means the Contractor or the Contractor's authorized representative. The relationship of Contractor to Owner shall be that of independent contractor, and nothing in the Contract Documents is intended to nor should it be construed as creating any other relationship, expressed or implied, between Owner and Contractor.

§ 3.1.2 The Contractor shall perform the Work in accordance with the Contract Documents.

§ 3.1.3 The Contractor shall not be relieved of its obligations to perform the Work in accordance with the Contract Documents either by activities or duties of the Architect in the Architect's administration of the Contract, or by tests, inspections or approvals required or performed by persons or entities other than the Contractor.

§ 3.2 Review of Contract Documents and Field Conditions by Contractor

§ 3.2.1 Execution of the Contract by the Contractor is a representation that the Contractor has visited the site, become generally familiar with local conditions under which the Work is to be performed, and correlated personal observations with requirements of the Contract Documents.

§ 3.2.2 Because the Contract Documents are complementary, the Contractor shall, before starting each portion of the Work, carefully study and compare the various Contract Documents relative to that portion of the Work, as well as the information furnished by the Owner pursuant to Section 2.3.4, shall take field measurements of any existing conditions related to that portion of the Work, and shall observe any conditions at the site affecting it. These obligations are for the purpose of facilitating coordination and construction by the Contractor and are not for the purpose of discovering errors, omissions, or inconsistencies in the Contract Documents; however, the Contractor shall promptly report to the Architect any errors, inconsistencies or omissions discovered by or made known to the Contractor as a request for information in such form as the Architect may require. It is recognized that the Contractor's review is made in the Contractor's capacity as a contractor and not as a licensed design professional, unless otherwise specifically provided in the Contract Documents.

§ 3.2.3 The Contractor is not required to ascertain that the Contract Documents are in accordance with applicable laws, statutes, ordinances, codes, rules and regulations, or lawful orders of public authorities, but the Contractor shall promptly report to the Architect any nonconformity discovered by or made known to the Contractor as a request for information in such form as the Architect may require.

§ 3.2.4 If the Contractor believes that additional cost or time is involved because of clarifications or instructions the Architect issues in response to the Contractor's notices or requests for information pursuant to Sections 3.2.2 or 3.2.3, the Contractor shall submit Claims as provided in Article 15. If the Contractor fails to perform the obligations of Sections 3.2.2 or 3.2.3, the Contractor shall pay such costs and damages to the Owner, subject to Section 15.1.7, as would have been avoided if the Contractor had performed such obligations. If the Contractor performs those obligations, the Contractor shall not be liable to the Owner or Architect for damages resulting from errors, inconsistencies or omissions in the Contract Documents, for differences between field measurements or conditions and the Contract Documents, or for nonconformities of the Contract Documents to applicable laws, statutes, ordinances, codes, rules and regulations, and lawful orders of public authorities. In no event shall the Owner be liable to the Contractor for alleged errors, omissions, inconsistencies, defects or inadequacies in the Contract Documents in an amount exceeding the Architect's liability to the Owner for same and the limit of the Owner's liability to the Contractor shall not exceed the amount actually recovered by the Owner from the Architect.

§ 3.2.5 The Owner is entitled to deduct from the Contractor's pay applications for amounts paid to the Architect for evaluating and responding to the Contractor's requests for information that are not prepared in accordance with the Contract Documents or where the requested information is available to the Contractor from a careful study and comparison of the Contract Documents, field conditions, other Owner-provided information, Contractor-prepared coordination drawings, or prior Project correspondence or documentation.

§ 3.2.6 Contractor shall not be entitled to an increase in the Price attributable to a claimed error, defect, inconsistency or omission in the design documents which would have been discoverable by a reasonable review by Contractor in the performance of preconstruction services or prior to the commencement of Work if the increased cost would have been avoided upon a discovery prior to commencement of construction. Such limitation does not apply to costs related to betterment or enhanced conditions may be subject to an increase in Price in accordance with the provisions for extras below. No extra charge or compensation shall be allowed on account of differences between actual dimensions and the measurements indicated on the Contract Document.

§ 3.3 Supervision and Construction Procedures

§ 3.3.1 The Contractor shall supervise and direct the Work, using the Contractor's best skill and attention. The Contractor shall be solely responsible for, and have control over, construction means, methods, techniques, sequences, and procedures, and for coordinating all portions of the Work under the Contract. If the Contract Documents give specific instructions concerning construction means, methods, techniques, sequences, or procedures, the Contractor shall evaluate the jobsite safety thereof and shall be solely responsible for the jobsite safety of such means, methods, techniques, sequences, or procedures. If the Contractor determines that such means, methods, techniques, sequences or procedures may not be safe, the Contractor shall give timely notice to the Owner and Architect, and shall propose alternative means, methods, techniques, sequences, or procedures. The Architect shall evaluate the proposed alternative solely for conformance with the design intent for the completed construction. Unless the Architect objects to the Contractor's proposed alternative, the Contractor shall perform the Work using its alternative means, methods, techniques, sequences, or procedures.

§ 3.3.2 The Contractor shall be responsible to the Owner for acts and omissions of the Contractor's employees, Subcontractors and their agents and employees, and other persons or entities performing portions of the Work for, or on behalf of, the Contractor or any of its Subcontractors.

§ 3.3.3 The Contractor shall be responsible for inspection of portions of Work already performed to determine that such portions are in proper condition to receive subsequent Work.

§ 3.4 Labor and Materials

§ 3.4.1 Unless otherwise provided in the Contract Documents, the Contractor shall provide and pay for labor, materials, equipment, tools, construction equipment and machinery, water, heat, utilities, transportation, and other facilities and services necessary for proper execution and completion of the Work, whether temporary or permanent and whether or not incorporated or to be incorporated in the Work.

§ 3.4.2 Except in the case of minor changes in the Work approved by the Architect in accordance with Section 3.12.8 or ordered by the Architect in accordance with Section 7.4, the Contractor may make substitutions only with the consent of the Owner, after evaluation by the Architect and in accordance with a Change Order or Construction Change Directive. Some Sections of the Specifications may not allow substitution of materials, products, or equipment. Where substitution is allowed the request for substitution will only be considered if made in strict accordance with the requirements of Article 3.4.4 below and in the Substitutions section of the Specifications.

§ 3.4.3 The Contractor shall enforce strict discipline and good order among the Contractor's employees and other persons carrying out the Work. The Contractor shall not permit employment of unfit persons or persons not properly skilled in tasks assigned to them.

§ 3.4.4 After the Contract has been executed, the Owner and the Architect may consider a request for the substitution of products in place of those specified only under the conditions set forth in the Substitutions section of the Specifications.

By making requests for substitutions, the Contractor:

- .1 Represents that the Contractor has personally investigated the proposed substitute product and determined that it is equal or superior in all respect to that specified;
- .2 Represents that the Contractor will provide the same warranty for the substitution that the Contractor would for that specified;
- .3 Certifies that the cost data presented is complete and includes all related costs for the substituted product and for Work that must be changed as a result of the substitution, except for the Architect's redesign costs, and waives all claims for additional costs related to the substitution which subsequently become apparent; and
- .4 Shall coordinate the installation of the accepted substitute, making such changes as may be required for the Work to be complete in all respects at its costs.

All substitutions shall be submitted within 30 days of the Notice to Proceed, as per the specifications.

§ 3.4.5 Contractor represents that it has independently investigated, considered and understands the labor conditions in the area surrounding the Project and acknowledges that such conditions may impact the Contractor's cost and/or time of performance of the Contract. Therefore, Contractor further represents that the Contract Price is based upon Contractor's independent investigations into such labor conditions and that the Contract time is reasonable and the date of Substantial Completion is obtainable. As a result, Contractor assumes the risk of increased costs, if any, incurred by it arising out of or related to such labor conditions and acknowledges that Contractor and its surety will reimburse Owner for any additional costs Owner incurs arising out of or related to such labor conditions.

§ 3.4.6 Materials shall conform to manufacturer's standards in effect as of the date they are approved and shall be installed in strict accordance with manufacturer's directions.

§ 3.4.7 Rejection of Defective Work. The Owner or Architect's inspection of the Work shall not relieve the Contractor of its responsibilities to perform the Work in accordance with the Contract Documents and all defective work shall be corrected. Unsuitable work may be rejected by the Architect or Owner, whether or not such work and materials have been previously overlooked or misjudged by the Architect or Owner and accepted for payment. If the Work or any part of the Work shall be found defective any time before the final completion of the Work, the Contractor shall immediately correct such defect satisfactory to the Architect or Owner. If any material brought on the site for use in the Work, or selected for use in the Work, shall be rejected by the Architect or Owner as unsuitable or nonconforming with the Contract Documents, the Contractor shall immediately remove such materials from the vicinity of the Work. Nothing contained herein shall operate in any manner as a waiver of any claim Contractor may have against the Owner or the Architect relating to the inspection of the Work.

§ 3.4.8 Debris.

§3.4.8.1 The Contractor shall not permit the accumulation of debris, both exterior and interior. The Work area shall always be kept satisfactorily clean. The Contractor shall remove debris from the Work site and dispose of it at any private or public dump the Contractor may choose. The Contractor shall arrange for and obtain any approvals necessary from the owners or officials in charge of such dumps and shall bear all costs, including fees resulting from such disposal, in the Contract Price, as applicable.

§3.4.8.2 Garbage shall be removed as frequently as necessary in order to satisfy the requirements of this section.

§3.4.8.3 No open fire shall be permitted on site.

§3.4.8.4 Chemical waste shall be stored in corrosion-resistant containers, removed from the Project site, and disposed of not less frequently than monthly unless directed otherwise. Disposal of chemical waste shall be according to requirements of the Environmental Protection Agency (EPA) and the applicable state and local agencies.

§3.4.8.5 Fueling and lubricating of vehicles and equipment shall be conducted to afford the maximum protection against spills and evaporation. Lubricants to be discarded or burned shall be disposed of according to approved procedures meeting all applicable federal, state and local regulations. In case of an oil or hazardous materials spill large enough to violate federal, state or applicable local regulations, the Architect or Owner shall be notified

immediately. The Contractor shall be responsible for immediately cleaning up any such oil or hazardous waste spills resulting from its operations. Any costs incurred in cleaning up any such spills shall not increase the GMP or Price, as applicable.

§3.4.9 Site and Weather Protection: The Contractor shall take necessary precautions during the execution of the Work involving demolition not to disturb or damage any existing structure, landscaping, walks, roads or other items scheduled to remain. Subject to the other terms of the Contract Documents, the Contractor shall restore any damaged items to original condition as directed by the Architect or Owner. The Contractor shall provide and erect acceptable barricades, fences, signs and other traffic devices to protect the Work from traffic and the public necessary and as required by applicable laws, ordinances, codes, rules and regulations.

§3.4.10 Archaeological and Historical Resources: All items having any apparent historical or archaeological interest discovered during any construction activities shall be carefully preserved and reported immediately to the Owner for determination of appropriate actions to be taken. Any increases to Contractor's time or cost of performance due to historical or archaeological items discovered on the site shall entitle Contractor to a Change Order equitably adjusting the Contract Time and the Contract Price accordingly.

§3.4.11 Safety Requirements:

§3.4.11.1 The Contractor must comply with all federal, state and local safety laws and regulations of the applicable authority in connection with the Work performed under this Contract.

§3.4.11.2 This Project is subject to compliance with Public Law 92-596 "Occupational Safety and Health Act of 1970" (OSHA) with respect to all rules and regulations concerning construction, U.S. Code Title 29, Section 651 et seq., including Volume 36 numbers 75 and 105, of the Federal Register as amended, and as published by the U.S. Department of Labor.

§3.4.11.3 As between Owner and Contractor, Contractor will maintain a Safety Program that requires compliance by everyone on the Project Site.

§ 3.5 Warranty

§ 3.5.1 The Contractor warrants to the Owner and Architect that materials and equipment furnished under the Contract will be of good quality and new unless the Contract Documents require or permit otherwise. The Contractor further warrants that the Work will conform to the requirements of the Contract Documents and will be free from defects, except for those inherent in the quality of the Work the Contract Documents require or permit. Work, materials, or equipment not conforming to these requirements may be considered defective. The Contractor's warranty excludes remedy for damage or defect caused by abuse, alterations to the Work not executed by the Contractor, improper or insufficient maintenance, improper operation, or normal wear and tear and normal usage. If required by the Architect, the Contractor shall furnish satisfactory evidence as to the kind and quality of materials and equipment. . This warranty is not exclusive but is in addition to any additional contract remedies available to Owner.

§ 3.5.2 All material, equipment, or other special warranties required by the Contract Documents shall be issued in the name of the Owner, or shall be transferable to the Owner, and shall commence in accordance with Section 9.8.4.

§ 3.6 Taxes

The Contractor shall pay sales, consumer, use and similar taxes for the Work provided by the Contractor that are legally enacted when bids are received or negotiations concluded, whether or not yet effective or merely scheduled to go into effect.

§ 3.7 Permits, Fees, Notices and Compliance with Laws

§ 3.7.1 The Contractor shall secure and pay for the building permit and all other permits, fees, licenses, inspections and all other approvals and charges necessary for proper execution and completion of the Work.

§ 3.7.2 The Contractor shall comply with and give notices required by applicable laws, statutes, ordinances, codes, rules and regulations, and lawful orders of public authorities applicable to performance of the Work. Contractor is responsible to comply and to assure compliance by its subcontractors and suppliers with all local, state and federal statutes, ordinances, regulations or requirements relating to the performance of the Work, including but not limited to: OSHA and health and safety requirements; labor requirements; worker's compensation and unemployment

requirements; insurance requirements; equal opportunity requirements, tax and withholding requirements; noise requirements; hazardous substance requirements; and waste disposal requirements. Contractor is further responsible for giving all notices required by all of the foregoing law. Contractor shall indemnify and hold harmless the Owner and their respective employees, officers and agents from any claims, damages, fines, penalties and attorney fees incurred by Owner or its employees, officers or agents as a result of Contractor's failure to comply with the foregoing obligations.

§ 3.7.3 If the Contractor performs Work contrary to applicable laws, statutes, ordinances, codes, rules and regulations, or lawful orders of public authorities, the Contractor shall assume appropriate responsibility for such Work and shall bear the costs attributable to correction.

§ 3.7.4 Concealed or Unknown Conditions

If the Contractor encounters conditions at the site that are (1) subsurface or otherwise concealed physical conditions that differ materially from those indicated in the Contract Documents or (2) unknown physical conditions of an unusual nature that differ materially from those ordinarily found to exist and generally recognized as inherent in construction activities of the character provided for in the Contract Documents, the Contractor shall promptly provide notice to the Owner and the Architect before conditions are disturbed and in no event later than 14 days after first observance of the conditions. The Architect will promptly investigate such conditions and, if the Architect determines that they differ materially and cause an increase or decrease in the Contractor's cost of, or time required for, performance of any part of the Work, will recommend that an equitable adjustment be made in the Contract Sum or Contract Time, or both. If the Architect determines that the conditions at the site are not materially different from those indicated in the Contract Documents and that no change in the terms of the Contract is justified, the Architect shall promptly notify the Owner and Contractor, stating the reasons. If either party disputes the Architect's determination or recommendation, that party may submit a Claim as provided in Article 15.

§ 3.7.5 If, in the course of the Work, the Contractor encounters human remains or recognizes the existence of burial markers, archaeological sites or wetlands not indicated in the Contract Documents, the Contractor shall immediately suspend any operations that would affect them and shall notify the Owner and Architect. Upon receipt of such notice, the Owner shall promptly take any action necessary to obtain governmental authorization required to resume the operations. The Contractor shall continue to suspend such operations until otherwise instructed by the Owner but shall continue with all other operations that do not affect those remains or features. Requests for adjustments in the Contract Sum and Contract Time arising from the existence of such remains or features may be made as provided in Article 15.

§ 3.8 Allowances

§ 3.8.1 The Contractor shall include in the Contract Sum all allowances stated in the Contract Documents. Items covered by allowances shall be supplied for such amounts and by such persons or entities as the Owner may direct, but the Contractor shall not be required to employ persons or entities to whom the Contractor has reasonable objection.

§ 3.8.2 Unless otherwise provided in the Contract Documents,

- .1 allowances shall cover the cost to the Contractor of materials and equipment delivered at the site and all required taxes, less applicable trade discounts;
- .2 Contractor's costs for unloading and handling at the site, labor, installation costs, overhead, profit, and other expenses contemplated for stated allowance amounts shall be included in the Contract Sum but not in the allowances; and
- .3 whenever costs are more than or less than allowances, the Contract Sum shall be adjusted accordingly by Change Order. The amount of the Change Order shall reflect (1) the difference between actual costs and the allowances under Section 3.8.2.1 and (2) changes in Contractor's costs under Section 3.8.2.2., except when installation is specified to be included as part of the allowance in the General Requirements.

§ 3.8.3 Materials and equipment under an allowance shall be selected by the Owner with reasonable promptness.

§ 3.9 Superintendent

§ 3.9.1 The Contractor shall employ a competent superintendent and necessary assistants who shall be in attendance at the Project site during performance of the Work. The superintendent shall represent the Contractor, and communications given to the superintendent shall be as binding as if given to the Contractor.

The Contractor shall also employ a competent project manager who shall be primarily responsible for the Contractor's home office activities in connection with the Contract.

The Owner shall have the right, which shall be exercised in a reasonable fashion, to approve the project manager and/or superintendent employed by the Contractor, either before or during the progress of construction.

The superintendent and project manager for the project shall be designated by the Contractor at the pre-construction conference. After Owner's approval of such project manager and superintendent, they shall not be replaced by the Contractor without the Owner's prior written consent, which consent is required unless the Contractor submits proof satisfactory to the Owner that the superintendent and/or the project manager should be terminated by the Contractor for cause.

§ 3.9.2 The Contractor, as soon as practicable after award of the Contract, shall notify the Owner and Architect of the name and qualifications of a proposed superintendent. Within 14 days of receipt of the information, the Architect may notify the Contractor, stating whether the Owner or the Architect (1) has reasonable objection to the proposed superintendent or (2) requires additional time for review. Failure of the Architect to provide notice within the 14-day period shall constitute notice of no reasonable objection.

§ 3.9.3 The Contractor shall not employ a proposed superintendent to whom the Owner or Architect has made reasonable and timely objection. The Contractor shall not change the superintendent without the Owner's consent, which shall not unreasonably be withheld or delayed.

§ 3.10 Contractor's Construction and Submittal Schedules

§ 3.10.1 The Contractor, promptly after being awarded the Contract, shall submit for the Owner's and Architect's information a Contractor's construction schedule for the Work. The schedule shall contain detail appropriate for the Project, including (1) the date of commencement of the Work, interim schedule milestone dates, and the date of Substantial Completion; (2) an apportionment of the Work by construction activity; and (3) the time required for completion of each portion of the Work. The schedule shall provide for the orderly progression of the Work to completion and shall not exceed time limits current under the Contract Documents. The schedule shall be revised at appropriate intervals but, in any event, no less than submission of a revised schedule with each monthly application for payment pursuant to Section 9.3 as required by the conditions of the Work and Project.

§ 3.10.2 The Contractor, promptly after being awarded the Contract and thereafter as necessary to maintain a current submittal schedule, shall submit a submittal schedule for the Architect's approval. The Architect's approval shall not be unreasonably delayed or withheld. The submittal schedule shall (1) be coordinated with the Contractor's construction schedule, and (2) allow the Architect reasonable time to review submittals. If the Contractor fails to submit a submittal schedule, or fails to provide submittals in accordance with the approved submittal schedule, the Contractor shall not be entitled to any increase in Contract Sum or extension of Contract Time based on the time required for review of submittals.

§ 3.10.3 Time being of the essence, the Contractor shall perform the Work in accordance with the most recent schedule submitted to and approved by the Owner and Architect.

§ 3.10.4 To the extent that the Date for Substantial Completion is impacted by any concealed condition or other event for which Contractor is entitled to a time extension, Contractor shall provide Owner with a proposal to accelerate the performance of the Work including estimated costs to be incurred to mitigate the time impact such event shall have on Substantial Completion of the Work. If accepted by Owner, a Change Order will be executed to reflect the change in the Contract Price and the Contract Time if any.

§ 3.10.5 The Contractor shall have weekly progress meetings at the Job Site. Progress of the Work shall be reported in detail with reference to the Construction Schedule. Each interested Subcontractor shall have a competent representative present to report the condition of its portion of the Work and to receive information.

§ 3.10.6 The Contractor will provide or notify Owner or Owner's representative if applicable of needed approvals of submittals, requests for information and requests for change, Owner selections or Owner information or services more than fourteen (14) days prior to the time such approvals or information will be needed so as not to delay the Work. Contractor will further advise Owner and Owner's representative of the date by which such selections must

be made. Contractor may not seek to extend the Contract Completion Date for delays in Owner selections or Owner information if Contractor fails to give Owner notice of the need for selections.

§ 3.11 Documents and Samples at the Site

The Contractor shall make available, at the Project site, the Contract Documents, including Change Orders, Construction Change Directives, and other Modifications, in good order and marked currently to indicate field changes and selections made during construction, and the approved Shop Drawings, Product Data, Samples, and similar required submittals. These shall be in electronic form or paper copy, available to the Architect and Owner, and delivered to the Architect for submittal to the Owner upon completion of the Work as a record of the Work as constructed.

§ 3.12 Shop Drawings, Product Data and Samples

§ 3.12.1 Shop Drawings are drawings, diagrams, schedules, and other data specially prepared for the Work by the Contractor or a Subcontractor, Sub-subcontractor, manufacturer, supplier, or distributor to illustrate some portion of the Work.

§ 3.12.2 Product Data are illustrations, standard schedules, performance charts, instructions, brochures, diagrams, and other information furnished by the Contractor to illustrate materials or equipment for some portion of the Work.

§ 3.12.3 Samples are physical examples that illustrate materials, equipment, or workmanship, and establish standards by which the Work will be judged.

§ 3.12.4 Shop Drawings, Product Data, Samples, and similar submittals are not Contract Documents. Their purpose is to demonstrate how the Contractor proposes to conform to the information given and the design concept expressed in the Contract Documents for those portions of the Work for which the Contract Documents require submittals. Review by the Architect is subject to the limitations of Section 4.2.7. Informational submittals upon which the Architect is not expected to take responsive action may be so identified in the Contract Documents. Submittals that are not required by the Contract Documents may be returned by the Architect without action.

§ 3.12.5 The Contractor shall review for compliance with the Contract Documents, approve, and submit to the Architect, Shop Drawings, Product Data, Samples, and similar submittals required by the Contract Documents, in accordance with the submittal schedule approved by the Architect or, in the absence of an approved submittal schedule, with reasonable promptness and in such sequence as to cause no delay in the Work or in the activities of the Owner or of Separate Contractors.

§ 3.12.6 By submitting Shop Drawings, Product Data, Samples, and similar submittals, the Contractor represents to the Owner and Architect that the Contractor has (1) reviewed and approved them, (2) determined and verified materials, field measurements and field construction criteria related thereto, or will do so, and (3) checked and coordinated the information contained within such submittals with the requirements of the Work and of the Contract Documents. In reviewing Shop Drawings, Product Data, Samples, and similar submittals the Architect shall be entitled to rely upon the Contractor's representation that such information is correct and accurate.

§ 3.12.7 The Contractor shall perform no portion of the Work for which the Contract Documents require submittal and review of Shop Drawings, Product Data, Samples, or similar submittals, until the respective submittal has been approved by the Architect.

§ 3.12.8 The Work shall be in accordance with approved submittals except that the Contractor shall not be relieved of responsibility for deviations from the requirements of the Contract Documents by the Architect's approval of Shop Drawings, Product Data, Samples, or similar submittals, unless the Contractor has specifically notified the Architect of such deviation at the time of submittal and (1) the Architect has given written approval to the specific deviation as a minor change in the Work, or (2) a Change Order or Construction Change Directive has been issued authorizing the deviation. The Contractor shall not be relieved of responsibility for errors or omissions in Shop Drawings, Product Data, Samples, or similar submittals, by the Architect's approval thereof. Unless such written notice has been given, the Architect's approval of a Shop Drawing, Product Data, Sample, or similar submittal shall not constitute approval of any changes not requested on the prior submittal.

§ 3.12.9 The Contractor shall direct specific attention, in writing or on resubmitted Shop Drawings, Product Data, Samples, or similar submittals, to revisions other than those requested by the Architect on previous submittals. In the

absence of such notice, the Architect's approval of a resubmission shall not apply to such revisions. The Architect's review of the Contractor's submittals will be limited to examination of an initial submittal and one (1) resubmittal. The Architect's review of additional submittals will be made only with the consent of the Owner after notification by the Architect. The Owner shall be entitled to deduct from the Contract Sum amounts paid to the Architect for evaluation of such additional resubmittals

§ 3.12.10 The Contractor shall not be required to provide professional services that constitute the practice of architecture or engineering unless such services are specifically required by the Contract Documents for a portion of the Work or unless the Contractor needs to provide such services in order to carry out the Contractor's responsibilities for construction means, methods, techniques, sequences, and procedures. The Contractor shall not be required to provide professional services in violation of applicable law.

§ 3.12.10.1 If professional design services or certifications by a design professional related to systems, materials, or equipment are specifically required of the Contractor by the Contract Documents, the Owner and the Architect will specify all performance and design criteria that such services must satisfy. The Contractor shall be entitled to rely upon the adequacy and accuracy of the performance and design criteria provided in the Contract Documents. The Contractor shall cause such services or certifications to be provided by an appropriately licensed design professional, whose signature and seal shall appear on all drawings, calculations, specifications, certifications, Shop Drawings, and other submittals prepared by such professional. Shop Drawings, and other submittals related to the Work, designed or certified by such professional, if prepared by others, shall bear such professional's written approval when submitted to the Architect. The Owner and the Architect shall be entitled to rely upon the adequacy and accuracy of the services, certifications, and approvals performed or provided by such design professionals, provided the Owner and Architect have specified to the Contractor the performance and design criteria that such services must satisfy. Pursuant to this Section 3.12.10, the Architect will review and approve or take other appropriate action on submittals only for the limited purpose of checking for conformance with information given and the design concept expressed in the Contract Documents.

§ 3.12.10.2 If the Contract Documents require the Contractor's design professional to certify that the Work has been performed in accordance with the design criteria, the Contractor shall furnish such certifications to the Architect at the time and in the form specified by the Architect.

§ 3.13 Use of Site

The Contractor shall confine operations at the site to areas permitted by applicable laws, statutes, ordinances, codes, rules and regulations, lawful orders of public authorities, and the Contract Documents and shall not unreasonably encumber the site with materials or equipment.

§ 3.14 Cutting and Patching

§ 3.14.1 The Contractor shall be responsible for cutting, fitting, or patching required to complete the Work or to make its parts fit together properly. All areas requiring cutting, fitting, or patching shall be restored to the condition existing prior to the cutting, fitting, or patching, unless otherwise required by the Contract Documents.

§ 3.14.2 The Contractor shall not damage or endanger a portion of the Work or fully or partially completed construction of the Owner or Separate Contractors by cutting, patching, or otherwise altering such construction, or by excavation. The Contractor shall not cut or otherwise alter construction by the Owner or a Separate Contractor except with written consent of the Owner and of the Separate Contractor. Consent shall not be unreasonably withheld. The Contractor shall not unreasonably withhold, from the Owner or a Separate Contractor, its consent to cutting or otherwise altering the Work.

§ 3.15 Cleaning Up

§ 3.15.1 The Contractor shall keep the premises and surrounding area free from accumulation of waste materials and rubbish caused by operations under the Contract. At completion of the Work, the Contractor shall remove waste materials, rubbish, the Contractor's tools, construction equipment, machinery, and surplus materials from and about the Project.

§ 3.15.2 If the Contractor fails to clean up as provided in the Contract Documents, the Owner may do so and the Owner shall be entitled to reimbursement from the Contractor.

§ 3.16 Access to Work

The Contractor shall provide the Owner and Architect with access to the Work in preparation and progress wherever located.

§ 3.17 Royalties, Patents and Copyrights

The Contractor shall pay all royalties and license fees. The Contractor shall defend suits or claims for infringement of copyrights and patent rights and shall hold the Owner and Architect harmless from loss on account thereof, but shall not be responsible for defense or loss when a particular design, process, or product of a particular manufacturer or manufacturers is required by the Contract Documents, or where the copyright violations are contained in Drawings, Specifications, or other documents prepared by the Owner or Architect. However, if an infringement of a copyright or patent is discovered by, or made known to, the Contractor, the Contractor shall be responsible for the loss unless the information is promptly furnished to the Architect.

§ 3.18 Indemnification

§ 3.18.1 During performance and up to the date of final acceptance of the work by the Owner, the Contractor shall be responsible for the protection of the person and property of others on or adjacent to the site from damage, loss or injury resulting from the performance of the Work as provided in Articles 3, 4, 5, and 10. The Owner shall not, in any case, be liable for any damage caused to any property by whomsoever owned, nor shall either of them, in any event, be responsible or liable for personal injury or death caused, by the act or omission of the Contractor, its officers, directors, employees, agents, Contractors or invitees.

§ 3.18.2 To the fullest extent permitted by law, the Contractor shall defend, indemnify and hold harmless the Owner, Architect, Architect's consultants, and agents and employees of any of them from and against claims, damages, losses, and expenses, including but not limited to attorneys' fees, arising out of or resulting from performance or nonperformance of the Work. Such obligation shall not be construed to negate, abridge, or reduce other rights or obligations of indemnity that would otherwise exist as to a party or person described in this Section 3.18.

§ 3.18.3 In claims against any person or entity indemnified under this Section 3.18 by an employee of the Contractor, a Subcontractor, anyone directly or indirectly employed by them, or anyone for whose acts they may be liable, the indemnification obligation under Section 3.18.1 shall not be limited by a limitation on amount or type of damages, compensation, or benefits payable by or for the Contractor or a Subcontractor under workers' compensation acts, disability benefit acts, or other employee benefit acts.

ARTICLE 4 ARCHITECT

§ 4.1 General

§ 4.1.1 The Architect is the person or entity retained by the Owner pursuant to Section 2.3.2 and identified as such in the Agreement.

§ 4.1.2 Duties, responsibilities, and limitations of authority of the Architect as set forth in the Contract Documents shall not be restricted, modified, or extended without written consent of the Owner, Contractor, and Architect. Consent shall not be unreasonably withheld.

§ 4.2 Administration of the Contract

§ 4.2.1 The Architect will provide administration of the Contract as described in the Contract Documents during construction until the date the Architect issues the final Certificate for Payment. The Architect will have authority to act on behalf of the Owner only to the extent provided in the Contract Documents.

§ 4.2.2 The Architect will visit the site at intervals appropriate to the stage of construction, or as otherwise agreed with the Owner, to become generally familiar with the progress and quality of the portion of the Work completed, and to determine in general if the Work observed is being performed in a manner indicating that the Work, when fully completed, will be in accordance with the Contract Documents. However, the Architect will not be required to make exhaustive or continuous on-site inspections to check the quality or quantity of the Work. The Architect will not have control over, charge of, or responsibility for the construction means, methods, techniques, sequences or procedures, or for the safety precautions and programs in connection with the Work, since these are solely the Contractor's rights and responsibilities under the Contract Documents.

§ 4.2.3 On the basis of the site visits, the Architect will keep the Owner reasonably informed about the progress and quality of the portion of the Work completed, and promptly report to the Owner (1) known deviations from the

Contract Documents, (2) known deviations from the most recent construction schedule submitted by the Contractor, and (3) defects and deficiencies observed in the Work. The Architect will not be responsible for the Contractor's failure to perform the Work in accordance with the requirements of the Contract Documents. The Architect will not have control over or charge of, and will not be responsible for acts or omissions of, the Contractor, Subcontractors, or their agents or employees, or any other persons or entities performing portions of the Work.

§ 4.2.4 Communications

The Owner and Contractor shall include the Architect in all communications that relate to or affect the Architect's services or professional responsibilities. The Owner shall promptly notify the Architect of the substance of any direct communications between the Owner and the Contractor otherwise relating to the Project. Communications by and with the Architect's consultants shall be through the Architect. Communications by and with Subcontractors and suppliers shall be through the Contractor. Communications by and with Separate Contractors shall be through the Owner.

§ 4.2.5 Based on the Architect's evaluations of the Contractor's Applications for Payment, the Architect after consultation with Owner, will review and certify the amounts due the Contractor and will issue Certificates for Payment in such amounts.

§ 4.2.6 The Architect has authority to reject Work that does not conform to the Contract Documents. Whenever the Architect considers it necessary or advisable, the Architect will have authority to require inspection or testing of the Work in accordance with Sections 13.4.2 and 13.4.3, whether or not the Work is fabricated, installed or completed. However, neither this authority of the Architect nor a decision made in good faith either to exercise or not to exercise such authority shall give rise to a duty or responsibility of the Architect to the Contractor, Subcontractors, suppliers, their agents or employees, or other persons or entities performing portions of the Work.

§ 4.2.7 The Architect will review and approve, or take other appropriate action upon, the Contractor's submittals such as Shop Drawings, Product Data, and Samples, but only for the limited purpose of checking for conformance with information given and the design concept expressed in the Contract Documents. The Architect's action will be taken in accordance with the submittal schedule approved by the Architect or, in the absence of an approved submittal schedule, with reasonable promptness while allowing sufficient time in the Architect's professional judgment to permit adequate review. Review of such submittals is not conducted for the purpose of determining the accuracy and completeness of other details such as dimensions and quantities, or for substantiating instructions for installation or performance of equipment or systems, all of which remain the responsibility of the Contractor as required by the Contract Documents. The Architect's review of the Contractor's submittals shall not relieve the Contractor of the obligations under Sections 3.3, 3.5, and 3.12. The Architect's review shall not constitute approval of safety precautions or of any construction means, methods, techniques, sequences, or procedures. The Architect's approval of a specific item shall not indicate approval of an assembly of which the item is a component.

§ 4.2.8 The Architect will prepare Change Orders and Construction Change Directives, and may order minor changes in the Work as provided in Section 7.4. The Architect will investigate and make determinations and recommendations regarding concealed and unknown conditions as provided in Section 3.7.4. All Change Orders, Construction Change Directives and field directives shall require the approval of the Owner in writing to be binding on the Owner and before Contractor is required to commence the changed Work.

§ 4.2.9 The Architect will conduct inspections to determine the date or dates of Substantial Completion and the date of final completion; issue Certificates of Substantial Completion pursuant to Section 9.8; receive and forward to the Owner, for the Owner's review and records, written warranties and related documents required by the Contract and assembled by the Contractor pursuant to Section 9.10; and issue a final Certificate for Payment pursuant to Section 9.10.

§ 4.2.10 If the Owner and Architect agree, the Architect will provide one or more Project representatives to assist in carrying out the Architect's responsibilities at the site. The Owner shall notify the Contractor of any change in the duties, responsibilities and limitations of authority of the Project representatives.

§ 4.2.11 The Architect will interpret and decide matters concerning performance under, and requirements of, the Contract Documents on written request of either the Owner or Contractor. The Architect's response to such requests will be made in writing within any time limits agreed upon or otherwise with reasonable promptness.

§ 4.2.12 Interpretations and decisions of the Architect will be consistent with the intent of, and reasonably inferable from, the Contract Documents and will be in writing or in the form of drawings. When making such interpretations and decisions, the Architect will endeavor to secure faithful performance by both Owner and Contractor, will not show partiality to either, and will not be liable for results of interpretations or decisions rendered in good faith.

§ 4.2.13 The Architect's decisions on matters relating to aesthetic effect will be final if consistent with the intent expressed in the Contract Documents.

§ 4.2.14 The Architect will review and respond to requests for information about the Contract Documents. The Architect's response to such requests will be made in writing within any time limits agreed upon or otherwise with reasonable promptness. If appropriate, the Architect will prepare and issue supplemental Drawings and Specifications in response to the requests for information.

ARTICLE 5 SUBCONTRACTORS

§ 5.1 Definitions

§ 5.1.1 A Subcontractor is a person or entity who has a direct contract with the Contractor to perform a portion of the Work at the site. The term "Subcontractor" is referred to throughout the Contract Documents as if singular in number and means a Subcontractor or an authorized representative of the Subcontractor. The term "Subcontractor" does not include a Separate Contractor or the subcontractors of a Separate Contractor.

§ 5.1.2 A Sub-subcontractor is a person or entity who has a direct or indirect contract with a Subcontractor to perform a portion of the Work at the site. The term "Sub-subcontractor" is referred to throughout the Contract Documents as if singular in number and means a Sub-subcontractor or an authorized representative of the Sub-subcontractor.

§ 5.2 Award of Subcontracts and Other Contracts for Portions of the Work

§ 5.2.1 The Contractor, with its first Application for Payment and as a condition to the Owner's obligation to make payments to Contractor under Article 9 of the General Conditions as supplemented herein shall notify the Owner and Architect of the persons or entities proposed for each principal portion of the Work, including those who are to furnish materials or equipment fabricated to a special design. Within 14 days of receipt of the information, the Architect may notify the Contractor whether the Owner or the Architect (1) has reasonable objection to any such proposed person or entity or (2) requires additional time for review. Failure of the Architect to provide notice within the 14-day period shall constitute notice of no reasonable objection.

§ 5.2.2 The Contractor shall not contract with a proposed person or entity to whom the Owner or Architect has made reasonable and timely objection. The Contractor shall not be required to contract with anyone to whom the Contractor has made reasonable objection.

§ 5.2.3 If the Owner or Architect has reasonable objection to a person or entity proposed by the Contractor, the Contractor shall propose another to whom the Owner or Architect has no reasonable objection. If the proposed but rejected Subcontractor was reasonably capable of performing the Work, the Contract Sum and Contract Time shall be increased or decreased by the difference, if any, occasioned by such change, and an appropriate Change Order shall be issued before commencement of the substitute Subcontractor's Work. However, no increase in the Contract Sum or Contract Time shall be allowed for such change unless the Contractor has acted promptly and responsively in submitting names as required.

§ 5.2.4 The Contractor shall not substitute a Subcontractor, person, or entity for one previously selected if the Owner or Architect makes reasonable objection to such substitution.

§ 5.2.5 The Contractor's substitution of any subcontractor, supplier, person, or entity previously identified by Contractor in accordance with Article 5.2.1 shall entitle the Owner to reject the work, materials or product furnished and require removal and replacement at no additional cost to the Owner unless the substitution is approved by Owner in writing.

§ 5.3 Subcontractual Relations

By appropriate written agreement, the Contractor shall require each Subcontractor, to the extent of the Work to be performed by the Subcontractor, to be bound to the Contractor by terms of the Contract Documents, and to assume

toward the Contractor all the obligations and responsibilities, including the responsibility for safety of the Subcontractor's Work that the Contractor, by these Contract Documents, assumes toward the Owner and Architect. Each subcontract agreement shall preserve and protect the rights of the Owner and Architect under the Contract Documents with respect to the Work to be performed by the Subcontractor so that subcontracting thereof will not prejudice such rights, and shall allow to the Subcontractor, unless specifically provided otherwise in the subcontract agreement, the benefit of all rights, remedies, and redress against the Contractor that the Contractor, by the Contract Documents, has against the Owner. Where appropriate, the Contractor shall require each Subcontractor to enter into similar agreements with Sub-subcontractors. The Contractor shall make available to each proposed Subcontractor, prior to the execution of the subcontract agreement, copies of the Contract Documents to which the Subcontractor will be bound, and, upon written request of the Subcontractor, identify to the Subcontractor terms and conditions of the proposed subcontract agreement that may be at variance with the Contract Documents. Subcontractors will similarly make copies of applicable portions of such documents available to their respective proposed Sub-subcontractors.

§ 5.4 Contingent Assignment of Subcontracts

§ 5.4.1 Each subcontract agreement for a portion of the Work is assigned by the Contractor to the Owner, provided that

- .1 assignment is effective only after termination of the Contract by the Owner for cause pursuant to Section 14.2 and only for those subcontract agreements that the Owner accepts by notifying the Subcontractor and Contractor; and
- .2 assignment is subject to the prior rights of the surety, if any, obligated under bond relating to the Contract.

When the Owner accepts the assignment of a subcontract agreement, the Owner assumes the Contractor's rights and obligations under the subcontract.

§ 5.4.2 Upon such assignment, if the Work has been suspended for more than 30 days, the Subcontractor's compensation shall be equitably adjusted for increases in cost resulting from the suspension.

§ 5.4.3 Upon assignment to the Owner under this Section 5.4, the Owner may further assign the subcontract to a successor contractor or other entity. If the Owner assigns the subcontract to a successor contractor or other entity, the Owner shall nevertheless remain legally responsible for all of the successor contractor's obligations under the subcontract.

ARTICLE 6 CONSTRUCTION BY OWNER OR BY SEPARATE CONTRACTORS

§ 6.1 Owner's Right to Perform Construction and to Award Separate Contracts

§ 6.1.1 The term "Separate Contractor(s)" shall mean other contractors retained by the Owner under separate agreements. The Owner reserves the right to perform construction or operations related to the Project with the Owner's own forces and to award separate contracts either in connection with other portions of the Project or other construction or operation on the site. In such event, the Contractor shall coordinate its activities with those of the Owner and of Separate Contractors so as to facilitate the general progress of all work being performed by all parties. Cooperation will be required in the arrangement for the storage of materials, and in the detailed execution of the Work.

The Contractor, including his subcontractors, shall keep informed of the progress and the detailed work of the Owner or Separate Contractors and shall immediately notify the Architect of lack of progress or delays by Separate Contractors which are affecting Contractor's Work. Failure of Contractor to keep informed of the progress of the work of the Owner or Separate Contractors and/or failure of Contractor to give notice of lack of progress or delays by the Owner or Separate Contractors shall be deemed to be acceptance by Contractor of the status of progress by Separate Contractors for the proper coordination and completion of Contractor's Work. If, through acts or neglect on the part of the Contractor, the Owner or any Separate Contractors shall suffer loss or damage or assert any claims of whatever nature against the Owner, the Contractor shall defend, indemnify and hold harmless the Owner from any such claims or alleged damages, and the Contractor shall resolve such alleged damages or claims directly with the Separate Contractors

§ 6.2 Mutual Responsibility

§ 6.2.1 The Contractor shall afford the Owner and Separate Contractors reasonable opportunity for introduction and storage of their materials and equipment and performance of their activities, and shall connect and coordinate the Contractor's construction and operations with theirs as required by the Contract Documents.

§ 6.2.2 If part of the Contractor's Work depends for proper execution or results upon construction or operations by the Owner or a Separate Contractor, the Contractor shall, prior to proceeding with that portion of the Work, promptly notify the Architect of apparent discrepancies or defects in the construction or operations by the Owner or Separate Contractor that would render it unsuitable for proper execution and results of the Contractor's Work. Failure of the Contractor to notify the Architect of apparent discrepancies or defects prior to proceeding with the Work shall constitute an acknowledgment that the Owner's or Separate Contractor's completed or partially completed construction is fit and proper to receive the Contractor's Work. The Contractor shall not be responsible for discrepancies or defects in the construction or operations by the Owner or Separate Contractor that are not apparent.

§ 6.2.3 Intentionally Omitted.

§ 6.2.4 The Contractor shall promptly remedy damage that the Contractor wrongfully causes to completed or partially completed construction or to property of the Owner or Separate Contractor as provided in Section 10.2.5.

§ 6.2.5 The Owner and each Separate Contractor shall have the same responsibilities for cutting and patching as are described for the Contractor in Section 3.14.

§ 6.3 Owner's Right to Clean Up

If a dispute arises among the Contractor, Separate Contractors, and the Owner as to the responsibility under their respective contracts for maintaining the premises and surrounding area free from waste materials and rubbish, the Owner may clean up and the Architect will allocate the cost among those responsible.

ARTICLE 7 CHANGES IN THE WORK

§ 7.1 General

§ 7.1.1 Changes in the Work may be accomplished after execution of the Contract, and without invalidating the Contract, by Change Order, Construction Change Directive or order for a minor change in the Work, subject to the limitations stated in this Article 7 and elsewhere in the Contract Documents. Contractor shall be entitled to a claim for an increase in the Price or an equitable adjustment in the Price only in the following circumstances and compliance with the requirements of this Agreement and Article 15 of the General Conditions. When submitting its Change Order proposal, the Contractor shall include and set forth in clear and reasonable detail breakdowns of labor and materials for all trades involved and the estimated impact on the construction schedule to the extent then reasonably known by Contractor. The Contractor shall furnish spreadsheets from which the breakdowns were prepared, plus spread sheets if requested of any Subcontractors.

§ 7.1.2 A Change Order shall be based upon agreement among the Owner, Contractor, and Architect. A Construction Change Directive requires agreement by the Owner and Architect and may or may not be agreed to by the Contractor. An order for a minor change in the Work may be issued by the Architect alone.

§ 7.1.3 Changes in the Work shall be performed under applicable provisions of the Contract Documents. The Contractor shall proceed promptly with changes in the Work, unless otherwise provided in the Change Order, Construction Change Directive, or order for a minor change in the Work. . No course of conduct or dealings between the parties, nor verbal express or implied acceptance of alterations or additions to the Work, and no claim that Owner has been unjustly enriched by any alteration of or addition to the Work, whether or not there is, in fact, any unjust enrichment to the Work, shall be the basis of any claim to an increase in any amounts due under the Contract Documents or a change in any time period provided for the in the Contract Documents in the absence of written Notice as provided in the Contract Document.

§ 7.1.4 The combined overhead (overhead includes general home office, field personnel, superintendents, and all costs attributable to field and office personnel), taxes (including Mississippi's 3.5 percent gross receipts tax), insurance and profit included in the total cost to the Owner of a change in the Work shall be based on the following schedule:

- .1 For the Contractor, the Work performed by the Contractor's own forces, fifteen percent of the cost.
- .2 For the Contractor, for Work performed by the Contractor's Subcontractors, ten percent of the amount due the Subcontractor.
- .3 For each Subcontractor or Sub-subcontractor involved, for Work performed by that Subcontractor's or Sub-subcontractor's own forces, fifteen percent of the cost.
- .4 For each Subcontractor involved, for Work performed by the Subcontractor's Sub-subcontractor, ten percent of the amount due the Sub-subcontractor.
- .5 Cost to which overhead and profit is to be applied shall be determined in accordance with Subparagraph 7.3.7.
- .6 In order to facilitate checking of quotations for extras or credits, all proposals, except those so minor that their propriety can be seen by inspection, shall be accompanied by a complete itemization of costs including labor, materials, and Subcontracts. Labor and materials shall be itemized in the manner prescribed above. Where major cost items are Subcontracts, they shall be itemized also. In no case will a change involving an amount over Five Hundred Dollars be approved without such itemization.

§ 7.1.5 If the methods set forth in Section 7.1.4 is not applicable, the Contractor, provided he receives a written order signed by the Owner, shall promptly proceed with the Work involved. The cost of such Work shall then be subject to a recommendation by the Architect on the basis of the reasonable expenditures and savings of those performing the Work attributable to the change, including, in the case of an increase in the Contract Sum, a reasonable allowance for overhead and profit. The Architect recommendation shall be advisory and admissible in any proceeding but it shall not be binding on Contractor or Owner in the absence of a mutual agreement. If the Owner and Contractor cannot reach a mutual agreement, any Claim shall be subject to the provisions of Article 15.

§ 7.2 Change Orders

§ 7.2.1 A Change Order is a written instrument prepared by the Architect and signed by the Owner, Contractor, and Architect stating their agreement upon all of the following:

- .1 The change in the Work;
- .2 The amount of the adjustment, if any, in the Contract Sum; and
- .3 The extent of the adjustment, if any, in the Contract Time.

§ 7.2.2 Contractor's execution of a change order constitutes a final settlement to the Contract Sum and construction schedule and the Contract Time for all matters relating to or arising out of the change in the Work that is the subject of the change order including, but not limited to, all direct and indirect costs associated with such change, all extended direct job site and home office overhead expenses and any and all delay and impact cost for the change, whether alone or in combination with other changes, including any impact, ripple or cumulative effect resulting therefrom, if any.

§ 7.2.3 Adjustments to the Contract Sum by change order shall be based upon one of the methods set forth in Article 7.3, as appropriate. A reasonable allowance for the combined overhead and profit included in the change order shall be based upon the schedule set forth in Article 7.1.4, as supplemented.

§ 7.2.4 In order to facilitate consideration of change order requests, all such requests, except those involving an amount less than \$500 must be accompanied by a complete itemization of costs, including labor, materials and subcontractor costs which shall likewise be itemized. Changes for more than \$500 will not be approved without such itemization.

§ 7.3 Construction Change Directives

§ 7.3.1 A Construction Change Directive is a written order prepared by the Architect and signed by the Owner and Architect, directing a change in the Work prior to agreement on adjustment, if any, in the Contract Sum or Contract Time, or both. The Owner may by Construction Change Directive, without invalidating the Contract, order changes in the Work within the general scope of the Contract consisting of additions, deletions, or other revisions, the Contract Sum and Contract Time being adjusted accordingly.

§ 7.3.2 A Construction Change Directive shall be used in the absence of total agreement on the terms of a Change Order.

§ 7.3.3 If the Construction Change Directive provides for an adjustment to the Contract Sum, the adjustment shall be based on one of the following methods:

- .1 Mutual acceptance of a lump sum properly itemized and supported by sufficient substantiating data to permit evaluation; The cost or credit to the Owner resulting from a change in the work shall be calculated in the same manner as described in Subparagraph 7.1.4 (above);
- .2 Unit prices stated in the Contract Documents or subsequently agreed upon;

§ 7.3.4 Intentionally Deleted

§ 7.3.5 If the Owner or Contractor disagrees with the adjustment in the Contract Time, the Contractor may make a Claim in accordance with applicable provisions of Article 15.

§ 7.3.6 Upon receipt of a Construction Change Directive, the Contractor shall promptly proceed with the change in the Work involved and advise the Architect of the Contractor's agreement or disagreement with the method, if any, provided in the Construction Change Directive for determining the proposed adjustment in the Contract Sum or Contract Time.

§ 7.3.7 A Construction Change Directive signed by the Contractor indicates the Contractor's agreement therewith, including adjustment in Contract Sum and Contract Time or the method for determining them. Such agreement shall be effective immediately and shall be recorded as a Change Order.

§ 7.3.8 The amount of credit to be given by the Contractor to the Owner for a deletion or change which results in a net decrease in the Contract Sum shall be the actual net cost plus reasonable allowance for overhead on net cost and profit thereon as approved by the Architect and Owner. When both additions and credits covering related Work or substitutions are involved in a change, the allowance for overhead and profit shall be figured on the basis of net increase, if any, with respect to that change.

§ 7.3.9 Pending final determination of the total cost of a Construction Change Directive to the Owner, the Contractor may request payment for Work completed under the Construction Change Directive in Applications for Payment. The Architect will make an interim determination for purposes of monthly certification for payment for those costs and certify for payment the amount that the Architect determines, in the Architect's professional judgment, to be reasonably justified. The Architect's interim determination of cost shall adjust the Contract Sum on the same basis as a Change Order, subject to the right of either party to disagree and assert a Claim in accordance with Article 15.

§ 7.3.10 When the Owner and Contractor agree with a determination made by the Architect concerning the adjustments in the Contract Sum and Contract Time, or otherwise reach agreement upon the adjustments, such agreement shall be effective immediately and the Architect will prepare a Change Order. Change Orders may be issued for all or any part of a Construction Change Directive.

§ 7.4 Minor Changes in the Work

The Architect may order minor changes in the Work that are consistent with the intent of the Contract Documents and do not involve an adjustment in the Contract Sum or an extension of the Contract Time. The Architect's order for minor changes shall be in writing. If the Contractor believes that the proposed minor change in the Work will affect the Contract Sum or Contract Time, the Contractor shall notify the Architect and shall not proceed to implement the change in the Work. If the Contractor performs the Work set forth in the Architect's order for a minor change without prior notice to the Architect that such change will affect the Contract Sum or Contract Time, the Contractor waives any adjustment to the Contract Sum or extension of the Contract Time.

ARTICLE 8 TIME

§ 8.1 Definitions

§ 8.1.1 Unless otherwise provided, Contract Time is the period of time, including authorized adjustments, allotted in the Contract Documents for Substantial Completion of the Work.

§ 8.1.2 The date of commencement of the Work is the date established in the Agreement.

§ 8.1.3 The date of Substantial Completion is the date certified in writing by both the Architect and Owner in accordance with Section 9.8.

§ 8.1.4 The term "day" as used in the Contract Documents shall mean calendar day unless otherwise specifically defined.

§ 8.2 Progress and Completion

§ 8.2.1 Time limits stated in the Contract Documents are of the essence of the Contract. By executing the Agreement, the Contractor confirms that the Contract Time is a reasonable period for performing the

Work and that the Contractor is fully capable of properly completing the Work within the Contract Time.

§ 8.2.2 The Contractor shall not knowingly, except by agreement or instruction of the Owner in writing, commence the Work prior to the effective date of insurance required to be furnished by the Contractor and Owner.

§ 8.2.3 The Contractor shall proceed expeditiously with adequate forces and shall achieve Substantial Completion within the Contract Time.

§ 8.3 Delays and Extensions of Time

§ 8.3.1 If the Contractor is delayed at any time in the commencement or progress of the Work by (1) an act or neglect of the Owner or Architect, of an employee of either, or of a Separate Contractor; (2) by changes ordered in the Work; (3) by labor disputes, fire, unusual delay in deliveries, unavoidable casualties, adverse weather conditions documented in accordance with Section 15.1.6.2, or other causes beyond the Contractor's control; or (4) by other causes that the Contractor asserts, and the Architect determines, justify delay, then the Contract Time shall be extended for such reasonable time as the Architect may determine.

§ 8.3.1.1 The words "other causes beyond the Contractor's control" as used in Subparagraph 8.3.1 shall not be interpreted as pertaining to bad weather days. The term "consecutive calendar days", as used in the bid form and the Agreement Between the Owner and Contractor to define a specific time period, shall include bad weather days. The term "bad weather days" shall be defined as days which adverse weather conditions, such as rain, snow, sleet, wind, fog, thunderstorms, hurricanes, lightning, temperature, rising water, or other extreme weather conditions, were excessive to the extent that the Contractor could not access the building site or could not perform the work in its proposed or proper sequence. No time extensions shall be granted for "bad weather days".

§ 8.3.1.2 Notwithstanding any other provisions of the Agreement Between the Owner and Contractor, it is mutually understood that the time extensions for changes in the work will depend on the extent, if any, by which the changes cause delay in the completion of the various elements of construction. The change order granting the time extension may provide that the contract completion date will be extended only for those specific elements so delayed and that the remaining contract completion dates for all other portions of the work not be altered.

§ 8.3.2 Claims relating to time shall be made in accordance with applicable provisions of Article 15.

§ 8.3.3 This Section 8.3 does not preclude recovery of damages for delay by either party under other provisions of the Contract Documents. No delay, interference, hindrance or disruption, from whatever source or cause, in the progress of the Contractor's Work shall be a basis for an extension of time and/or additional compensation, unless the delay, interference, hindrance or disruption (1) is without the fault and not the responsibility of the Contractor, its subcontractors and/or suppliers and (2) directly affects the overall completion of the Work as reflected on the critical path of the Contractor's updated and accepted construction schedules. The Contractor expressly agrees that the Owner shall have the benefit of any float in the construction schedule and that delays to construction activities, which do not affect the overall completion of the Work, do not entitle the Contractor to any extension in the Contract Time and/or increase in Contract Sum.

§ 8.3.4 All claims by the Contractor for an increase in the Contract Time must follow the procedures set forth in Articles 15.1.2, 15.1.3, 15.1.5 and 15.1.6, including the requirement that the Contractor give written notice of any claim within twenty-one (21) days after occurrence of the event giving rise to such claim or within twenty-one (21) days after the Contractor first recognizes the condition giving rise to the claim, whichever is earlier

§ 8.3.5 If the Contractor submits a schedule indicating or otherwise expressing an intent to complete the Work prior to the date of substantial completion, the Owner shall have no liability to the Contractor for any failure by the Contractor to complete the Work prior to the expiration of the Contract Time.

ARTICLE 9 PAYMENTS AND COMPLETION

§ 9.1 Contract Sum

§ 9.1.1 The Contract Sum is stated in the Agreement and, including authorized adjustments, is the total amount payable by the Owner to the Contractor for performance of the Work under the Contract Documents.

§ 9.1.2 If unit prices are stated in the Contract Documents or subsequently agreed upon, and if quantities originally contemplated are materially changed so that application of such unit prices to the actual quantities causes substantial inequity to the Owner or Contractor, the applicable unit prices shall be equitably adjusted.

§ 9.2 Schedule of Values

Where the Contract is based on a stipulated sum or Guaranteed Maximum Price, the Contractor shall submit a schedule of values to the Architect before the first Application for Payment, allocating the entire Contract Sum to the various portions of the Work. The schedule of values shall be prepared in the form, and supported by the data to substantiate its accuracy, required by the Architect. This schedule, unless objected to by the Architect, shall be used as a basis for reviewing the Contractor's Applications for Payment. Any changes to the schedule of values shall be submitted to the Architect and supported by such data to substantiate its accuracy as the Architect may require, and unless objected to by the Architect, shall be used as a basis for reviewing the Contractor's subsequent Applications for Payment.

§ 9.3 Applications for Payment

§ 9.3.1 At least ten days before the date established for each progress payment, the Contractor shall submit to the Architect an itemized Application for Payment prepared in accordance with the schedule of values, if required under Section 9.2, for completed portions of the Work. The application shall be notarized, if required, and supported by all data substantiating the Contractor's right to payment that the Owner or Architect require, such as copies of requisitions, and releases and waivers of liens from Subcontractors and suppliers, and shall reflect retainage if provided for in the Contract Documents. The form of Application for Payment will be the current edition of the AIA Document G702, Application and Certification for Payment, supported with AIA Document G703, Continuation Sheet.

§ 9.3.1.1 As provided in Section 7.3.9, such applications may include requests for payment on account of changes in the Work that have been properly authorized by Construction Change Directives, or by interim determinations of the Architect, but not yet included in Change Orders.

§ 9.3.1.2 Applications for Payment shall not include requests for payment for portions of the Work for which the Contractor does not intend to pay a Subcontractor or supplier, unless such Work has been performed by others whom the Contractor intends to pay.

§ 9.3.1.3 In any contract awarded by the state of Mississippi or any agency, unit, or department of the State of Mississippi, or by any political subdivision thereof, the amount of retainage that may be withheld is governed by Mississippi law.

§ 9.3.1.4 There will be no extension of time due to weather.

§ 9.3.2 Unless otherwise provided in the Contract Documents, payments shall be made on account of materials and equipment delivered and suitably stored at the site for subsequent incorporation in the Work. If approved in advance by the Owner, payment may similarly be made for materials and equipment suitably stored off the site at a location agreed upon in writing. Payment for materials and equipment stored on or off the site shall be conditioned upon compliance by the Contractor with procedures satisfactory to the Owner to establish the Owner's title to such

materials and equipment or otherwise protect the Owner's interest, and shall include the costs of applicable insurance, storage, and transportation to the site, for such materials and equipment stored off the site.

§ 9.3.2.1 Payment for materials stored at some location other than the Project site, may be approved by the Architect and the Owner after the Contractor has submitted the following items:

- .1 An acceptable Lease Agreement between the Contractor or one of its subcontractors or suppliers and the owner of the land, or building, where the materials are stored covering the specific area where the materials are located.
- .2 Consent of Surety or other acceptable bond to cover the materials stored off-site.
- .3 All Perils Insurance coverage for the full value of the materials stored off-site.
- .4 A Bill of Sale from the Manufacturer to the Contractor for the stored materials.
- .5 A complete list and inventory of materials manufactured, stored and delivered to the storage site and of materials removed from the storage site and delivered to the Project.
- .6 A review by the Architect of the materials stored off-site prior to release of payment.
- .7 Proof of payment of stored materials verified by the supplier must be submitted to the Architect within thirty (30) days of the Application for Payment on which payment for said materials was made. If proof of payment is not submitted within thirty (30) days, then payment for said materials will be deducted from the next application for payment and withheld until proof of payment is received.

§ 9.3.3 The Contractor warrants that title to all Work covered by an Application for Payment will pass to the Owner no later than the time of payment. The Contractor further warrants that upon submittal of an Application for Payment all Work for which Certificates for Payment have been previously issued and payments received from the Owner shall, to the best of the Contractor's knowledge, information, and belief, be free and clear of liens, claims, security interests, or encumbrances, in favor of the Contractor, Subcontractors, suppliers, or other persons or entities that provided labor, materials, and equipment relating to the Work.

§ 9.4 Certificates for Payment

§ 9.4.1 The Architect will, within seven days after receipt of the Contractor's Application for Payment, either (1) issue to the Owner a Certificate for Payment in the full amount of the Application for Payment, with a copy to the Contractor; or (2) issue to the Owner a Certificate for Payment for such amount as the Architect determines is properly due, and notify the Contractor and Owner of the Architect's reasons for withholding certification in part as provided in Section 9.5.1; or (3) withhold certification of the entire Application for Payment, and notify the Contractor and Owner of the Architect's reason for withholding certification in whole as provided in Section 9.5.1.

§ 9.4.2 The issuance of a Certificate for Payment will constitute a representation by the Architect to the Owner, based on the Architect's evaluation of the Work and the data in the Application for Payment, that, to the best of the Architect's knowledge, information, and belief, the Work has progressed to the point indicated, the quality of the Work is in accordance with the Contract Documents, and that the Contractor is entitled to payment in the amount certified. The foregoing representations are subject to an evaluation of the Work for conformance with the Contract Documents upon Substantial Completion, to results of subsequent tests and inspections, to correction of minor deviations from the Contract Documents prior to completion, and to specific qualifications expressed by the Architect. However, the issuance of a Certificate for Payment will not be a representation that the Architect has (1) made exhaustive or continuous on-site inspections to check the quality or quantity of the Work; (2) reviewed construction means, methods, techniques, sequences, or procedures; (3) reviewed copies of requisitions received from Subcontractors and suppliers and other data requested by the Owner to substantiate the Contractor's right to payment; or (4) made examination to ascertain how or for what purpose the Contractor has used money previously paid on account of the Contract Sum.

§ 9.5 Decisions to Withhold Certification

§ 9.5.1 The Architect may withhold a Certificate for Payment in whole or in part, to the extent reasonably necessary to protect the Owner, if in the Architect's opinion the representations to the Owner required by Section 9.4.2 cannot

be made. If the Architect is unable to certify payment in the amount of the Application, the Architect will notify the Contractor and Owner as provided in Section 9.4.1. If the Contractor and Architect cannot agree on a revised amount, the Architect will promptly issue a Certificate for Payment for the amount for which the Architect is able to make such representations to the Owner. The Architect may also withhold a Certificate for Payment or, because of subsequently discovered evidence, may nullify the whole or a part of a Certificate for Payment previously issued, to such extent as may be necessary in the Architect's opinion to protect the Owner from loss for which the Contractor is responsible, including loss resulting from acts and omissions described in Section 3.3.2, because of

- .1 defective Work not remedied;
- .2 third party claims filed or reasonable evidence indicating probable filing of such claims, unless security acceptable to the Owner is provided by the Contractor;
- .3 failure of the Contractor to make payments properly to Subcontractors or suppliers for labor, materials or equipment;
- .4 reasonable evidence that the Work cannot be completed for the unpaid balance of the Contract Sum;
- .5 damage to the Owner or a Separate Contractor;
- .6 reasonable evidence that the Work will not be completed within the Contract Time, and that the unpaid balance would not be adequate to cover actual or liquidated damages for the anticipated delay; or
- .7 failure to carry out the Work in accordance with the Contract Documents.
- .8 The letter from the Contractor which is required by Article 15.1.6.2 has not been received.
- .9 Failure to properly coordinate all phases of the Work, including the failure to prepare, maintain and/or update the Progress Schedule;
- .10 Failure to verify that all materials, equipment, and work in full accordance with the Contract Documents;
- .11 Failure to comply with the specified submittal procedures.

§ 9.5.2 When either party disputes the Architect's decision regarding a Certificate for Payment under Section 9.5.1, in whole or in part, that party may submit a Claim in accordance with Article 15.

§ 9.5.3 When the reasons for withholding certification are removed, certification will be made for amounts previously withheld.

§ 9.5.4 If the Architect withholds certification for payment under Section 9.5.1.3, the Owner may, at its sole option, issue joint checks to the Contractor and to any Subcontractor or supplier to whom the Contractor failed to make payment for Work properly performed or material or equipment suitably delivered. If the Owner makes payments by joint check, the Owner shall notify the Architect and the Contractor shall reflect such payment on its next Application for Payment.

§ 9.6 Progress Payments

§ 9.6.1 After the Architect has issued a Certificate for Payment, the Owner shall make payment in the manner and within the time provided in the Contract Documents, and shall so notify the Architect.

§ 9.6.2 The Contractor shall pay each Subcontractor, no later than seven days after receipt of payment from the Owner, the amount to which the Subcontractor is entitled, reflecting percentages actually retained from payments to the Contractor on account of the Subcontractor's portion of the Work. The Contractor shall, by appropriate agreement with each Subcontractor, require each Subcontractor to make payments to Sub-subcontractors in a similar manner.

§ 9.6.3 The Architect will, on request, furnish to a Subcontractor, if practicable, information regarding percentages of completion or amounts applied for by the Contractor and action taken thereon by the Architect and Owner on account of portions of the Work done by such Subcontractor.

§ 9.6.4 The Owner has the right to request written evidence from the Contractor that the Contractor has properly paid Subcontractors and suppliers amounts paid by the Owner to the Contractor for subcontracted Work. If the Contractor fails to furnish such evidence within seven days, the Owner shall have the right to contact Subcontractors and suppliers to ascertain whether they have been properly paid. Neither the Owner nor Architect shall have an obligation to pay, or to see to the payment of money to, a Subcontractor or supplier, except as may otherwise be required by law.

§ 9.6.5 The Contractor's payments to suppliers shall be treated in a manner similar to that provided in Sections 9.6.2, 9.6.3 and 9.6.4.

§ 9.6.6 A Certificate for Payment, a progress payment, or partial or entire use or occupancy of the Project by the Owner shall not constitute acceptance of Work not in accordance with the Contract Documents.

§ 9.6.7 Whether or not the Contractor provides the Owner with a payment bond in the full penal sum of the Contract Sum, payments received by the Contractor for Work properly performed by Subcontractors or provided by suppliers shall be held by the Contractor for those Subcontractors or suppliers who performed Work or furnished materials, or both, under contract with the Contractor for which payment was made by the Owner. Nothing contained herein shall require money to be placed in a separate account and not commingled with money of the Contractor, create any fiduciary liability or tort liability on the part of the Contractor for breach of trust, or entitle any person or entity to an award of punitive damages against the Contractor for breach of the requirements of this provision.

§ 9.6.8 Provided the Owner has fulfilled its payment obligations under the Contract Documents, the Contractor shall defend and indemnify the Owner from all loss, liability, damage or expense, including reasonable attorney's fees and litigation expenses, arising out of any lien claim or other claim for payment by any Subcontractor or supplier of any tier. Upon receipt of notice of a lien claim or other claim for payment, the Owner shall notify the Contractor. If approved by the applicable court, when required, the Contractor may substitute a surety bond for the property against which the lien or other claim for payment has been asserted.

§ 9.7 Failure of Payment

If the Architect does not issue a Certificate for Payment, through no fault of the Contractor, within seven days after receipt of the Contractor's Application for Payment, or if the Owner does not pay the Contractor within seven days after the date established in the Contract Documents, the amount certified by the Architect, then the Contractor may, upon seven additional days' notice to the Owner and Architect, stop the Work until payment of the amount owing has been received. The Contract Time shall be extended appropriately and the Contract Sum shall be increased by the amount of the Contractor's reasonable costs of shutdown, delay and start-up, plus interest as provided for in the Contract Documents.

§ 9.8 Substantial Completion

§ 9.8.1 Substantial completion for purposes of this Contract occurs only upon Contractor's compliance with the following conditions precedent: (a) the Contractor furnishes to the Architect all close-out documents required by the Contract Documents in a form satisfactory to the Architect and the Owner, (b) the Contractor furnishes the manufacturers' certifications and/or warranties required by the Contract Documents; (c) the Contractor furnishes the Guarantee of Work set forth herein below; and (d) the Architect certifies that the Work is sufficiently complete in accordance with the Contract Documents so that the Owner can occupy or utilize the Work for its intended purpose.

The Guarantee of Work shall be submitted as a separate document signed by Contractor and Contractor's Surety and shall state the following:

Contractor and Contractor's Surety hereby guarantee that all Work performed on the Project is free from defective and/or nonconforming materials and workmanship and that for a period of one year from the date of substantial completion or such longer period of time as may be called for in the Contract Documents for such portions of the Work, Contractor or its Surety will repair and/or replace any defective and/or nonconforming materials and workmanship in accordance with the requirements of the Contract Documents

§ 9.8.2 When the Contractor considers that the Work, or a portion thereof which the Owner agrees to accept separately, is substantially complete, the Contractor shall prepare and submit to the Architect a comprehensive list of items to be completed or corrected prior to final payment. Failure to include an item on such list does not alter the responsibility of the Contractor to complete all Work in accordance with the Contract Documents.

§ 9.8.2.1 The Contractor shall be responsible for the costs of inspections made by the Architect including any and all other related expenses incurred by the Architect for providing services for the Project required by failure of the Contractor to achieve final acceptance / completion of the Project within 30 days after the first occurrence of the below described events:

1. Specified date of Substantial Completion; or

2. Actual date of Substantial Completion.

The costs of the Architect's additional services shall be deducted by the Owner from the Contractor's final application for payment to pay the Architect for additional services required by the Contractor's failure to achieve final completion of the project within the 30 day period described above.

§ 9.8.3 Upon receipt of the Contractor's list, the Architect will make an inspection to determine whether the Work or designated portion thereof is substantially complete. If the Architect's inspection discloses any item, whether or not included on the Contractor's list, which is not sufficiently complete in accordance with the Contract Documents so that the Owner can occupy or utilize the Work or designated portion thereof for its intended use, the Contractor shall, before issuance of the Certificate of Substantial Completion, complete or correct such item upon notification by the Architect. In such case, the Contractor shall then submit a request for another inspection by the Architect to determine Substantial Completion.

§ 9.8.4 When the Work or designated portion thereof is substantially complete, the Architect will prepare a Certificate of Substantial Completion that shall establish the date of Substantial Completion; establish responsibilities of the Owner and Contractor for security, maintenance, heat, utilities, damage to the Work and insurance; and fix the time within which the Contractor shall finish all items on the list accompanying the Certificate. Warranties required by the Contract Documents shall commence and continue for one (1) year from the date of Substantial Completion except that the roof system shall be warranted for a period of three (3) years from the date of Substantial Completion.

§ 9.8.5 The Certificate of Substantial Completion shall be submitted to the Owner and Contractor for their written acceptance of responsibilities assigned to them in the Certificate. Upon such acceptance, and consent of surety if any, the Owner shall make payment of retainage applying to the Work or designated portion thereof. Such payment shall be adjusted for Work that is incomplete or not in accordance with the requirements of the Contract Documents. Contractor's execution of the Certificate of Substantial Completion constitutes Contractor's representation that the items on the list accompanying the Certificate can and will be completed by Contractor and his subcontractors within thirty (30) days of Contractor's execution of the Certificate. Based upon this representation by Contractor and upon the acknowledgment of the Architect that the listed items remaining can be completed within thirty (30) days, the Owner agrees to execute the Certificate of Substantial Completion. If Contractor fails to complete the items on the list within thirty (30) days of Contractor's execution of the Certificate, then the Owner, at its option and without prejudice to any other rights or remedies it may have under this Contract or otherwise and without notice to Contractor or Surety, may proceed to have same completed and to deduct the reasonable costs thereof from the amounts then due or thereafter to become due to Contractor.

§ 9.8.6 The costs of inspections made by Architect which are not required by Articles 4, 9.8 or 9.10 of the General Conditions and any other inspection required by Article 12 other than the year-end inspection itself, will be the responsibility of the Contractor and will be deducted by the Owner from the Application for Payment submitted after the Owner's receipt of the Architect's statement for its costs of additional inspections. These costs are not the result of Contractor's failure to and timely complete the Contract within the specified time and, therefore, such costs are in addition to and not a part of any liquidated damages calculation, if any

§ 9.8.7 Upon the Owner's acceptance of the Work as substantially complete and upon Contractor's compliance with all conditions precedent to substantial completion as set forth in the Specifications, Article 9.8.1 and upon application by the Contractor, the Owner will pay to the Contractor all retainage held by the Owner less an amount equal to the greater of (a) two percent (2%) of the Contract Sum, or (b) two hundred percent (200%) of the estimated cost of the Work remaining to be performed by the Contractor in accordance with the Architect's determination. Final payment, including all retainage, shall be made at the time and in the manner provided for final payment in accordance with the provisions of Article 9.10 and the additional conditions precedent to final acceptance / payment set forth in the Specifications.

§ 9.9 Partial Occupancy or Use

§ 9.9.1 The Owner may occupy or use any completed or partially completed portion of the Work at any stage when such portion is designated by separate agreement with the Contractor, provided such occupancy or use is consented to by the insurer and authorized by public authorities having jurisdiction over the Project. Such partial occupancy or use may commence whether or not the portion is substantially complete, provided the Owner and Contractor have accepted in writing the responsibilities assigned to each of them for payments, retainage, if any, security,

maintenance, heat, utilities, damage to the Work and insurance, and have agreed in writing concerning the period for correction of the Work and commencement of warranties required by the Contract Documents. When the Contractor considers a portion substantially complete, the Contractor shall prepare and submit a list to the Architect as provided under Section 9.8.2. Consent of the Contractor to partial occupancy or use shall not be unreasonably withheld. The stage of the progress of the Work shall be determined by written agreement between the Owner and Contractor or, if no agreement is reached, by decision of the Architect.

§ 9.9.2 The Owner's occupancy or use of any completed or partially completed portions of the Work shall not affect Contractor's obligation to complete incomplete items on the list attached to the Certificate of Substantial Completion within the time fixed in the Certificate and does not waive Owner's right to obtain completion of incomplete items at Contractor's expense upon Contractor's failure to timely complete same. Immediately prior to such partial occupancy or use, the Owner, Contractor, and Architect shall jointly inspect the area to be occupied or portion of the Work to be used in order to determine and record the condition of the Work.

§ 9.9.3 Unless otherwise agreed upon, partial occupancy or use of a portion or portions of the Work shall not constitute acceptance of Work not complying with the requirements of the Contract Documents.

§ 9.10 Final Completion and Final Payment

§ 9.10.1 Upon receipt of the Contractor's notice that the Work is ready for final inspection and acceptance and upon receipt of a final Application for Payment, the Architect will promptly make such inspection. When the Architect finds the Work acceptable under the Contract Documents and the Contract fully performed, the Architect will promptly issue a final Certificate for Payment stating that to the best of the Architect's knowledge, information and belief, and on the basis of the Architect's on-site visits and inspections, the Work has been completed in accordance with the Contract Documents and that the entire balance found to be due the Contractor and noted in the final Certificate is due and payable. The Architect's final Certificate for Payment will constitute a further representation that conditions listed in Section 9.10.2 as precedent to the Contractor's being entitled to final payment have been fulfilled.

Final acceptance/completion under occurs only upon Contractor's compliance with the following conditions precedent: (a) the Contractor furnishes the Architect all required close-out documents in a form satisfactory to Architect and Owner; (b) Contractor furnishes the required manufacturer's certifications; (c) Contractor furnishes the signed Guarantee of Work required by the Specifications; and (d) Architect certifies final acceptance/completion through issuance of a "Certificate of Final Completion"

§ 9.10.2 Neither final payment nor any remaining retained percentage shall become due until the Contractor submits to the Architect (1) an affidavit that payrolls, bills for materials and equipment, and other indebtedness connected with the Work for which the Owner or the Owner's property might be responsible or encumbered (less amounts withheld by Owner) have been paid or otherwise satisfied, (2) a certificate evidencing that insurance required by the Contract Documents to remain in force after final payment is currently in effect, (3) a written statement that the Contractor knows of no reason that the insurance will not be renewable to cover the period required by the Contract Documents, (4) consent of surety, if any, to final payment, (5) documentation of any special warranties, such as manufacturers' warranties or specific Subcontractor warranties, and (6) if required by the Owner, other data establishing payment or satisfaction of obligations, such as receipts and releases and waivers of liens, claims, security interests, or encumbrances arising out of the Contract, to the extent and in such form as may be designated by the Owner. If a Subcontractor refuses to furnish a release or waiver required by the Owner, the Contractor may furnish a bond satisfactory to the Owner to indemnify the Owner against such lien, claim, security interest, or encumbrance. If a lien, claim, security interest, or encumbrance remains unsatisfied after payments are made, the Contractor shall refund to the Owner all money that the Owner may be compelled to pay in discharging the lien, claim, security interest, or encumbrance, including all costs and reasonable attorneys' fees.

§ 9.10.3 If, after Substantial Completion of the Work, final completion thereof is materially delayed through no fault of the Contractor or by issuance of Change Orders affecting final completion, and the Architect so confirms, the Owner shall, upon application by the Contractor and certification by the Architect, and without terminating the Contract, make payment of the balance due for that portion of the Work fully completed, corrected, and accepted. If the remaining balance for Work not fully completed or corrected is less than retainage stipulated in the Contract Documents, and if bonds have been furnished, the written consent of the surety to payment of the balance due for that portion of the Work fully completed and accepted shall be submitted by the Contractor to the Architect prior to

certification of such payment. Such payment shall be made under terms and conditions governing final payment, except that it shall not constitute a waiver of Claims.

§ 9.10.4 The making of final payment shall constitute a waiver of Claims by the Owner except those arising from

- .1 liens, Claims, security interests, or encumbrances arising out of the Contract and unsettled;
- .2 failure of the Work to comply with the requirements of the Contract Documents;
- .3 terms of special warranties required by the Contract Documents; or
- .4 audits performed by the Owner, if permitted by the Contract Documents, after final payment.

§ 9.10.5 Acceptance of final payment by the Contractor, a Subcontractor, or a supplier, shall constitute a waiver of claims by that payee except those previously made in writing and identified by that payee as unsettled at the time of final Application for Payment.

ARTICLE 10 PROTECTION OF PERSONS AND PROPERTY

§ 10.1 Safety Precautions and Programs

The Contractor shall be responsible for initiating, maintaining, and supervising all safety precautions and programs in connection with the performance of the Contract. The Architect shall not administer the Contractor's performance of its duties and responsibilities under Article 10 (including Articles 10.1 through 10.6) because the initiation, maintenance and supervision of safety precautions and programs is the sole responsibility of the Contractor as means, methods, techniques, sequences, and procedures of construction and, therefore, is not part of the Contractor's scope of Work which is to be administered by the Architect.

§ 10.2 Safety of Persons and Property

§ 10.2.1 The Contractor shall take reasonable precautions for safety of, and shall provide reasonable protection to prevent damage, injury, or loss to

- .1 employees on the Work and other persons who may be affected thereby;
- .2 the Work and materials and equipment to be incorporated therein, whether in storage on or off the site, under care, custody, or control of the Contractor, a Subcontractor, or a Sub-subcontractor; and
- .3 other property at the site or adjacent thereto, such as trees, shrubs, lawns, walks, pavements, roadways, structures, and utilities not designated for removal, relocation, or replacement in the course of construction.

§ 10.2.2 The Contractor shall comply with, and give notices required by applicable laws, statutes, ordinances, codes, rules and regulations, and lawful orders of public authorities, bearing on safety of persons or property or their protection from damage, injury, or loss.

§ 10.2.3 The Contractor shall implement, erect, and maintain, as required by existing conditions and performance of the Contract, reasonable safeguards for safety and protection, including posting danger signs and other warnings against hazards; promulgating safety regulations; and notifying the owners and users of adjacent sites and utilities of the safeguards.

§ 10.2.4 When use or storage of explosives or other hazardous materials or equipment, or unusual methods are necessary for execution of the Work, the Contractor shall (a) give Owner prior written notice and (b) exercise utmost care and carry on such activities under supervision of properly qualified personnel.

§ 10.2.5 The Contractor shall promptly remedy damage and loss (other than damage or loss insured under property insurance required by the Contract Documents) to property referred to in Sections 10.2.1.2 and 10.2.1.3 caused in whole or in part by the Contractor, a Subcontractor, a Sub-subcontractor, or anyone directly or indirectly employed by any of them, or by anyone for whose acts they may be liable and for which the Contractor is responsible under Sections 10.2.1.2 and 10.2.1.3. The Contractor may make a Claim for the cost to remedy the damage or loss to the extent such damage or loss is attributable to acts or omissions of the Owner or Architect or anyone directly or indirectly employed by either of them, or by anyone for whose acts either of them may be liable, and not attributable to the fault or negligence of the Contractor. The foregoing obligations of the Contractor are in addition to the Contractor's obligations under Section 3.18.

§ 10.2.6 The Contractor shall designate a responsible member of the Contractor's organization at the site whose duty shall be the prevention of accidents. This person shall be the Contractor's superintendent unless otherwise designated by the Contractor in writing to the Owner and Architect.

§ 10.2.7 The Contractor shall not permit any part of the construction or site to be loaded so as to cause damage or create an unsafe condition.

§ 10.2.8 Injury or Damage to Person or Property

If either party suffers injury or damage to person or property because of an act or omission of the other party, or of others for whose acts such party is legally responsible, notice of the injury or damage, whether or not insured, shall be given to the other party within a reasonable time not exceeding 21 days after discovery. The notice shall provide sufficient detail to enable the other party to investigate the matter.

§ 10.3 Hazardous Materials and Substances

§ 10.3.1 The Contractor is responsible for compliance with any requirements included in the Contract Documents regarding hazardous materials or substances. If the Contractor encounters a hazardous material or substance not addressed in the Contract Documents and if reasonable precautions will be inadequate to prevent foreseeable bodily injury or death to persons resulting from a material or substance, including but not limited to asbestos or polychlorinated biphenyl (PCB), encountered on the site by the Contractor, the Contractor shall, upon recognizing the condition, immediately stop Work in the affected area and notify the Owner and Architect of the condition.

§ 10.3.2 Upon receipt of the Contractor's notice, the Owner shall obtain the services of a licensed laboratory to verify the presence or absence of the material or substance reported by the Contractor and, in the event such material or substance is found to be present, to cause it to be rendered harmless. Unless otherwise required by the Contract Documents, the Owner shall furnish in writing to the Contractor and Architect the names and qualifications of persons or entities who are to perform tests verifying the presence or absence of the material or substance or who are to perform the task of removal or safe containment of the material or substance. The Contractor and the Architect will promptly reply to the Owner in writing stating whether or not either has reasonable objection to the persons or entities proposed by the Owner. If either the Contractor or Architect has an objection to a person or entity proposed by the Owner, the Owner shall propose another to whom the Contractor and the Architect have no reasonable objection. When the material or substance has been rendered harmless, Work in the affected area shall resume upon written agreement of the Owner and Contractor. By Change Order, the Contract Time shall be extended appropriately and the Contract Sum shall be increased by the amount of the Contractor's reasonable additional costs of shutdown, delay, and start-up.

§ 10.3.3 Intentionally omitted.

§ 10.3.4 The Owner shall not be responsible under this Section 10.3 for hazardous materials or substances the Contractor brings to the site unless such materials or substances are required by the Contract Documents. The Owner shall be responsible for hazardous materials or substances required by the Contract Documents, except to the extent of the Contractor's fault or negligence in the use and handling of such materials or substances.

§ 10.3.5 The Contractor shall reimburse the Owner for the cost and expense the Owner incurs (1) for remediation of hazardous materials or substances the Contractor brings to the site and negligently handles, or (2) where the Contractor fails to perform its obligations under Section 10.3.1, except to the extent that the cost and expense are due to the Owner's fault or negligence.

§ 10.3.6 If, without negligence on the part of the Contractor, the Contractor is held liable by a government agency for the cost of remediation of a hazardous material or substance solely by reason of performing Work as required by the Contract Documents, the Owner shall reimburse the Contractor for all cost and expense thereby incurred.

§ 10.4 Emergencies

In an emergency affecting safety of persons or property, the Contractor shall act, at the Contractor's discretion, to prevent threatened damage, injury, or loss. Additional compensation or extension of time claimed by the Contractor on account of an emergency shall be determined as provided in Article 15 and Article 7.

ARTICLE 11 INSURANCE AND BONDS

§ 11.1 Contractor's Insurance and Bonds

§ 11.1.1 The Contractor shall purchase and maintain insurance of the types and limits of liability, containing the endorsements, and subject to the terms and conditions, as described in the Agreement or elsewhere in the Contract Documents. The Contractor shall purchase and maintain the required insurance from an insurance company or

insurance companies lawfully authorized to issue insurance in the jurisdiction where the Project is located. The Owner, Architect, and Architect's consultants shall be named as additional insureds under the Contractor's commercial general liability policy or as otherwise described in the Contract Documents.

§ 11.1.2 The Contractor shall provide surety bonds of the types, for such penal sums, and subject to such terms and conditions as required by the Contract Documents. The Contractor shall purchase and maintain the required bonds from a company or companies lawfully authorized to issue surety bonds in the jurisdiction where the Project is located.

§ 11.1.3 Upon the request of any person or entity appearing to be a potential beneficiary of bonds covering payment of obligations arising under the Contract, the Contractor shall promptly furnish a copy of the bonds or shall authorize a copy to be furnished.

§ 11.1.4 Notice of Cancellation or Expiration of Contractor's Required Insurance. Within three (3) business days of the date the Contractor becomes aware of an impending or actual cancellation or expiration of any insurance required by the Contract Documents, the Contractor shall provide notice to the Owner of such impending or actual cancellation or expiration. Upon receipt of notice from the Contractor, the Owner shall, unless the lapse in coverage arises from an act or omission of the Owner, have the right to stop the Work until the lapse in coverage has been cured by the procurement of replacement coverage by the Contractor. The furnishing of notice by the Contractor shall not relieve the Contractor of any contractual obligation to provide any required coverage.

§ 11.1.5 All insurance coverage procured by the Contractor shall be provided by insurance companies having policy holder ratings no lower than "A" and financial ratings not lower than "XII" in the *Best's Insurance Guide*, latest edition in effect as of the date of the Contract, and subsequently in effect at the time of renewal of any policies required by the Contract Documents.

§ 11.2 Owner's Insurance

§ 11.2.1 The Owner shall purchase and maintain insurance of the types and limits of liability, containing the endorsements, and subject to the terms and conditions, as described in the Agreement or elsewhere in the Contract Documents. The Owner shall purchase and maintain the required insurance from an insurance company or insurance companies lawfully authorized to issue insurance in the jurisdiction where the Project is located.

§ 11.2.2 Failure to Purchase Required Property Insurance. If the Owner fails to purchase and maintain the required property insurance, with all of the coverages and in the amounts described in the Agreement or elsewhere in the Contract Documents, the Owner shall inform the Contractor in writing prior to commencement of the Work. Upon receipt of notice from the Owner, the Contractor may delay commencement of the Work and may obtain insurance that will protect the interests of the Contractor, Subcontractors, and Sub-Subcontractors in the Work. When the failure to provide coverage has been cured or resolved, the Contract Sum and Contract Time shall be equitably adjusted. In the event the Owner fails to procure coverage, the Owner waives all rights against the Contractor, Subcontractors, and Sub-subcontractors to the extent the loss to the Owner would have been covered by the insurance to have been procured by the Owner. The cost of the insurance shall be charged to the Owner by a Change Order. If the Owner does not provide written notice, and the Contractor is damaged by the failure or neglect of the Owner to purchase or maintain the required insurance, the Owner shall reimburse the Contractor for all reasonable costs and damages attributable thereto.

§ 11.2.3 Notice of Cancellation or Expiration of Owner's Required Property Insurance. Within three (3) business days of the date the Owner becomes aware of an impending or actual cancellation or expiration of any property insurance required by the Contract Documents, the Owner shall provide notice to the Contractor of such impending or actual cancellation or expiration. Unless the lapse in coverage arises from an act or omission of the Contractor: (1) the Contractor, upon receipt of notice from the Owner, shall have the right to stop the Work until the lapse in coverage has been cured by the procurement of replacement coverage by either the Owner or the Contractor; (2) the Contract Time and Contract Sum shall be equitably adjusted; and (3) the Owner waives all rights against the Contractor, Subcontractors, and Sub-subcontractors to the extent any loss to the Owner would have been covered by the insurance had it not expired or been cancelled. If the Contractor purchases replacement coverage, the cost of the insurance shall be charged to the Owner by an appropriate Change Order. The furnishing of notice by the Owner shall not relieve the Owner of any contractual obligation to provide required insurance.

§ 11.3 Waivers of Subrogation

§ 11.3.1 The Owner and Contractor waive all rights against (1) each other and any of their subcontractors, sub-subcontractors, agents, and employees, each of the other; (2) the Architect and Architect's consultants; and (3) Separate Contractors, if any, and any of their subcontractors, sub-subcontractors, agents, and employees, for damages caused by fire, or other causes of loss, to the extent those losses are covered by property insurance required by the Agreement or other property insurance applicable to the Project, except such rights as they have to proceeds of such insurance. The Owner or Contractor, as appropriate, shall require similar written waivers in favor of the individuals and entities identified above from the Architect, Architect's consultants, Separate Contractors, subcontractors, and sub-subcontractors. The policies of insurance purchased and maintained by each person or entity agreeing to waive claims pursuant to this section 11.3.1 shall not prohibit this waiver of subrogation. This waiver of subrogation shall be effective as to a person or entity (1) even though that person or entity would otherwise have a duty of indemnification, contractual or otherwise, (2) even though that person or entity did not pay the insurance premium directly or indirectly, or (3) whether or not the person or entity had an insurable interest in the damaged property.

§ 11.3.2 If during the Project construction period the Owner insures properties, real or personal or both, at or adjacent to the site by property insurance under policies separate from those insuring the Project, or if after final payment property insurance is to be provided on the completed Project through a policy or policies other than those insuring the Project during the construction period, to the extent permissible by such policies, the Owner waives all rights in accordance with the terms of Section 11.3.1 for damages caused by fire or other causes of loss covered by this separate property insurance.

§ 11.4 Intentionally Deleted

§ 11.5 Adjustment and Settlement of Insured Loss

§ 11.5.1 A loss insured under the property insurance required by the Agreement shall be adjusted by the Owner in good faith and made payable to the Owner in good faith for the insureds, as their interests may appear, subject to requirements of any applicable mortgagee clause and of Section 11.5.2. The Owner shall pay the Architect and Contractor their just shares of insurance proceeds received by the Owner, and by appropriate agreements the Architect and Contractor shall make payments to their consultants and Subcontractors in similar manner.

§ 11.5.2 Prior to settlement of an insured loss, the Owner shall notify the Contractor of the terms of the proposed settlement as well as the proposed allocation of the insurance proceeds. The Contractor shall have 14 days from receipt of notice to object to the proposed settlement or allocation of the proceeds. If the Contractor does not object, the Owner shall settle the loss and the Contractor shall be bound by the settlement and allocation. Upon receipt, the Owner shall deposit the insurance proceeds in a separate account and make the appropriate distributions. Thereafter, if no other agreement is made or the Owner does not terminate the Contract for convenience, the Owner and Contractor shall execute a Change Order for reconstruction of the damaged or destroyed Work in the amount allocated for that purpose. If the Contractor timely objects to either the terms of the proposed settlement or the allocation of the proceeds, the Owner may proceed to settle the insured loss, and any dispute between the Owner and Contractor arising out of the settlement or allocation of the proceeds shall be resolved pursuant to Article 15. Pending resolution of any dispute, the Owner may issue a Construction Change Directive for the reconstruction of the damaged or destroyed Work.

ARTICLE 12 UNCOVERING AND CORRECTION OF WORK

§ 12.1 Uncovering of Work

§ 12.1.1 If a portion of the Work is covered contrary to the Architect's request or to requirements specifically expressed in the Contract Documents, it must, if requested in writing by the Architect, be uncovered for the Architect's examination and be replaced at the Contractor's expense without change in the Contract Time.

§ 12.1.2 If a portion of the Work has been covered that the Architect has not specifically requested to examine prior to its being covered, the Architect may request to see such Work and it shall be uncovered by the Contractor. If such Work is in accordance with the Contract Documents, costs of uncovering and replacement shall, by appropriate Change Order, be at the Owner's expense.

§ 12.2 Correction of Work

§ 12.2.1 Before Substantial Completion

The Contractor shall promptly correct Work rejected by the Architect or failing to conform to the requirements of the Contract Documents, discovered before Substantial Completion and whether or not fabricated, installed or completed. Costs of correcting such rejected Work, including additional testing and inspections, the cost of uncovering and replacement, and compensation for the Architect's services and expenses made necessary thereby, shall be at the Contractor's expense.

§ 12.2.2 After Substantial Completion

§ 12.2.2.1 In addition to the Contractor's obligations under Section 3.5, if, within one year after the date of Substantial Completion of the Work or designated portion thereof or after the date for commencement of warranties established under Section 9.9.1, or by terms of any applicable special warranty required by the Contract Documents, any of the Work is found to be not in accordance with the requirements of the Contract Documents, the Contractor shall correct it promptly after receipt of notice from the Owner to do so, unless the Owner has previously given the Contractor a written acceptance of such condition. The Owner shall give such notice promptly after discovery of the condition. During the one-year period for correction of Work, if the Owner fails to notify the Contractor and give the Contractor an opportunity to make the correction, the Owner waives the rights to require correction by the Contractor and to make a claim for breach of warranty. If the Contractor fails to correct nonconforming Work within a reasonable time during that period after receipt of notice from the Owner or Architect, the Owner may correct it in accordance with Section 2.5. Prior to the end of the one-year period, (three years for roof systems), the Architect may schedule a warranty inspection which shall be attended by the Architect, the Owner, the Contractor, and all major subcontractors. During this inspection, the parties shall identify all defective and/or nonconforming items and fix a time within which all defective and/or nonconforming items shall be repaired and/or replaced.

Within the one-year period (three years for roof systems) provided for in the Guarantee of Work required by Article 9.8.1, if repairs or replacement are requested by Owner in connection with the Work which, in the opinion of the Owner, are rendered necessary as a result of the use of materials, equipment or workmanship which are inferior, defective or not in accordance with the Contract Documents, the Contractor and/or its Surety shall promptly, upon receipt of notice from and without expense to the Owner, place in satisfactory condition in every particular, all such Work, correct all defects therein and make good all damages to the building, site, equipment or contents thereof; and make good any work or materials or the equipment and contents of said buildings or site disturbed in fulfilling any such guarantee. If, after notice or within the time agreed upon by the parties at the warranty inspection, the Contractor and/or its Surety fail to proceed promptly to comply with the terms of the guarantee, the Owner may have the defects corrected in accordance with Article 2.5 and the Contractor and his Surety shall be liable for all expenses incurred. All special guarantees applicable to definite parts of the Work stipulated in the Contract Documents shall be subject to the terms of this paragraph during the first year of the life of such special guarantee.

§ 12.2.2.2 The one-year period for correction of Work shall be extended with respect to portions of Work first performed after Substantial Completion by the period of time between Substantial Completion and the actual completion of that portion of the Work.

§ 12.2.2.3 The one-year period for correction of Work shall not be extended by corrective Work performed by the Contractor pursuant to this Section 12.2.

§ 12.2.3 The Contractor shall remove from the site portions of the Work that are not in accordance with the requirements of the Contract Documents and are neither corrected by the Contractor nor accepted by the Owner.

§ 12.2.4 The Contractor shall bear the cost of correcting destroyed or damaged construction of the Owner or Separate Contractors, whether completed or partially completed, caused by the Contractor's correction or removal of Work that is not in accordance with the requirements of the Contract Documents.

§ 12.2.5 Nothing contained in this Section 12.2 shall be construed to establish a period of limitation with respect to other obligations the Contractor has under the Contract Documents. Establishment of the one-year period for correction of Work as described in Section 12.2.2 relates only to the specific obligation of the Contractor to correct the Work, and has no relationship to the time within which the obligation to comply with the Contract Documents may be sought to be enforced, nor to the time within which proceedings may be commenced to establish the Contractor's liability with respect to the Contractor's obligations other than specifically to correct the Work.

§ 12.3 Acceptance of Nonconforming Work

If the Owner prefers to accept Work that is not in accordance with the requirements of the Contract Documents, the Owner may do so instead of requiring its removal and correction, in which case the Contract Sum will be reduced as appropriate and equitable. Such adjustment shall be effected whether or not final payment has been made.

ARTICLE 13 MISCELLANEOUS PROVISIONS

§ 13.1 Governing Law

The Contract shall be governed by Mississippi law.

§ 13.2 Successors and Assigns

§ 13.2.1 The Owner and Contractor respectively bind themselves, their partners, successors, assigns, and legal representatives to covenants, agreements, and obligations contained in the Contract Documents. Except as provided in Section 13.2.2, neither party to the Contract shall assign the Contract as a whole without written consent of the other. If either party attempts to make an assignment without such consent, that party shall nevertheless remain legally responsible for all obligations under the Contract.

§ 13.2.2 The Owner may, without consent of the Contractor, assign the Contract to a lender providing construction financing for the Project, if the lender assumes the Owner's rights and obligations under the Contract Documents. The Contractor shall execute all consents reasonably required to facilitate the assignment.

§ 13.3 Rights and Remedies

§ 13.3.1 Duties and obligations imposed by the Contract Documents and rights and remedies available thereunder shall be in addition to and not a limitation of duties, obligations, rights, and remedies otherwise imposed or available by law.

§ 13.3.2 No action or failure to act by the Owner, Architect, or Contractor shall constitute a waiver of a right or duty afforded them under the Contract, nor shall such action or failure to act constitute approval of or acquiescence in a breach thereunder, except as may be specifically agreed upon in writing.

§ 13.4 Tests and Inspections

§ 13.4.1 Tests, inspections, and approvals of portions of the Work shall be made as required by the Contract Documents and by applicable laws, statutes, ordinances, codes, rules, and regulations or lawful orders of public authorities. Unless otherwise provided, the Contractor shall make arrangements for such tests, inspections, and approvals with an independent testing laboratory or entity acceptable to the Owner, or with the appropriate public authority, and shall bear all related costs of tests, inspections, and approvals. The Contractor shall give the Architect timely notice of when and where tests and inspections are to be made so that the Architect may be present for such procedures.

§ 13.4.2 If the Architect, Owner, or public authorities having jurisdiction determine that portions of the Work require additional testing, inspection, or approval not included under Section 13.4.1, the Architect will, upon written authorization from the Owner, instruct the Contractor to make arrangements for such additional testing, inspection, or approval, by an entity acceptable to the Owner, and the Contractor shall give timely notice to the Architect of when and where tests and inspections are to be made so that the Architect may be present for such procedures. Such costs, except as provided in Section 13.4.3, shall be at the Owner's expense.

§ 13.4.3 If procedures for testing, inspection, or approval under Sections 13.4.1 and 13.4.2 reveal failure of the portions of the Work to comply with requirements established by the Contract Documents, all costs made necessary by such failure, including those of repeated procedures and compensation for the Architect's services and expenses, shall be at the Contractor's expense.

§ 13.4.4 Required certificates of testing, inspection, or approval shall, unless otherwise required by the Contract Documents, be secured by the Contractor and promptly delivered to the Architect.

§ 13.4.5 If the Architect is to observe tests, inspections, or approvals required by the Contract Documents, the Architect will do so promptly and, where practicable, at the normal place of testing.

§ 13.4.6 Tests or inspections conducted pursuant to the Contract Documents shall be made promptly to avoid unreasonable delay in the Work.

§ 13.5 Interest

Payments due and unpaid under the Contract Documents shall bear interest as provided by applicable Mississippi law or as required by the Owner in the Contract

§ 13.6 COUNTERPARTS.

The Agreement may be executed in any number of counterparts, all of which, when taken together, shall constitute one and the same instrument, and any of the parties hereto may execute the Agreement by signing any such counterpart.

ARTICLE 14 TERMINATION OR SUSPENSION OF THE CONTRACT

§ 14.1 Termination by the Contractor

§ 14.1.1 The Contractor may terminate the Contract if the Work is stopped for a period of 60 consecutive days through no act or fault of the Contractor, a Subcontractor, a Sub-subcontractor, their agents or employees, or any other persons or entities performing portions of the Work, for any of the following reasons:

- .1 Issuance of an order of a court or other public authority having jurisdiction that requires all Work to be stopped;
- .2 An act of government, such as a declaration of national emergency, that requires all Work to be stopped;
- .3 Because the Architect has not issued a Certificate for Payment and has not notified the Contractor of the reason for withholding certification as provided in Section 9.4.1, or because the Owner has not made payment on a Certificate for Payment within the time stated in the Contract

Documents unless such non-payment is

the subject of

a good faith dispute between Owner and Contractor.

§ 14.2 Termination by the Owner for Cause

§ 14.2.1 The Owner may terminate the Contract if the Contractor

- .1 refuses or fails to supply enough properly skilled workers or proper materials;
- .2 fails to make payment to Subcontractors or suppliers in accordance with the respective agreements between the Contractor and the Subcontractors or Suppliers;
- .3 disregards applicable laws, statutes, ordinances, codes, rules and regulations, or lawful orders of a public authority; or
- .4 otherwise is guilty of substantial breach of a provision of the Contract Documents.
- .5 fails to achieve Substantial Completion of the Project within the time stated and as described in Article 9.8.5 and in the Specifications; or
- .6 fails to meet any deadline required by the Contract. Contractor acknowledges that time is of the essence of this Contract and that all deadlines required by the Contract are critical to timely completion of the Contract. Therefore, Contractor agrees that its failure to meet any deadline constitutes a substantial and material breach of this Contract, entitling the Owner to terminate the Contract.

§ 14.2.2 When any of the reasons described in Section 14.2.1 exist, and upon advice by the Architect that sufficient cause exists to justify such actions, the Owner may, without prejudice to any other rights or remedies of the Owner and after giving the Contractor and the Contractor's surety, if any, seven days' notice, terminate employment of the Contractor and may, subject to any prior rights of the surety:

- .1 Exclude the Contractor from the site and take possession of all materials, equipment, tools, and construction equipment and machinery thereon owned by the Contractor;
- .2 Accept assignment of subcontracts pursuant to Section 5.4; and
- .3 Finish the Work by whatever reasonable method the Owner may deem expedient. Upon written request of the Contractor, the Owner shall furnish to the Contractor a detailed accounting of the costs incurred by the Owner in finishing the Work.

§ 14.2.3 When the Owner terminates the Contract for one of the reasons stated in Section 14.2.1, the Contractor shall not be entitled to receive further payment until the Work is finished.

§ 14.2.4 If the unpaid balance of the Contract Sum exceeds costs of finishing the Work, including compensation for the Architect's services and expenses made necessary thereby, and other damages incurred by the Owner and not expressly waived, such excess shall be paid to the Contractor. If such costs and damages exceed the unpaid balance, the Contractor shall pay the difference to the Owner. The amount to be paid to the Contractor or Owner, as the case may be, shall be certified by the Architect, upon application, and this obligation for payment shall survive termination of the Contract.

§ 14.2.5 If the Owner terminates the Contract for cause, and it is determined for any reason that the Contractor was not actually in default under the Contract at the time of termination, the Contractor shall be entitled to recover from the Owner the same amount as the Contractor would be entitled to receive under a termination for convenience as provided by Article 14.4. The foregoing shall constitute the Contractor's sole and exclusive remedy for termination of the Contract. In no event shall the Contractor be entitled to special, consequential, or exemplary damages, nor shall the Contractor be entitled to anticipated profits resulting from termination of this Contract.

§ 14.3 Suspension by the Owner for Convenience

§ 14.3.1 The Owner may, without cause, order the Contractor in writing to suspend, delay or interrupt the Work, in whole or in part for such period of time as the Owner may determine.

§ 14.3.2 The Contract Sum and Contract Time shall be adjusted for increases in the cost and time caused by suspension, delay, or interruption under Section 14.3.1. Adjustment of the Contract Sum shall include profit. No adjustment shall be made to the extent

- .1 that performance is, was, or would have been, so suspended, delayed, or interrupted, by another cause for which the Contractor is responsible; or
- .2 that an equitable adjustment is made or denied under another provision of the Contract.

§ 14.4 Termination by the Owner for Convenience

§ 14.4.1 The Owner may, at any time, terminate the Contract for the Owner's convenience and without cause.

§ 14.4.2 Upon receipt of notice from the Owner of such termination for the Owner's convenience, the Contractor shall

- .1 cease operations as directed by the Owner in the notice;
- .2 take actions necessary, or that the Owner may direct, for the protection and preservation of the Work; and
- .3 except for Work directed to be performed prior to the effective date of termination stated in the notice, terminate all existing subcontracts and purchase orders and enter into no further subcontracts and purchase orders.

§ 14.4.3 In case of such termination for the Owner's convenience, the Owner shall pay the Contractor for Work properly executed; costs incurred by reason of the termination, including costs attributable to termination of Subcontracts; and the termination fee, if any, set forth in the Agreement. The Contractor shall not be entitled to receive any payment for either overhead or profit on work not performed.

ARTICLE 15 CLAIMS AND DISPUTES

§ 15.1 Claims

§ 15.1.1 Definition

A Claim is a demand or assertion by one of the parties seeking, as a matter of right, payment of money, a change in the Contract Time, or other relief with respect to the terms of the Contract. The term "Claim" also includes other disputes and matters in question between the Owner and Contractor arising out of or relating to the Contract. The responsibility to substantiate Claims shall rest with the party making the Claim. This Section 15.1.1 does not require the Owner to file a Claim in order to impose liquidated damages in accordance with the Contract Documents.

§ 15.1.2 Time Limits on Claims

The Owner and Contractor shall commence all Claims and causes of action against the other and arising out of or related to the Contract, whether in contract, tort, breach of warranty or otherwise, and within the period specified by

applicable law, but in any case not more than 10 years after the date of Substantial Completion of the Work. The Owner and Contractor waive all Claims and causes of action not commenced in accordance with this Section 15.1.2.

§ 15.1.3 Notice of Claims

§ 15.1.3.1 Claims by either the Owner or Contractor, where the condition giving rise to the Claim is first discovered prior to expiration of the period for correction of the Work set forth in Section 12.2.2, shall be initiated by notice to the other party and to the Initial Decision Maker with a copy sent to the Architect, if the Architect is not serving as the Initial Decision Maker. Claims by either party under this Section 15.1.3.1 shall be initiated within 21 days after occurrence of the event giving rise to such Claim or within 21 days after the claimant first recognizes the condition giving rise to the Claim, whichever is later.

§ 15.1.3.2 Claims by either the Owner or Contractor, where the condition giving rise to the Claim is first discovered after expiration of the period for correction of the Work set forth in Section 12.2.2, shall be initiated by notice to the other party. In such event, no decision by the Initial Decision Maker is required.

§ 15.1.4 Continuing Contract Performance

§ 15.1.4.1 Pending final resolution of a Claim, except as otherwise agreed in writing or as provided in Section 9.7 and Article 14, the Contractor shall proceed diligently with performance of the Contract and the Owner shall continue to make payments in accordance with the Contract Documents.

§ 15.1.4.2 The Contract Sum and Contract Time shall be adjusted in accordance with the Initial Decision Maker's decision, subject to the right of either party to proceed in accordance with this Article 15. The Architect will issue Certificates for Payment in accordance with the decision of the Initial Decision Maker.

§ 15.1.5 Claims for Additional Cost

.1 Concealed Conditions. If the Contractor encounters conditions at the site that are (1) subsurface or otherwise concealed physical conditions that differ materially from those indicated in the Contract Documents or (2) unknown physical conditions of an unusual nature, that differ materially from those ordinarily found to exist and generally recognized as inherent in construction activities of the character provided for in the Contract Documents, the Contractor shall promptly provide notice to the Owner and the Architect before conditions are disturbed and in no event later than five (5) days after first observance of the conditions. The Architect will promptly investigate such conditions and, if the Architect determines that they differ materially and cause an increase or decrease in the Contractor's cost of, or time required for, performance of any part of the Work, will recommend an equitable adjustment in the Contract Sum. Contract Time shall be addressed in accordance with Section 15.1.5 below. If the Architect determines that the conditions at the site are not materially different from those indicated in the Contract Documents and that no change in the terms of the Contract is justified, the Architect shall promptly notify the Owner and Contractor in writing, stating the reasons.

.2 Claims for Additional Cost For Reasons Other than Concealed Conditions. If the Contractor claims that it should be entitled to additional compensation for any damage sustained or may be sustained (i) by reason of any act or omission of the Owner or any other person for which the Owner is responsible or by reason that Owner directed the Contractor to perform any work which it believes is not required to be performed by the provisions of each Contract (collectively an "Event"), then Contractor shall within five (5) days after it first had notice of an Event, deliver to the Architect and Owner a written statement of the nature and basis of its claim and within twenty (20) days, the Contractor shall deliver to the Owner a verified itemized statement of the details and amount of such damage or extra work. If the Owner shall require any additional data, the Contractor shall furnish the same within three (3) days after written demand therefore. Unless such notice, statements and data shall be delivered within the times aforesaid, all claims for additional compensation or damages for such matters shall be deemed waived. Compliance by the Contractor with the provisions of this paragraph shall not, however, be deemed an admission by the Owner nor raise any presumption as to the validity or correctness of the claim. Contractor shall not be entitled to additional compensation by reason of any inconsistency or deficiency in the design documents.

.3 Change Orders and Construction Change Directives. To the extent that an Owner wishes to change the scope of Work under the Contract documents, the parties shall agree to any compensation and time as part of such agreed Change Order as provided in Article 7.2. Contractor shall not be obligated to perform any material change in the scope of Work in the absence of an executed Change Order. Neither the Owner

nor Architect shall be entitled to utilize the provisions for Construction Change Directives as provided in Article 7.3 for material changes in the scope of Work under the Contract Documents

.4 The Owner will not be responsible for damages or additional compensation due to delays in the work caused by, government delays, utility company delays, or other delays beyond the control of the Owner.

§ 15.1.6 Claims for Additional Time

§ 15.1.6.1 If the Contractor is delayed on its critical path at any time in the commencement or progress of the Work by an act or neglect of the Owner or Architect, or of an employee of either, or of a separate contractor employed by the Owner; or by changes ordered in the Work; or by labor disputes, fire, unavoidable casualties, concealed conditions, or by delay authorized by the Owner pending mediation; or by other causes that the Architect determines may justify delay, then the Contract Time shall be extended by Change Order to the extent such delay will prevent the Contractor from achieving Substantial Completion within the Contract Time as provided. The entitlement to a time extension provided in this paragraph shall not apply if the performance of the Work is not, was not, or would not have been delayed by any other cause for which the Contractor is not entitled to an extension in the Contract Time under the Contract Documents. The Contractor further acknowledges and agrees that adjustments in the Contract Time will be permitted for a delay only to the extent such delay (i) is not caused, or could not have been anticipated, by the Contractor and (ii) could not be limited or avoided by the Contractor's timely notice to the Owner of the delay or reasonable likelihood that the delay will occur for such reasonable time as the Architect may determine

§ 15.1.6.2 The Contractor assumes the risk of both normal and abnormally adverse weather and will not be entitled to any time extension or Contract price adjustment for either normal or abnormally adverse weather encountered during construction, notwithstanding any other provision of the Contract to the contrary.

§ 15.1.6.3 Claims for increase in the Contract Time shall set forth in detail the facts and circumstances which support such Claim, including but not limited to, the cause of such delay, the date such delay began to affect the critical path, the date such delay ceased to affect the critical path and the number of days of additional time requested. The Contractor shall not be entitled to an increase in the Contract Time for delays which did not affect the critical path or to the extent there were concurrent non-excusable delays. The Contractor may be requested to provide additional documentation to substantiate its Claim, including but not limited to, schedules that indicate all activities affected by such delay.

§ 15.1.7 Waiver of Claims for Consequential Damages

The Contractor and Owner waive Claims against each other for consequential damages arising out of or relating to this Contract. This mutual waiver includes

- .1 damages incurred by the Owner for rental expenses, for losses of use, income, profit, financing, business and reputation, and for loss of management or employee productivity or of the services of such persons; and
- .2 damages incurred by the Contractor for principal office expenses including the compensation of personnel stationed there, for losses of financing, loss of productivity, business and reputation, and for loss of profit, except anticipated profit arising directly from the Work.

This mutual waiver is applicable, without limitation, to all consequential damages due to either party's termination in accordance with Article 14. Nothing contained in this Section 15.1.7 shall be deemed to preclude assessment of liquidated damages, when applicable, in accordance with the requirements of the Contract Documents.

§ 15.1.8 The Contractor expressly agrees that the Article 15 Claims and Disputes process is the only dispute resolution mechanism that will be recognized by the parties for any claims put forward by the Contractor, notwithstanding any other claimed theory of entitlement on the part of the Contractor or its subcontractors or suppliers against the Owner and/or the Architect or any of their design consultants, including, but not limited to, all claims of breach of contract, breach of warranty, misrepresentation, negligence, professional negligence, and/or any other tort.

§ 15.2 Initial Decision

§ 15.2.1 Claims, excluding those where the condition giving rise to the Claim is first discovered after expiration of the period for correction of the Work set forth in Section 12.2.2 or arising under Sections 10.3, 10.4, and 11.5, shall be referred to the Initial Decision Maker for initial decision. The Architect will serve as the Initial Decision Maker,

unless otherwise indicated in the Agreement. Except for those Claims excluded by this Section 15.2.1, an initial decision shall be required as a condition precedent to mediation of any Claim. If an initial decision has not been rendered within 30 days after the Claim has been referred to the Initial Decision Maker, the party asserting the Claim may demand mediation and binding dispute resolution without a decision having been rendered. Unless the Initial Decision Maker and all affected parties agree, the Initial Decision Maker will not decide disputes between the Contractor and persons or entities other than the Owner.

§ 15.2.2 The Initial Decision Maker will review Claims and within ten days of the receipt of a Claim take one or more of the following actions: (1) request additional supporting data from the claimant or a response with supporting data from the other party, (2) reject the Claim in whole or in part, (3) approve the Claim, (4) suggest a compromise, or (5) advise the parties that the Initial Decision Maker is unable to resolve the Claim if the Initial Decision Maker lacks sufficient information to evaluate the merits of the Claim or if the Initial Decision Maker concludes that, in the Initial Decision Maker's sole discretion, it would be inappropriate for the Initial Decision Maker to resolve the Claim.

§ 15.2.3 In evaluating Claims, the Initial Decision Maker may, but shall not be obligated to, consult with or seek information from either party or from persons with special knowledge or expertise who may assist the Initial Decision Maker in rendering a decision. The Initial Decision Maker may request the Owner to authorize retention of such persons at the Owner's expense.

§ 15.2.4 If the Initial Decision Maker requests a party to provide a response to a Claim or to furnish additional supporting data, such party shall respond, within ten days after receipt of the request, and shall either (1) provide a response on the requested supporting data, (2) advise the Initial Decision Maker when the response or supporting data will be furnished, or (3) advise the Initial Decision Maker that no supporting data will be furnished. Upon receipt of the response or supporting data, if any, the Initial Decision Maker will either reject or approve the Claim in whole or in part within thirty (30) days

§ 15.2.5 The Initial Decision Maker will render an initial decision approving or rejecting the Claim, or indicating that the Initial Decision Maker is unable to resolve the Claim. This initial decision shall (1) be in writing; (2) state the reasons therefor; and (3) notify the parties and the Architect, if the Architect is not serving as the Initial Decision Maker, of any change in the Contract Sum or Contract Time or both. The initial decision shall be final and binding on the parties but subject to mediation and, if the parties fail to resolve their dispute through mediation, to binding dispute resolution.

§ 15.2.6 Either party may file for mediation of an initial decision at any time, subject to the terms of Section 15.2.6.1.

§ 15.2.6.1 Either party may, within 30 days from the date of receipt of an initial decision, demand in writing that the other party file for mediation. If such a demand is made and the party receiving the demand fails to file for mediation within 30 days after receipt thereof, then both parties waive their rights to mediate or pursue binding dispute resolution proceedings with respect to the initial decision.

§ 15.2.7 In the event of a Claim against the Contractor, the Owner may, but is not obligated to, notify the surety, if any, of the nature and amount of the Claim. If the Claim relates to a possibility of a Contractor's default, the Owner may, but is not obligated to, notify the surety and request the surety's assistance in resolving the controversy.

§ 15.2.8 If a Claim relates to or is the subject of a mechanic's lien, the party asserting such Claim may proceed in accordance with applicable law to comply with the lien notice or filing deadlines.

§ 15.3 Mediation

§ 15.3.1 Either party may file for mediation of a dispute at any time. Claims, disputes, or other matters in controversy arising out of or related to the Contract, except those waived as provided for in Sections 9.10.4, 9.10.5, and 15.1.7, shall be subject to mediation as a condition precedent to binding dispute resolution.

§ 15.3.2 The parties shall endeavor to resolve their Claims by mediation which through a mutually agreed upon mediator, unless the parties mutually are unable to agree, at which point the mediation shall be administered by the American Arbitration Association in accordance with its Construction Industry Mediation Procedures in effect on the date of the Agreement. A request for mediation shall be made in writing, delivered to the other party to the Contract, and filed with the person or entity administering the mediation. The request may be made concurrently

with the filing of binding dispute resolution proceedings but, in such event, mediation shall proceed in advance of binding dispute resolution proceedings, which shall be stayed pending mediation for a period of 60 days from the date of filing, unless stayed for a longer period by agreement of the parties or court order. If an arbitration is stayed pursuant to this Section 15.3.2, the parties may nonetheless proceed to the selection of the arbitrator(s) and agree upon a schedule for later proceedings.

§ 15.3.3 Intentionally Deleted

§ 15.3.4 The parties shall share the mediator's fee and any filing fees equally. The mediation shall be held in the place where the Project is located, unless another location is mutually agreed upon. Agreements reached in mediation shall be enforceable as settlement agreements in any court having jurisdiction thereof.

§ 15.4 Litigation. All claims or other matters in dispute which cannot be resolved by mutual agreement or Mediation shall be subject to litigation in a Court of appropriate jurisdiction. The Parties agree to that the exclusive jurisdiction and venue for any and all claims or disputes arising from or related to the Project or the Contract Documents shall be in Madison County, Mississippi. The prevailing party shall be entitled to their reasonable attorney fees and expenses incurred in any litigation of a claim or dispute relating to any Project.

CIVIL GENERAL NOTES

GENERAL NOTES:

1. THE CONTRACTOR SHALL FURNISH THE ENGINEER WITH TWO SETS OF "AS-BUILT" DRAWINGS PRIOR TO REQUESTING A FINAL INSPECTION. THE "AS-BUILT" DRAWINGS SHALL SHOW THE LOCATIONS OF ALL SEWER AND WATER STRUCTURES, LINES, BENDS, AND APPURTENANCES. GRADES ON STORM SEWER LINES SHALL ALSO BE FURNISHED ON "AS-BUILTS" DRAWINGS.
2. INSTALLATION OF ANY GRAVITY FLOW PIPE, SUCH AS SANITARY SEWER OR STORM DRAIN, SHALL REQUIRE THAT THE CONTRACTOR START AT THE LOWEST CONNECTION POINT ELEVATION, AND WORK IN THE UPHILL DIRECTION. IF, IN THE BEST INTEREST OF THE PROJECT, THE CONTRACTOR WISHES TO INITIATE PIPE LAYING AT SOME LOCATION OTHER THAN THE LOWEST CONTROL, IT SHALL BE THE CONTRACTOR'S RESPONSIBILITY TO CONFIRM A SATISFACTORY CONNECTION TO THE LOWEST CONTROL, PRIOR TO BEGINNING CONSTRUCTION AT SOME POINT OTHER THAN THE LOWEST CONTROL ELEVATION. THE CONTRACTOR SHALL REQUEST, IN WRITING, AND RECEIVE, IN WRITING, APPROVAL FROM THE DESIGN ENGINEER, WHOSE NAME APPEARS ON THESE PLANS. SANITARY SEWER MAINS OR SERVICES WITH LESS THAN THREE FEET OF COVER SHALL BE DUCTILE IRON PIPE. WHEREVER A SANITARY SEWER SERVICE CROSSES OVER OR UNDER A STORM DRAIN PIPE AND/OR A WATER MAIN, THE SERVICE SHALL BE EXTENDED A MINIMUM OF FIVE FEET BEYOND THE FURTHEST PIPELINE. IN NO CASE, WITHOUT THE ENGINEERS WRITTEN APPROVAL, SHALL THE CONTRACTOR TERMINATE THE SANITARY SEWER SERVICE AT A LOCATION THAT WOULD REQUIRE THE BUILDING PLUMBER TO INSTALL PIPE ACROSS THE STORM DRAIN PIPE AND/OR WATER MAIN.
3. CONTRACTOR SHALL PROVIDE ADEQUATE PROTECTION TO PREVENT DAMAGE TO ALL TREE ROOTS DURING ENTRENCHING AND ANY OTHER CONSTRUCTION THAT MAY ENDANGER THE HEALTH OF THE TREES.
4. UNLESS NOTED OTHERWISE, THE CONTRACTOR SHALL BE RESPONSIBLE FOR REPAIRING ANY DAMAGE DONE TO ANY EXISTING ON-SITE OR OFF-SITE ITEMS THAT WILL REMAIN IN PLACE AFTER CONSTRUCTION ACTIVITIES ARE COMPLETE. THOSE ITEMS INCLUDE, BUT ARE NOT LIMITED TO DRAINAGE SYSTEMS, UTILITIES, CURBING, PAVEMENT, LANDSCAPING, IRRIGATION SYSTEMS, FENCING, SITE STRUCTURES, RETAINING WALLS, ETC. REPAIRS SHALL BE EQUAL TO OR BETTER THAN EXISTING CONDITIONS, AND SHALL BE TO THE SATISFACTION OF THE OWNER OF THE REPAIRED ITEM. PRIOR TO MAKING ANY REPAIRS, THE CONTRACTOR SHALL SUBMIT A DETAILED REPAIR METHODOLOGY TO THE ENGINEER AND ARCHITECT. REPAIRS SHALL NOT BEGIN UNTIL APPROVAL FROM THE ENGINEER AND ARCHITECT HAS BEEN ISSUED. CONTRACTOR SHALL DOCUMENT ANY EXISTING DAMAGE WITH PHOTOS, VIDEOS, ETC., AND NOTIFY THE ARCHITECT AND ENGINEER PRIOR TO COMMENCING CONSTRUCTION IN THE AREA OF THE EXISTING DAMAGED ITEM.
5. IF THE CONTRACTOR MUST CROSS AN EXISTING ITEM (PAVEMENT, SIDEWALK, ETC.) TO INSTALL A NEW IMPROVEMENT (UTILITIES, STORM DRAINAGE, ETC.), THE CONTRACTOR SHALL INCLUDE IN HIS BASE BID, ALL COST REQUIRED TO REPLACE THE EXISTING ITEM IMPACTED BY CONSTRUCTION.

CONTRACTOR RESPONSIBILITY NOTES:

1. THE PROPOSED WORK ITEMS SHOWN ON THESE PLANS DO NOT NECESSARILY DEPICT ANY AND ALL ITEMS THAT MAY BE REQUIRED TO IMPLEMENT A FINAL BEST MANAGEMENT PRACTICES STORMWATER POLLUTION PREVENTION PLAN. THESE WORK ITEMS DO NOT RELIEVE THE CONTRACTOR OF ENSURING THAT ALL LOCAL, STATE AND FEDERAL REQUIREMENTS FOR STORM WATER POLLUTION PREVENTION, WATER QUALITY AND ILLEGAL POINT SOURCE DISCHARGE ARE STRICTLY ADHERED TO. THE CONTRACTOR SHALL BE RESPONSIBLE FOR ANY AND ALL ACTIONS THAT ARE NECESSARY TO BE IN COMPLIANCE WITH ALL OF THESE REGULATIONS. THE CONTRACTOR SHALL BEAR ALL EXPENSES RELATED TO IMPLEMENTING THESE MEASURES AND A PROPER BEST MANAGEMENT PRACTICES STORMWATER POLLUTION PREVENTION PLAN IRREGARDLESS OF WHETHER A REQUIRED FACILITY, STRUCTURE, FENCING, SEEDING, MATS, ETC. ARE SHOWN ON THESE PLANS.
2. THE CONTRACTOR SHALL BE RESPONSIBLE FOR READING AND IMPLEMENTING ALL NOTES SHOWN IN THESE PLANS. THE CONTRACTOR SHALL NOT BE RELIEVED OF ANY REQUIREMENTS SET FORTH AS PART OF NOTES SHOWN ON THIS SHEET OR ANY ADDITIONAL COSTS THAT MAY BE INCURRED FOR FAILURE TO READ SAID NOTES.

EROSION CONTROL NOTES:

1. THE CONTRACTOR SHALL EXECUTE THE SCNOI AND FOLLOW THE STORM WATER POLLUTION PREVENTION PLAN (SWPPP) INCLUDED IN THE PROJECT SPECIFICATIONS.
2. EROSION CONTROL MEASURES SHALL BE INSTALLED PROMPTLY DURING ALL CONSTRUCTION PHASES. ALL EROSION CONTROL MEASURES SHALL BE IN ACCORDANCE WITH THE MISSISSIPPI PLANNING AND DESIGN MANUAL FOR THE CONTROL OF EROSION, SEDIMENT AND STORMWATER. INSTALLATION AND MAINTENANCE OF STRUCTURAL AND VEGETATIVE PRACTICES SHALL BE PER THE MISSISSIPPI DEPARTMENT OF ENVIRONMENTAL QUALITY, FIELD MANUAL FOR EROSION AND SEDIMENT CONTROL ON CONSTRUCTION SITES IN MISSISSIPPI, SECOND EDITION 2005. IN ADDITION, CONTRACTOR SHALL COMPLY WITH ALL LOCAL, STATE AND FEDERAL REQUIREMENTS.
3. CONTRACTOR SHALL COMPLY WITH ALL MDEQ AND OWNER REQUIREMENTS. PROJECT SUPERINTENDENT AND OTHERS PERFORMING WORK RELATED TO CONSTRUCTION STORMWATER MANAGEMENT SHALL ATTEND ANY LOCAL TRAINING PERTAINING TO EROSION CONTROL IF REQUIRED BY THE OWNER.

DEMOLITION NOTES:

1. CONTRACTOR SHALL REFERENCE THE GEOTECHNICAL INVESTIGATION REPORT ATTACHED WITH THE PROJECT MANUAL AND SHALL FAMILIARIZE HIMSELF WITH ALL OBSERVATIONS, RECOMMENDATIONS, AND DATA CONTAINED IN THAT INVESTIGATION PRIOR TO ANY DISTURBANCE TO THE PROJECT AREA.
2. CONTRACTOR SHALL REMOVE EXISTING ASPHALT, PCC CONCRETE, CURB AND GUTTER, ETC. AS REQUIRED TO INSTALL NEW IMPROVEMENTS. CONTRACTOR SHALL BE RESPONSIBLE FOR REMOVAL AND DISPOSAL OF ANY AND ALL DEBRIS RELATED TO DEMOLITION. CONTRACTOR SHALL INCLUDE, IN HIS BASE BID, ALL COSTS REQUIRED TO DEMOLISH AND REPLACE ANY ITEMS REQUIRED TO INSTALL THE NEW IMPROVEMENTS SHOWN IN THE CONSTRUCTION DOCUMENTS.
3. CONTRACTOR SHALL REMOVE AND STORE ON SITE ANY EXISTING SIGNAGE WITHIN THE LIMITS OF DISTURBANCE TO PREVENT DAMAGE DURING CONSTRUCTION.

SITE NOTES:

1. CONTRACTOR SHALL BE RESPONSIBLE FOR OBTAINING ALL PERMITS FOR THIS PROJECT PRIOR TO COMMENCEMENT OF ANY CONSTRUCTION OR DEMOLITION.
2. CONTRACTOR SHALL INSTALL ISOLATION JOINTS BETWEEN THE SIDEWALKS AND OTHER FIXED STRUCTURES.
3. CONTRACTOR SHALL BE RESPONSIBLE FOR COORDINATING WITH ANY AND ALL UTILITY COMPANIES IN REGARDS TO UTILITIES THAT MAY NEED TO BE RELOCATED AS PART OF THIS WORK.
4. CONTRACTOR SHALL PROVIDE PROPER TRAFFIC CONTROL WARNING SIGNS THROUGH THE DURATION OF THE PROJECT AS REQUIRED BY THE ENGINEER OF RECORD AND AUTHORITIES HAVING JURISDICTION. ALL SIGNAGE SHALL BE IN ACCORDANCE WITH THE "MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES" (MUTCD), LATEST EDITION.
5. IF TRAFFIC INTERRUPTIONS ARE REQUIRED, THEY SHALL BE KEPT TO A MINIMUM AND THE CONTRACTOR SHALL BE SUBJECT TO LOCAL LAWS IN REGARDS TO TRAFFIC INTERRUPTIONS.
6. CONTRACTOR SHALL KEEP ALL OTHER ROADS OPERATIONAL THROUGHOUT THE COURSE OF THE PROJECT. HOWEVER, IN THE EVENT ROAD CLOSURE IS NECESSARY, CONTRACTOR SHALL NOTIFY ALL AGENCIES AT LEAST SEVENTY-TWO (72) HOURS IN ADVANCE OF ANY ROAD CLOSINGS. THIS NOTIFICATION SHALL INCLUDE, BUT NOT BE LIMITED TO, POLICE, FIRE AND OWNER ALONG WITH ALL REGULATORY AND GOVERNMENTAL AGENCIES. IF TRAFFIC INTERRUPTIONS ARE REQUIRED, THEY SHALL BE KEPT TO A MINIMUM AND THE CONTRACTOR SHALL BE SUBJECT TO LOCAL LAWS IN REGARDS TO TRAFFIC INTERRUPTIONS.
7. CONTRACTOR SHALL BE RESPONSIBLE FOR VERIFYING ALL DIMENSIONS AS SHOWN ON THE SITE LAYOUT PLAN. ANY DISCREPANCIES SHALL BE BROUGHT TO THE IMMEDIATE ATTENTION OF THE ENGINEER. CONTRACTOR SHALL CONSULT AND VERIFY ALL BUILDING DIMENSIONS WITH THE BUILDING PLANS AND THE FOUNDATION PLANS. IF ANY DISCREPANCIES ARISE, THE BUILDING PLANS AND/OR THE FOUNDATION PLAN OVERRIDE ANY DIMENSIONS ON THE SITE LAYOUT PLAN. CONTRACTOR SHALL BE RESPONSIBLE FOR NOTIFYING ENGINEER IF ANY SAID DISCREPANCIES MAY AFFECT THE LAYOUT OF THE SITE PLAN.
8. PROPERTY LINE AND OTHER SITE FEATURES ARE BASED ON PREVIOUS SURVEYS AND PROJECTS. THEY SHOULD BE TAKEN AS APPROXIMATE AND CONTRACTOR SHOULD LOCATE THE TRUE PROPERTY BOUNDARY WHERE WORKING NEAR THE PROPERTY LINES.

SITE GRADING & DRAINAGE NOTES:


1. ALL TOPOGRAPHIC INFORMATION INCLUDING, BUT NOT LIMITED TO, LOCATIONS OF ALL EXISTING ABOVE AND BELOW GROUND UTILITIES, EXISTING SANITARY SEWER INVERT INFORMATION, TREES, AND EXISTING ROADWAYS WERE TAKEN FROM A TOPOGRAPHIC SURVEY PERFORMED BY BARNES SURVEYING, LLC AND EXISTING AS-BUILT DRAWINGS. IF THE CONTRACTOR DOES NOT ACCEPT THE EXISTING TOPOGRAPHY AND/OR UTILITIES AS SHOWN ON THESE PLANS, WITHOUT EXCEPTION, HE SHALL HAVE MADE, AT HIS EXPENSE, A TOPOGRAPHIC SURVEY BY A REGISTERED LAND SURVEYOR AND SUBMIT IT TO THE OWNER AND THE ENGINEER OF RECORD FOR REVIEW.
2. THE CONTRACTOR IS SPECIFICALLY CAUTIONED THAT THE LOCATION AND/OR ELEVATION OF EXISTING UTILITIES AS SHOWN ON THESE PLANS IS BASED ON THE PROVIDED SURVEY, RECORDS OF THE VARIOUS UTILITY COMPANIES, EXISTING AS-BUILT DRAWINGS, AND CONVERSATIONS WITH THE OWNER. THE INFORMATION IS NOT TO BE RELIED ON AS BEING EXACT OR COMPLETE. THE CONTRACTOR MUST CALL THE APPROPRIATE UTILITY COMPANY AT LEAST 72 HOURS BEFORE ANY EXCAVATION TO REQUEST EXACT FIELD LOCATION OF UTILITIES. IT SHALL BE THE CONTRACTOR'S RESPONSIBILITY TO RELOCATE ALL EXISTING UTILITIES WHICH CONFLICT WITH THE PROPOSED IMPROVEMENTS SHOWN ON THE PLANS.
3. CONTRACTOR SHALL BE RESPONSIBLE FOR VERIFYING HORIZONTAL AND VERTICAL LOCATIONS OF ALL EXISTING STORM SEWER STRUCTURES, PIPES, ETC., AND ALL UTILITIES PRIOR TO CONSTRUCTION.
4. CLEARING AND GRUBBING LIMITS SHALL INCLUDE ALL AREAS DISTURBED BY GRADING OPERATIONS. CONTRACTOR IS RESPONSIBLE FOR THE PROTECTION OF ALL UNDISTURBED AREAS, ALL PROPERTY CORNERS AND REPLACING ALL PINS AND SURVEY BENCHMARKS ELIMINATED OR DAMAGED DURING CONSTRUCTION.
5. CONTRACTOR SHALL BE RESPONSIBLE FOR FAMILIARIZING HIMSELF WITH ALL LOCAL GOVERNING CODES AND SHALL COMPLY WITH SAID CODES.
6. ALL PIPE SHALL BE INSTALLED IN ACCORDANCE WITH THE MANUFACTURER'S RECOMMENDATIONS.
7. ANY DRAINAGE STRUCTURE, CURB INLET, OR CATCH BASIN WITH A DEPTH GREATER THAN FOUR FEET ARE REQUIRED TO HAVE STEPS.
8. ALL FINISHED GRADES SHOWN IN ROADWAY/PARKING ARE TOP OF PAVEMENT UNLESS OTHERWISE NOTED.

SHEET LIST	
SHEET	DESCRIPTION
C001	CIVIL GENERAL NOTES
C101	EROSION CONTROL PLAN
C111	DEMOLITION PLAN
C112	OVEREXCAVATION PLAN
C121	SITE PLAN
C131	GRADING PLAN
C201	CIVIL DETAILS
C202	CIVIL DETAILS
C203	CIVIL DETAILS



FOOTBALL
FIELD TURF &
TRACK
REPLACEMENT

RIDGELAND HIGH
SCHOOL
586 SUNNYBROOK ROAD
RIDGELAND, MS 39157



APRIL 8, 2021

CONSTRUCTION
DOCUMENTS
WBA # 5620

REVISIONS		
NO.	DESCRIPTION	DATE



C001
CIVIL
GENERAL
NOTES

DEVELOPER/OWNER
DEVELOPER/GENERAL CONTRACTOR
SUPERINTENDENT

ACREAGE SUMMARY	
TOTAL PROPERTY AREA	71.18 ACRES *
ON-SITE DISTURBED AREA	3.53 ACRES
OFF-SITE DISTURBED AREA	0.00 ACRES
TOTAL DISTURBED AREA	3.53 ACRES

* PER MADISON COUNTY TAX MAPS

SPECIFICATIONS REQUIREMENT:
THE REQUIREMENTS SHOWN ON THIS PLAN ARE SUPPLEMENTED BY THE SWPPP CONTAINED WITHIN THE PROJECT SPECIFICATIONS. IN CASE OF CONFLICTS BETWEEN THE PLANS, SWPPP SPECIFICATIONS AND THE ACTUAL GENERAL PERMIT, THE MOST STRINGENT REQUIREMENTS SHALL APPLY.

-CAUTION NOTICE TO CONTRACTOR:
IF PROPERLY IMPLEMENTED, THIS PLAN WILL PROVIDE AN EFFECTIVE MEANS FOR CONTROLLING EROSION. HOWEVER, IT IS ACKNOWLEDGED THAT NO ONE PLAN CAN BE PREPARED THAT WILL DEPICT ALL POSSIBLE MEASURES NECESSARY FOR VARIOUS STAGES OF CONSTRUCTION. THE CONTRACTOR SHALL INCLUDE IN THE BASE BID ADEQUATE FUNDS TO PROVIDE ALL EROSION CONTROL MEASURES NECESSARY TO COMPLY WITH CODES FOR THE DURATION OF THE CONSTRUCTION PROJECT.


LIMITS OF DISTURBANCE
CONTRACTOR TO LIMIT DISTURBANCE OF SITE IN STRICT ACCORDANCE WITH THE EROSION CONTROL SEQUENCING SHOWN ON THIS PLAN. NO UNNECESSARY OR IMPROPERLY SEQUENCED CLEARING AND/OR GRADING SHALL BE PERMITTED.

- PHASE I EROSION CONTROL SEQUENCING
1. INSTALL STABILIZED CONSTRUCTION EXIT(S) AND INSTALL SILT FENCE(S) ON THE SITE (CLEAR ONLY THOSE AREAS NECESSARY TO INSTALL SILT FENCE).
 2. PREPARE TEMPORARY PARKING AND STORAGE AREA.
 3. INSTALL INLET PROTECTION AT EXISTING STORM STRUCTURES.
 4. SEQUENCE GRADING OPERATIONS TO MINIMIZE EXPOSED AREAS.
- PHASE II EROSION CONTROL SEQUENCING
5. TEMPORARILY SEED, THROUGHOUT CONSTRUCTION, DENUDE AREAS THAT WILL BE INACTIVE FOR 14 DAYS OR MORE.
 6. INSTALL, REPLACE, REPAIR, OR MAINTAIN PERIMETER SILT FENCE, INLET PROTECTION, AND CONSTRUCTION EXIT AS NEEDED.
 7. UNDERCUT MATERIALS FOR TRACK AND PLAYING SURFACE.
 8. BEGIN CONSTRUCTION OF TRACK AND PLAYING SURFACE.
 9. INSTALL STORM SEWERS.
 10. INSTALL INLET PROTECTION AT ALL STORM SEWER STRUCTURES AS EACH INLET STRUCTURE IS INSTALLED.
 11. PREPARE SITE FOR PAVING AND INSTALLATION OF TURF.
 12. PAVE SITE AND INSTALL TURF.
 13. INSTALL APPROPRIATE INLET PROTECTION DEVICES FOR PAVED AREAS AS WORK PROGRESSES.
 14. COMPLETE GRADING AND INSTALLATION OF PERMANENT STABILIZATION OVER ALL AREAS.

- 100 YEAR FLOODPLAINS, FLOODWAY FRINGES, AND FLOODWAYS
- THE PROJECT IS LOCATED IN ZONE X (AREAS DETERMINED TO BE OUTSIDE THE 0.2% ANNUAL CHANCE FLOODPLAIN)
- RECEIVING WATERS
- THE MAJORITY OF THE SITE DRAINS TO THE SOUTHWEST VIA UNDERGROUND STORM SEWER TO AN UNNAMED TRIBUTARY OF BRASHEAR CREEK WHICH IS THE ULTIMATE RECEIVING WATER OF THE SITE. BRASHEAR CREEK IS LOCATED APPROXIMATELY 1.44 MILES TO THE EAST OF THE SITE. BRASHEAR CREEK IS NOT LISTED ON THE 2018 STATE OF MISSISSIPPI 303D LIST OF IMPAIRED WATERWAYS.
- SOIL TYPE
- THERE ARE TWO SOIL TYPES FOR THE PROJECT LISTED ON THE USDA NRCS SOIL SURVEY. THESE SOILS ARE AS FOLLOWS:
BR2C BYRAM SILT LOAM MODERATELY WELL DRAINED
RE RIEDTOWN SILT LOAM MODERATELY WELL DRAINED

EROSION CONTROL LEGEND



- 327 --- MINOR CONTOUR, EXISTING
--- 330 --- MAJOR CONTOUR, EXISTING
--- LD --- LIMITS OF DISTURBANCE
--- SF --- SILT FENCE
--- IP1 --- STRAW WATTLE INLET PROTECTION
--- CONSTRUCTION ENTRANCE

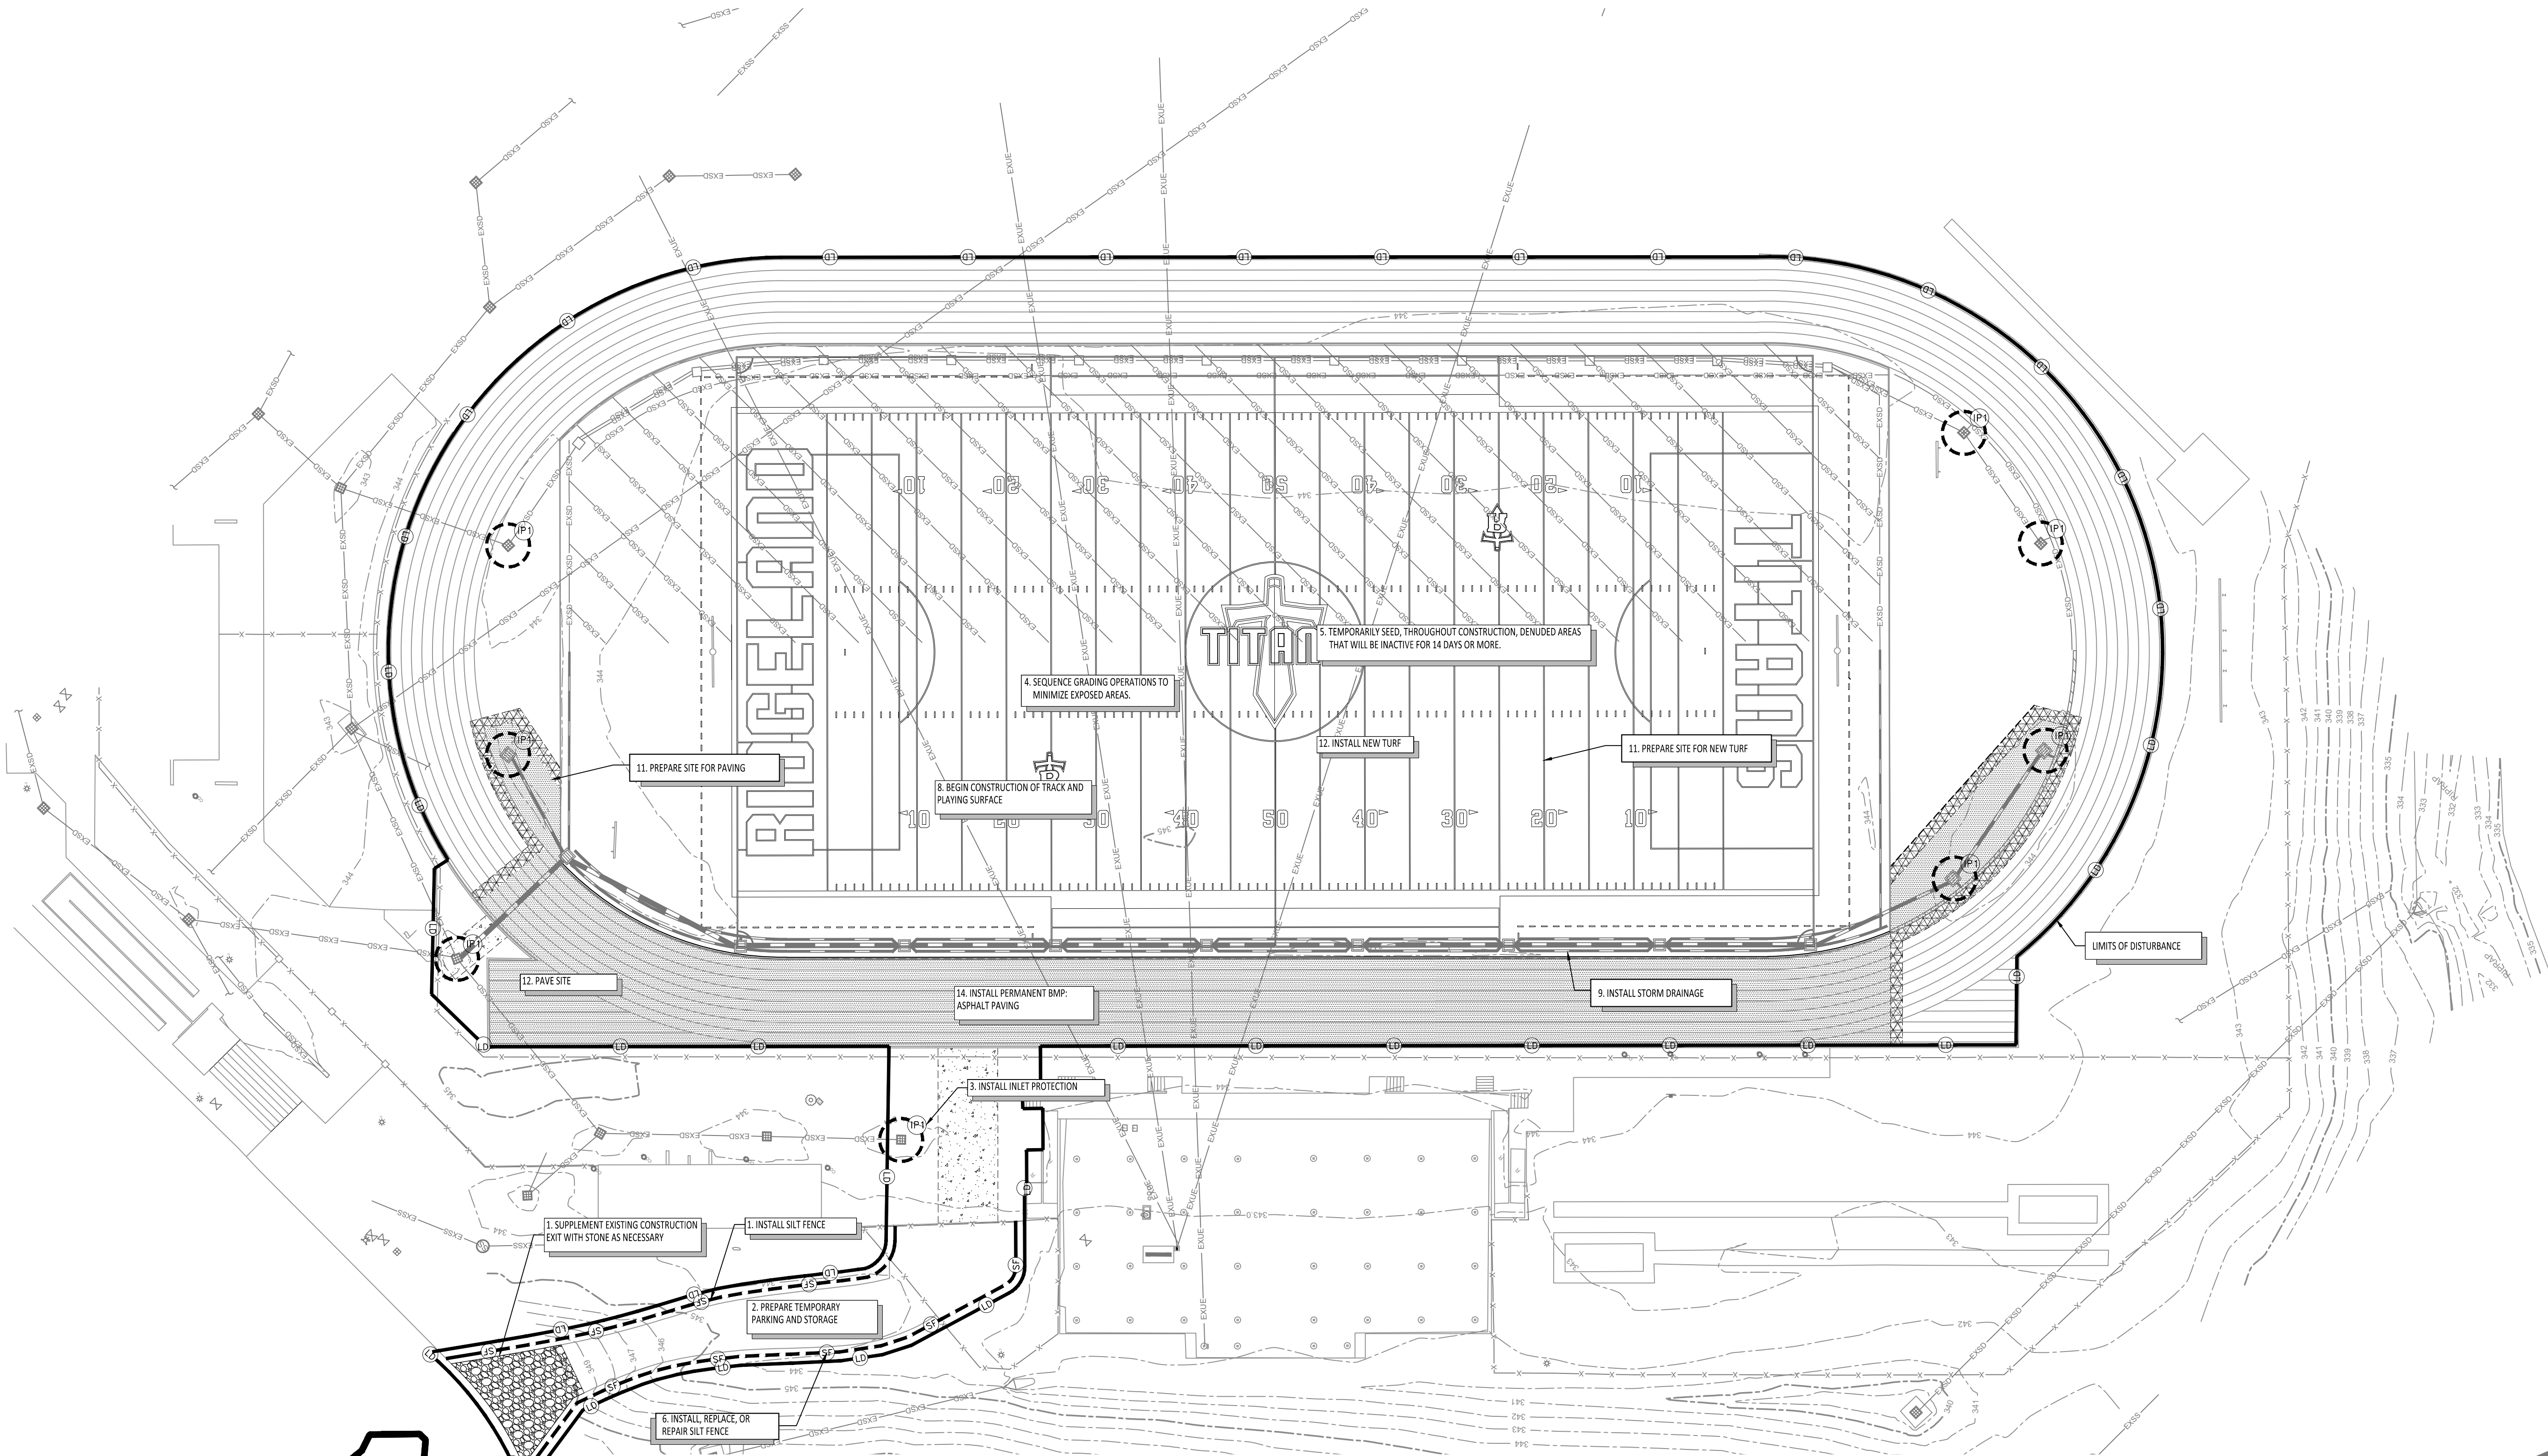

DEMOLITION NOTES:

- CONTRACTOR MUST USE CAUTION DURING DEMOLITION, PARTICULARLY IN AREAS TO RECEIVE CONCRETE OR ASPHALT DEMOLITION. ANY UTILITY, STRUCTURES, OR OTHER ITEMS DAMAGED AS A RESULT OF CONSTRUCTION ACTIVITIES SHALL BE REPLACED BY THE CONTRACTOR AT NO ADDITIONAL COST TO THE OWNER.
- THE CONTRACTOR SHALL KEEP ALL UTILITIES OPERATIONAL THROUGHOUT THE ENTIRETY OF THE PROJECT. ANY INTERRUPTION IN UTILITY SERVICE SHALL BE COORDINATED WITH THE OWNER AND AUTHORITIES HAVING JURISDICTION PRIOR TO COMMENCING CONSTRUCTION ACTIVITIES.
- IT IS THE CONTRACTOR'S RESPONSIBILITY TO PHASE CONSTRUCTION ACTIVITIES TO PROVIDE POSITIVE STORM WATER RUNOFF AT ALL TIMES. SEE STORM WATER POLLUTION PREVENTION PLAN (SWPPP) PLAN FOR ADDITIONAL INFORMATION ON EROSION CONTROL MEASURES REQUIRED.
- CONTRACTOR SHALL REFERENCE SITE AND GRADING PLANS TO COORDINATE PAVEMENT AND UTILITY DEMOLITION AND CONNECTION TO PROPOSED PAVEMENT, ETC. PRIOR TO COMMENCING CONSTRUCTION ACTIVITIES.
- EXISTING PIPE TO BE REMOVED SHALL BE REMOVED IN ITS ENTIRETY.
- IN ALL AREAS WHERE THE CONTRACTOR MUST CROSS THE EXISTING ASPHALT OR SIDEWALK, IT IS THE CONTRACTOR'S RESPONSIBILITY TO REPAIR THE PAVEMENT OR SIDEWALK PER THE DETAIL SHEETS. THE CONTRACTOR SHALL INCLUDE THE COST NECESSARY TO PERFORM THE ASPHALT REPAIRS IN HIS BASE BID IF DEEMED NECESSARY.
- IF THE CONTRACTOR MUST CROSS AN EXISTING ITEM (PAVEMENT, SIDEWALK, ETC.) TO INSTALL A NEW IMPROVEMENT (UTILITIES, STORM DRAINAGE, ETC.), THE CONTRACTOR SHALL INCLUDE IN HIS BASE BID, ALL COST REQUIRED TO REPLACE THE EXISTING ITEM IMPACTED BY CONSTRUCTION.



DEMOLITION PLAN LEGEND:

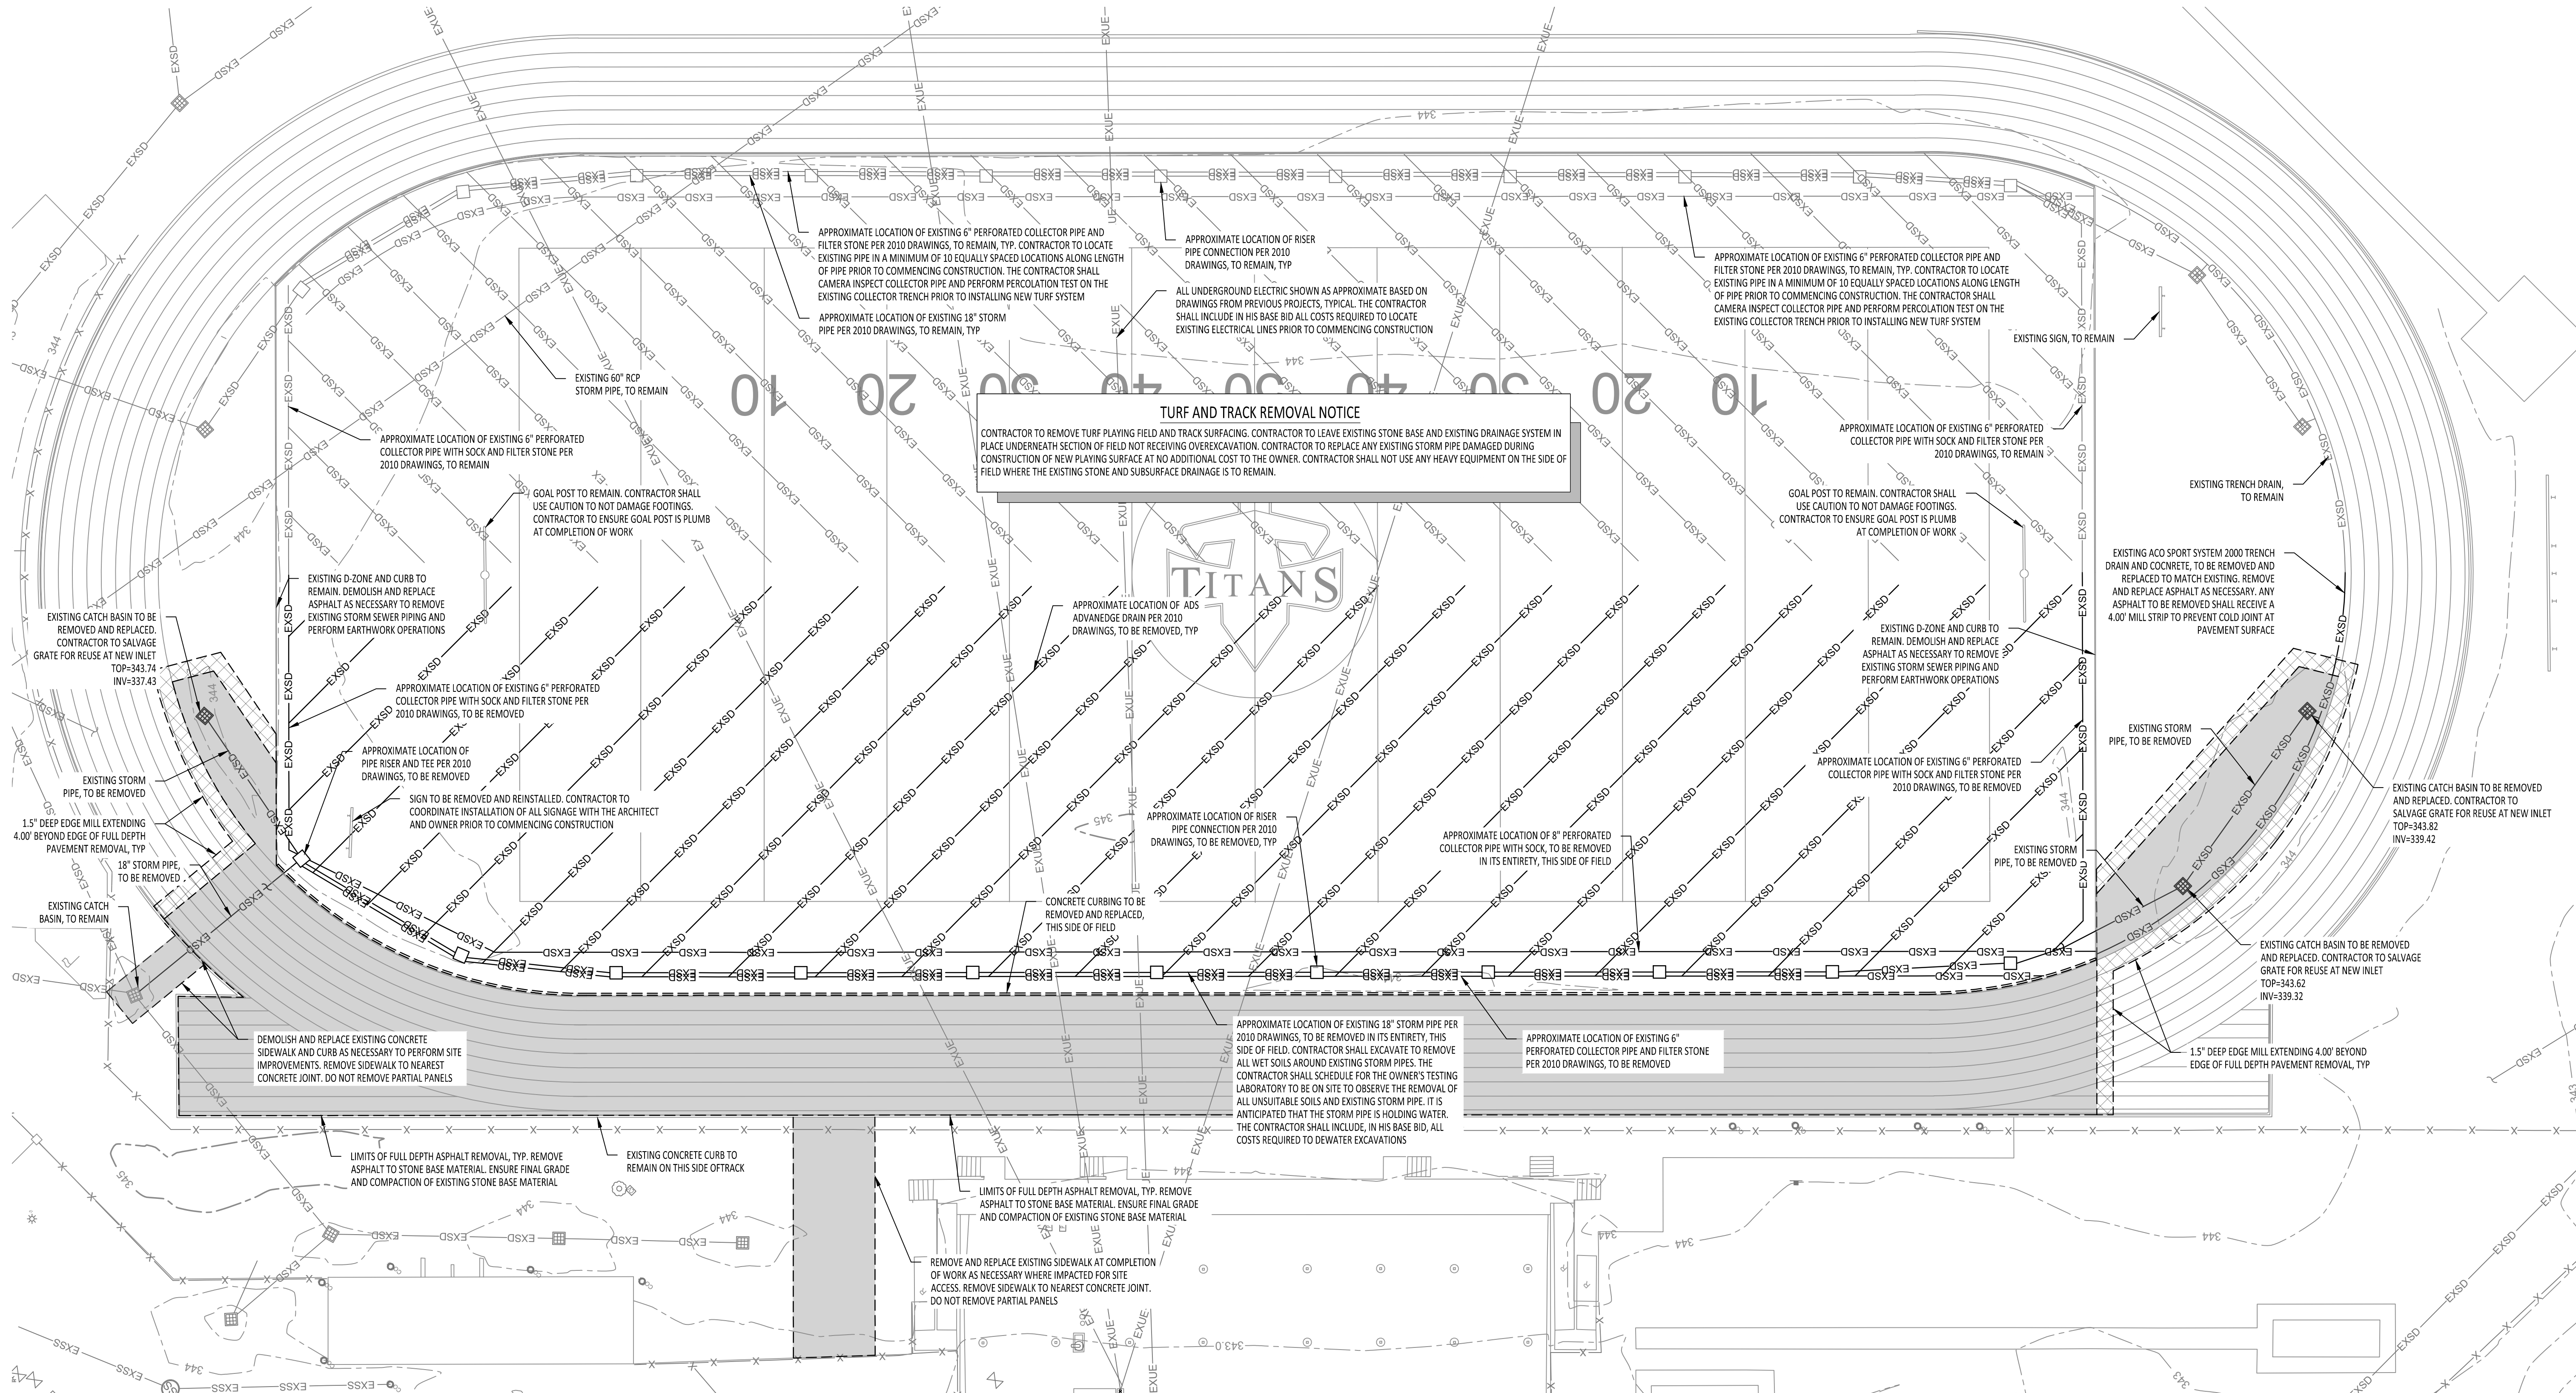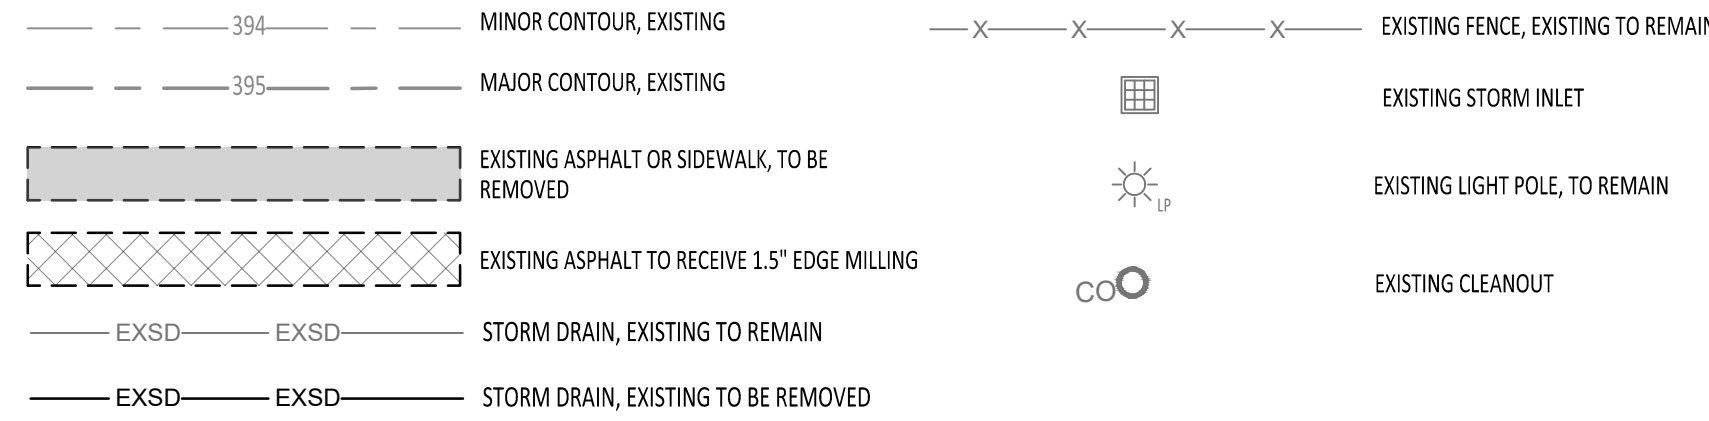

APRIL 8, 2021

CONSTRUCTION
DOCUMENTS
WBA # 5620

REVISIONS
NO. DESCRIPTION DATE



UNDERCUTTING NOTICE

THE EXISTING FIELD SHALL BE OVER EXCAVATED TO THE ELEVATIONS DEPICTED ON THIS PLAN TO REMOVE EXISTING WET AND/OR EXPANSIVE SUBGRADE SOILS IN ACCORDANCE WITH THE GEOTECHNICAL REPORT. ALL OVER EXCAVATION SHALL BE BACKFILLED WITH SUITABLE FILL MATERIALS COMPACTED TO A MINIMUM OF 95% STANDARD PROCTOR DENSITY. OVEREXCAVATION AND PLACEMENT OF FILL MATERIALS SHALL MEET ALL REQUIREMENTS STATED IN THE GEOTECHNICAL REPORT. THE OWNERS CONSTRUCTION TESTING LABORATORY SHALL BE PRESENT TO OBSERVE ALL EXCAVATION AND FILLING WORK.

OVEREXCAVATION STORM WATER CONTROL


THE CONTRACTOR'S BASE BID SHALL INCLUDE ALL COSTS NECESSARY TO CONTROL STORM WATER AND GROUND WATER IN THE OVEREXCAVATION AREAS. THIS INCLUDES DIVERSION BERMS, PUMPING, AND ANY OTHER MEANS NECESSARY. DISCHARGE OF STORM WATER FROM OVEREXCAVATION AREAS SHALL MEET ALL LOCAL, STATE, AND FEDERAL REQUIREMENTS. UPDATE THE EROSION CONTROL PLAN AS NECESSARY TO SECURE THIS WORK IF THE CONTRACTOR OBSERVES ANY SUBSURFACE WATER DURING EXCAVATION WORK. THEY SHALL IMMEDIATELY NOTIFY THE DESIGN TEAM AND OWNER'S CONSTRUCTION TESTING LABORATORY FOR REVIEW BEFORE PROCEEDING WITH WORK IN THAT AREA.

OVEREXCAVATION PLAN LEGEND:


- 327 --- EXISTING MINOR CONTOUR
- 380 --- EXISTING MAJOR CONTOUR
- 344 --- MINOR EXCAVATION CONTOUR
- 345 --- MAJOR EXCAVATION CONTOUR

OVEREXCAVATION AND BACKFILL NOTES:



- BELOW IS A GRAPHICAL REPRESENTATION OF THE FIELD OVEREXCAVATION AND BACKFILL. THE CONTRACTOR SHALL CLOSELY FOLLOW THE RECOMMENDATIONS IN THE GEOTECHNICAL REPORT. ANY DISCREPANCIES BETWEEN THE PLANS AND GEOTECHNICAL REPORT SHALL BE BROUGHT TO THE ATTENTION OF THE CIVIL ENGINEER PRIOR TO COMMENCING CONSTRUCTION ACTIVITIES.
- CONTRACTOR SHALL OVER EXCAVATE TO THE ELEVATIONS SHOWN ON THIS PLAN AND THE MATERIALS SHALL BE DISPOSED OF OFFSITE. THE BOTTOM OF EXCAVATION SHALL BE SLOPED TO DRAIN. SEE OVEREXCAVATION STORM WATER CONTROL BOX NOTE.
- ONCE THE OVEREXCAVATION GRADE IS REACHED, THE CTL SHALL VISUALLY OBSERVE THE BOTTOM OF THE OVEREXCAVATION FOR POTENTIALLY SOFT, WET OR UNSTABLE AREAS.
- THE BOTTOM OF THE OVEREXCAVATION SHALL BE PROOFROLLED IN ACCORDANCE WITH THE EARTHWORK SPECIFICATION. ANY AREAS OF INSTABILITY SHALL BE MITIGATED AT THE DIRECTION OF THE GEOTECHNICAL ENGINEER.
- TESTING OF SUBGRADE MATERIALS SHALL BE PERFORMED IN ACCORDANCE WITH THE EARTHWORK SPECIFICATION.
- THE BUILDING PAD SHALL THEN BE BACKFILLED WITH SUITABLE MATERIALS WITHIN 3% OF OPTIMUM MOISTURE CONTENT IN LIFTS NOT EXCEEDING 9" AND COMPACTED TO A MINIMUM 95% STANDARD PROCTOR DRY DENSITY (ASTM D 698). FIELD DENSITY AND LABORATORY TESTING SHALL BE PERFORMED BY THE CTL IN ACCORDANCE WITH THE EARTHWORK SPECIFICATION. WHERE CONTROLLED MECHANICAL TAMPERS ARE USED TO COMPACT FILL MATERIALS, THE LOOSE LIFT THICKNESS SHALL BE LIMITED TO 5".
- THE SIDES OF THE OVEREXCAVATION SHALL BE BENCHMARKED PRIOR TO PLACEMENT OF SUITABLE FILL MATERIALS.

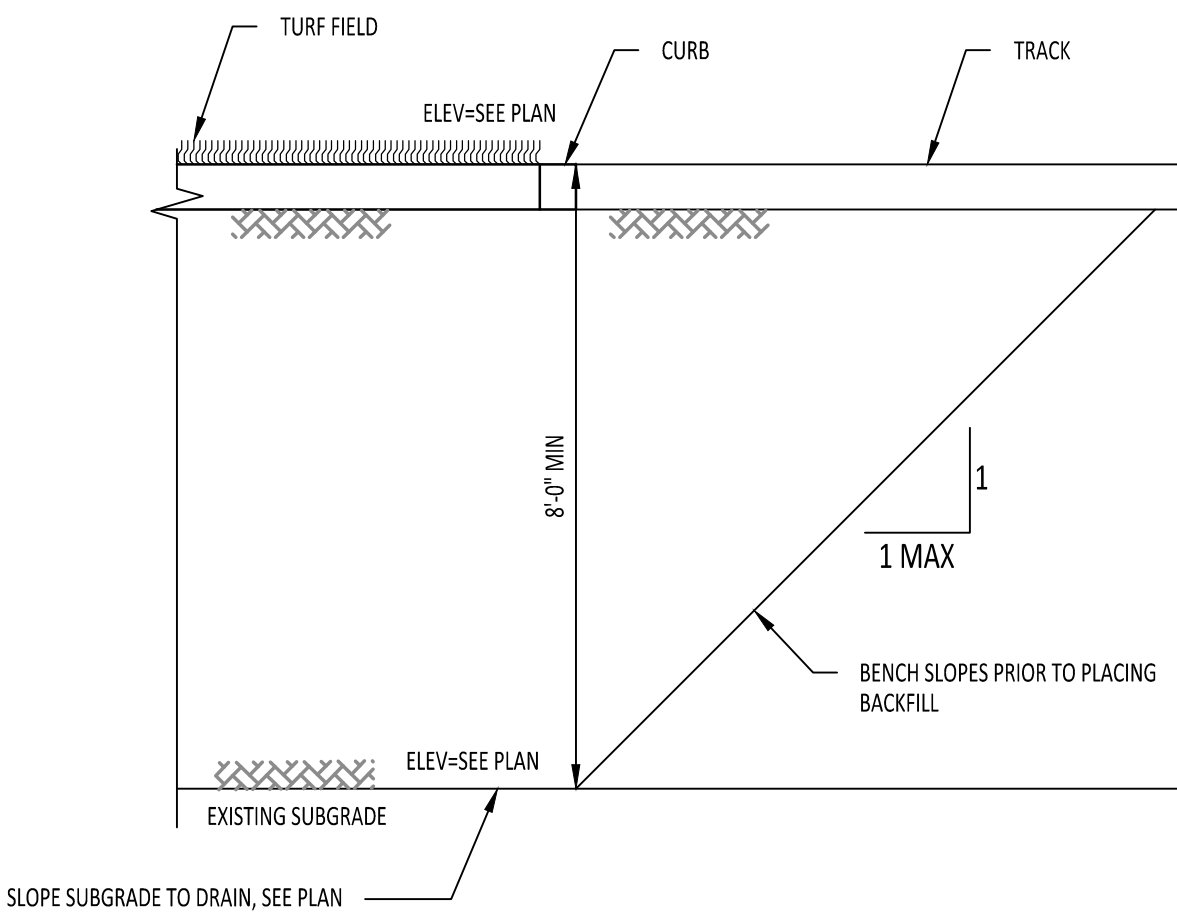

1 FIELD OVEREXCAVATION AND BACKFILL
SCALE: NOT TO SCALE

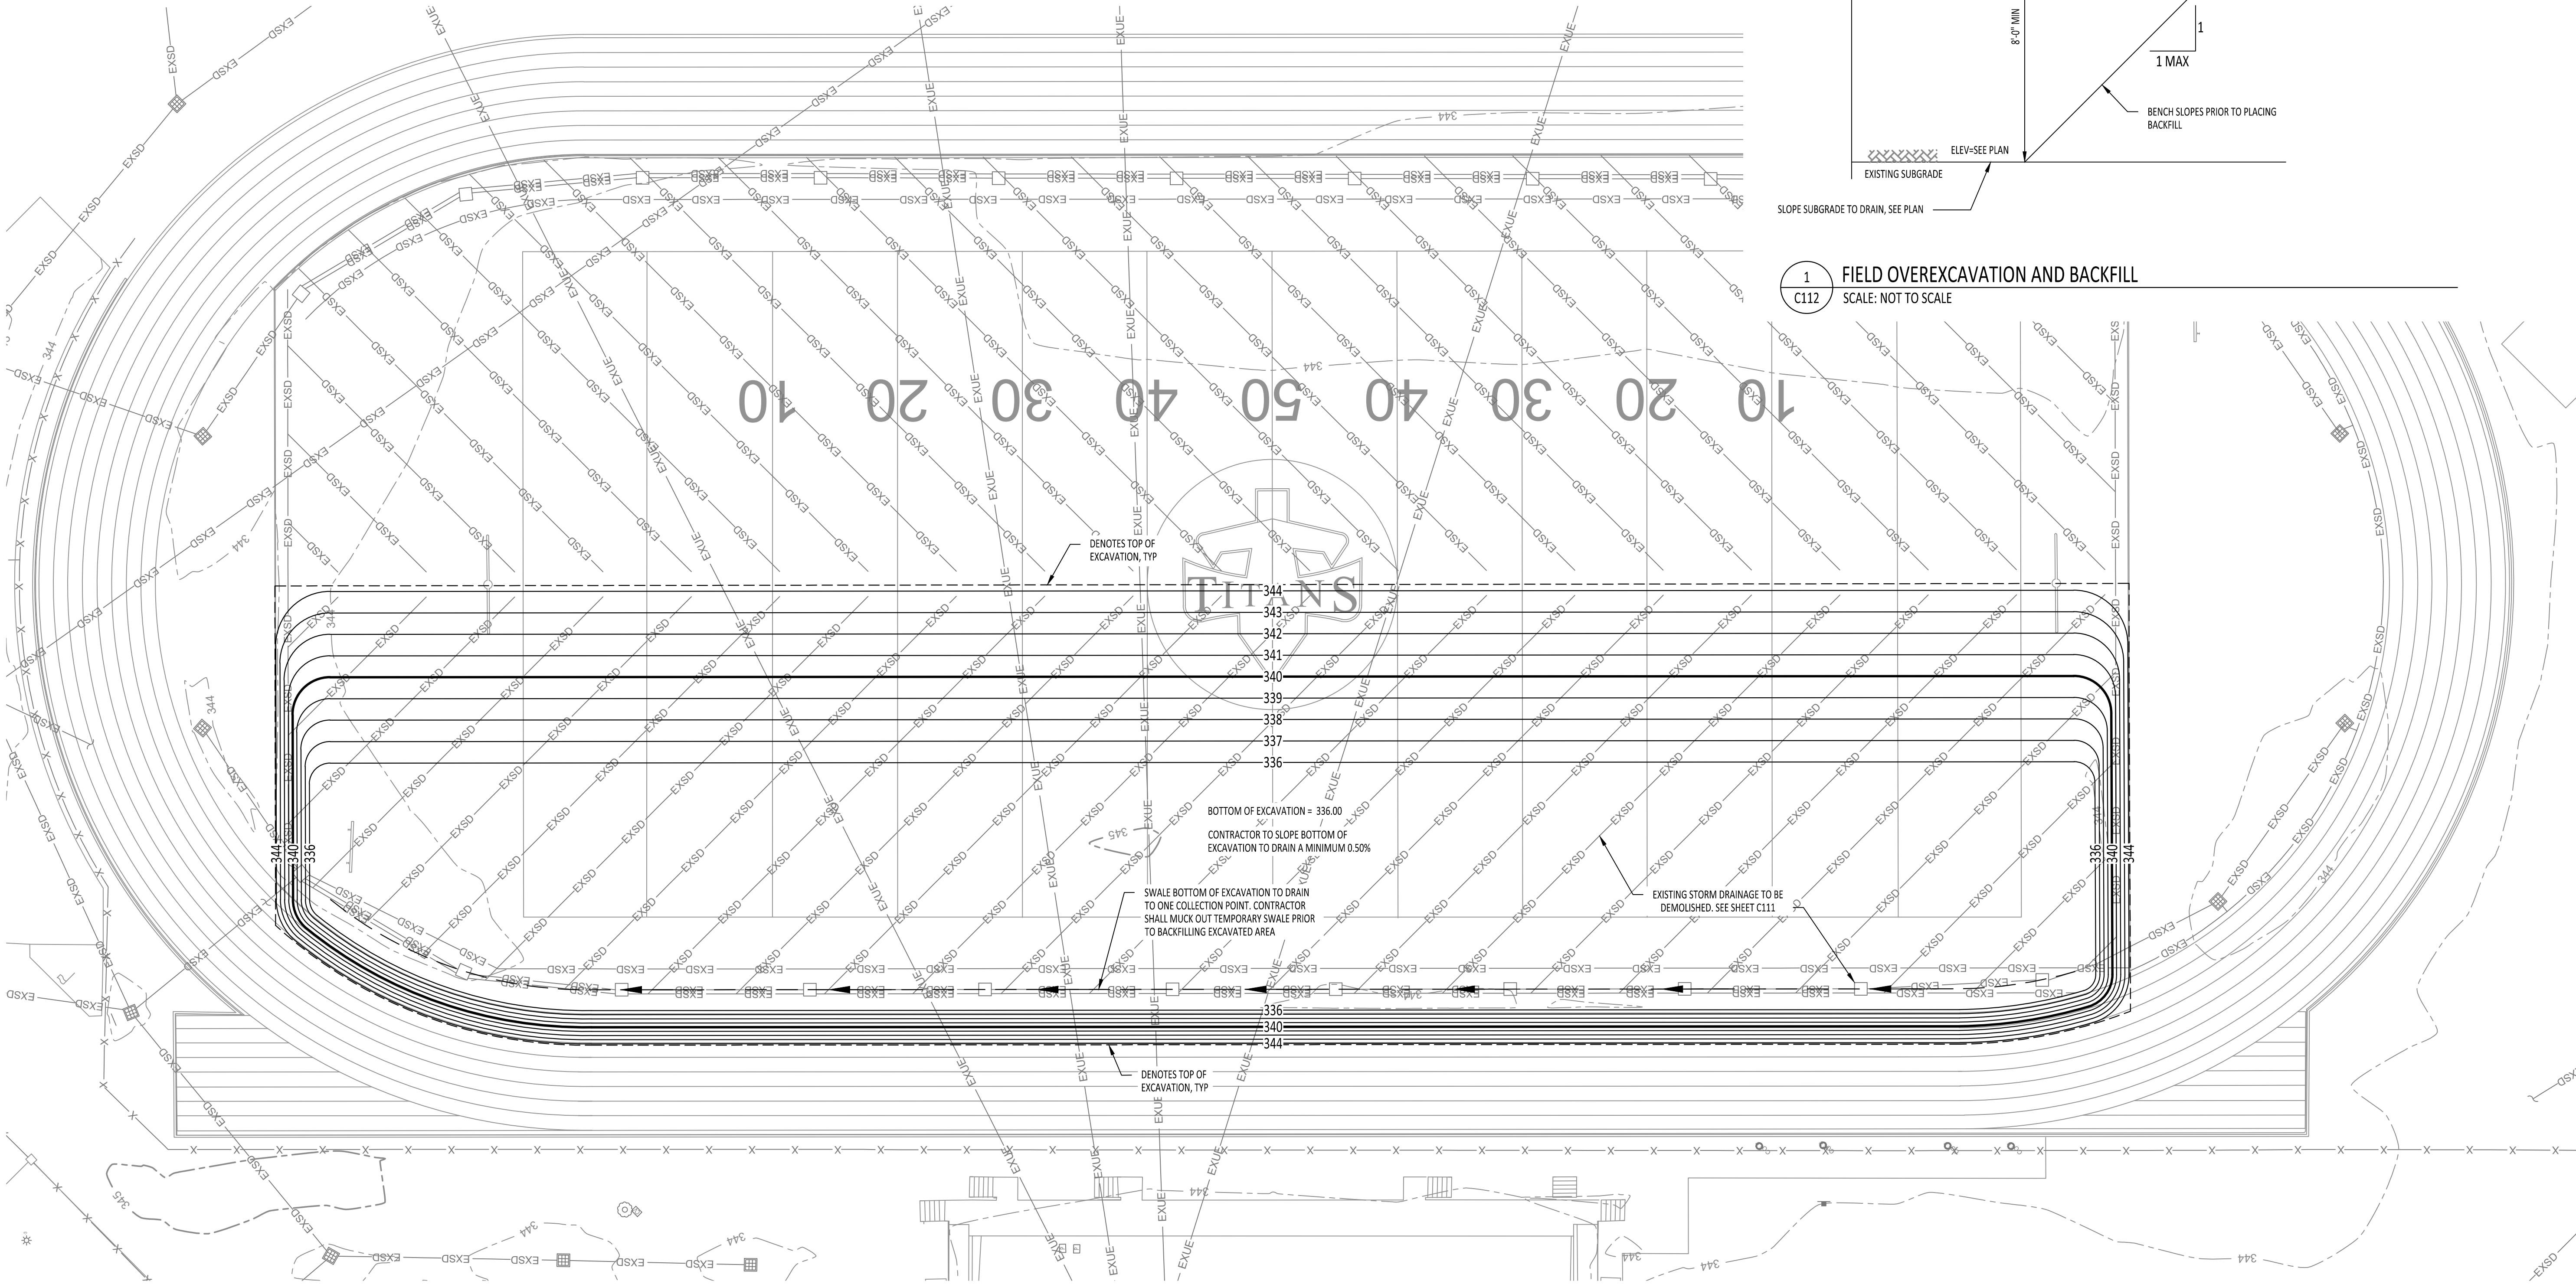


OVEREXCAVATION PLAN
SCALE: 1"=20'-0"



FOOTBALL
FIELD TURF &
TRACK
REPLACEMENT

RIDGELAND HIGH
SCHOOL
586 SUNNYBROOK ROAD
RIDGELAND, MS 39157



APRIL 8, 2021



CONSTRUCTION
DOCUMENTS
WBA # 5620

REVISIONS		
NO.	DESCRIPTION	DATE




SITE PLAN NOTES:

- 1 ALL DIMENSIONS SHALL BE TO FACE OF CURB UNLESS NOTED OTHERWISE.
- 2 ALL CURBS SHALL BE CONCRETE NOTED OTHERWISE. SEE DETAIL SHEET FOR ADDITIONAL INFORMATION.
- 3 IT IS THE CONTRACTOR'S RESPONSIBILITY TO ENSURE A SMOOTH TRANSITION BETWEEN EXISTING AND PROPOSED PAVING AND SIDEWALK AREAS.
- 4 HANDICAP ROUTES SHALL MEET CITY OF RIDGELAND AND CURRENT ADA STANDARDS.
- 5 SIDEWALK WIDTH VARIES. CONTROL JOINTS SHALL BE PLACED EVERY 5' O.C. MIN. AND CONSTRUCTION JOINTS SHALL BE PLACED EVERY 30' O.C. MIN. REFERENCE SIDEWALK DETAIL PROJECT SPECIFICATIONS FOR ADDITIONAL INFORMATION.
- 6 CONTRACTOR SHALL COMPLY TO ALL APPLICABLE LOCAL AND STATE CODES
- 7 CONTRACTOR SHALL TIE-IN PROPOSED CURB AND GUTTER TO EXISTING. MATCH THE EXISTING CURB SIZE AND TYPE AT TIE-IN.
- 8 ISOLATION JOINT TYPICAL AT FIXED STRUCTURES (BUILDING, RETAINING WALLS, DRAINAGE STRUCTURES, MANHOLES, LIGHT POLE BASES, BOLLARDS, ETC). SEE DETAIL SHEET FOR ADDITIONAL INFORMATION.
- 9 SEE DETAIL SHEET FOR CONCRETE JOINT REQUIREMENTS.

SITE PLAN LEGEND :

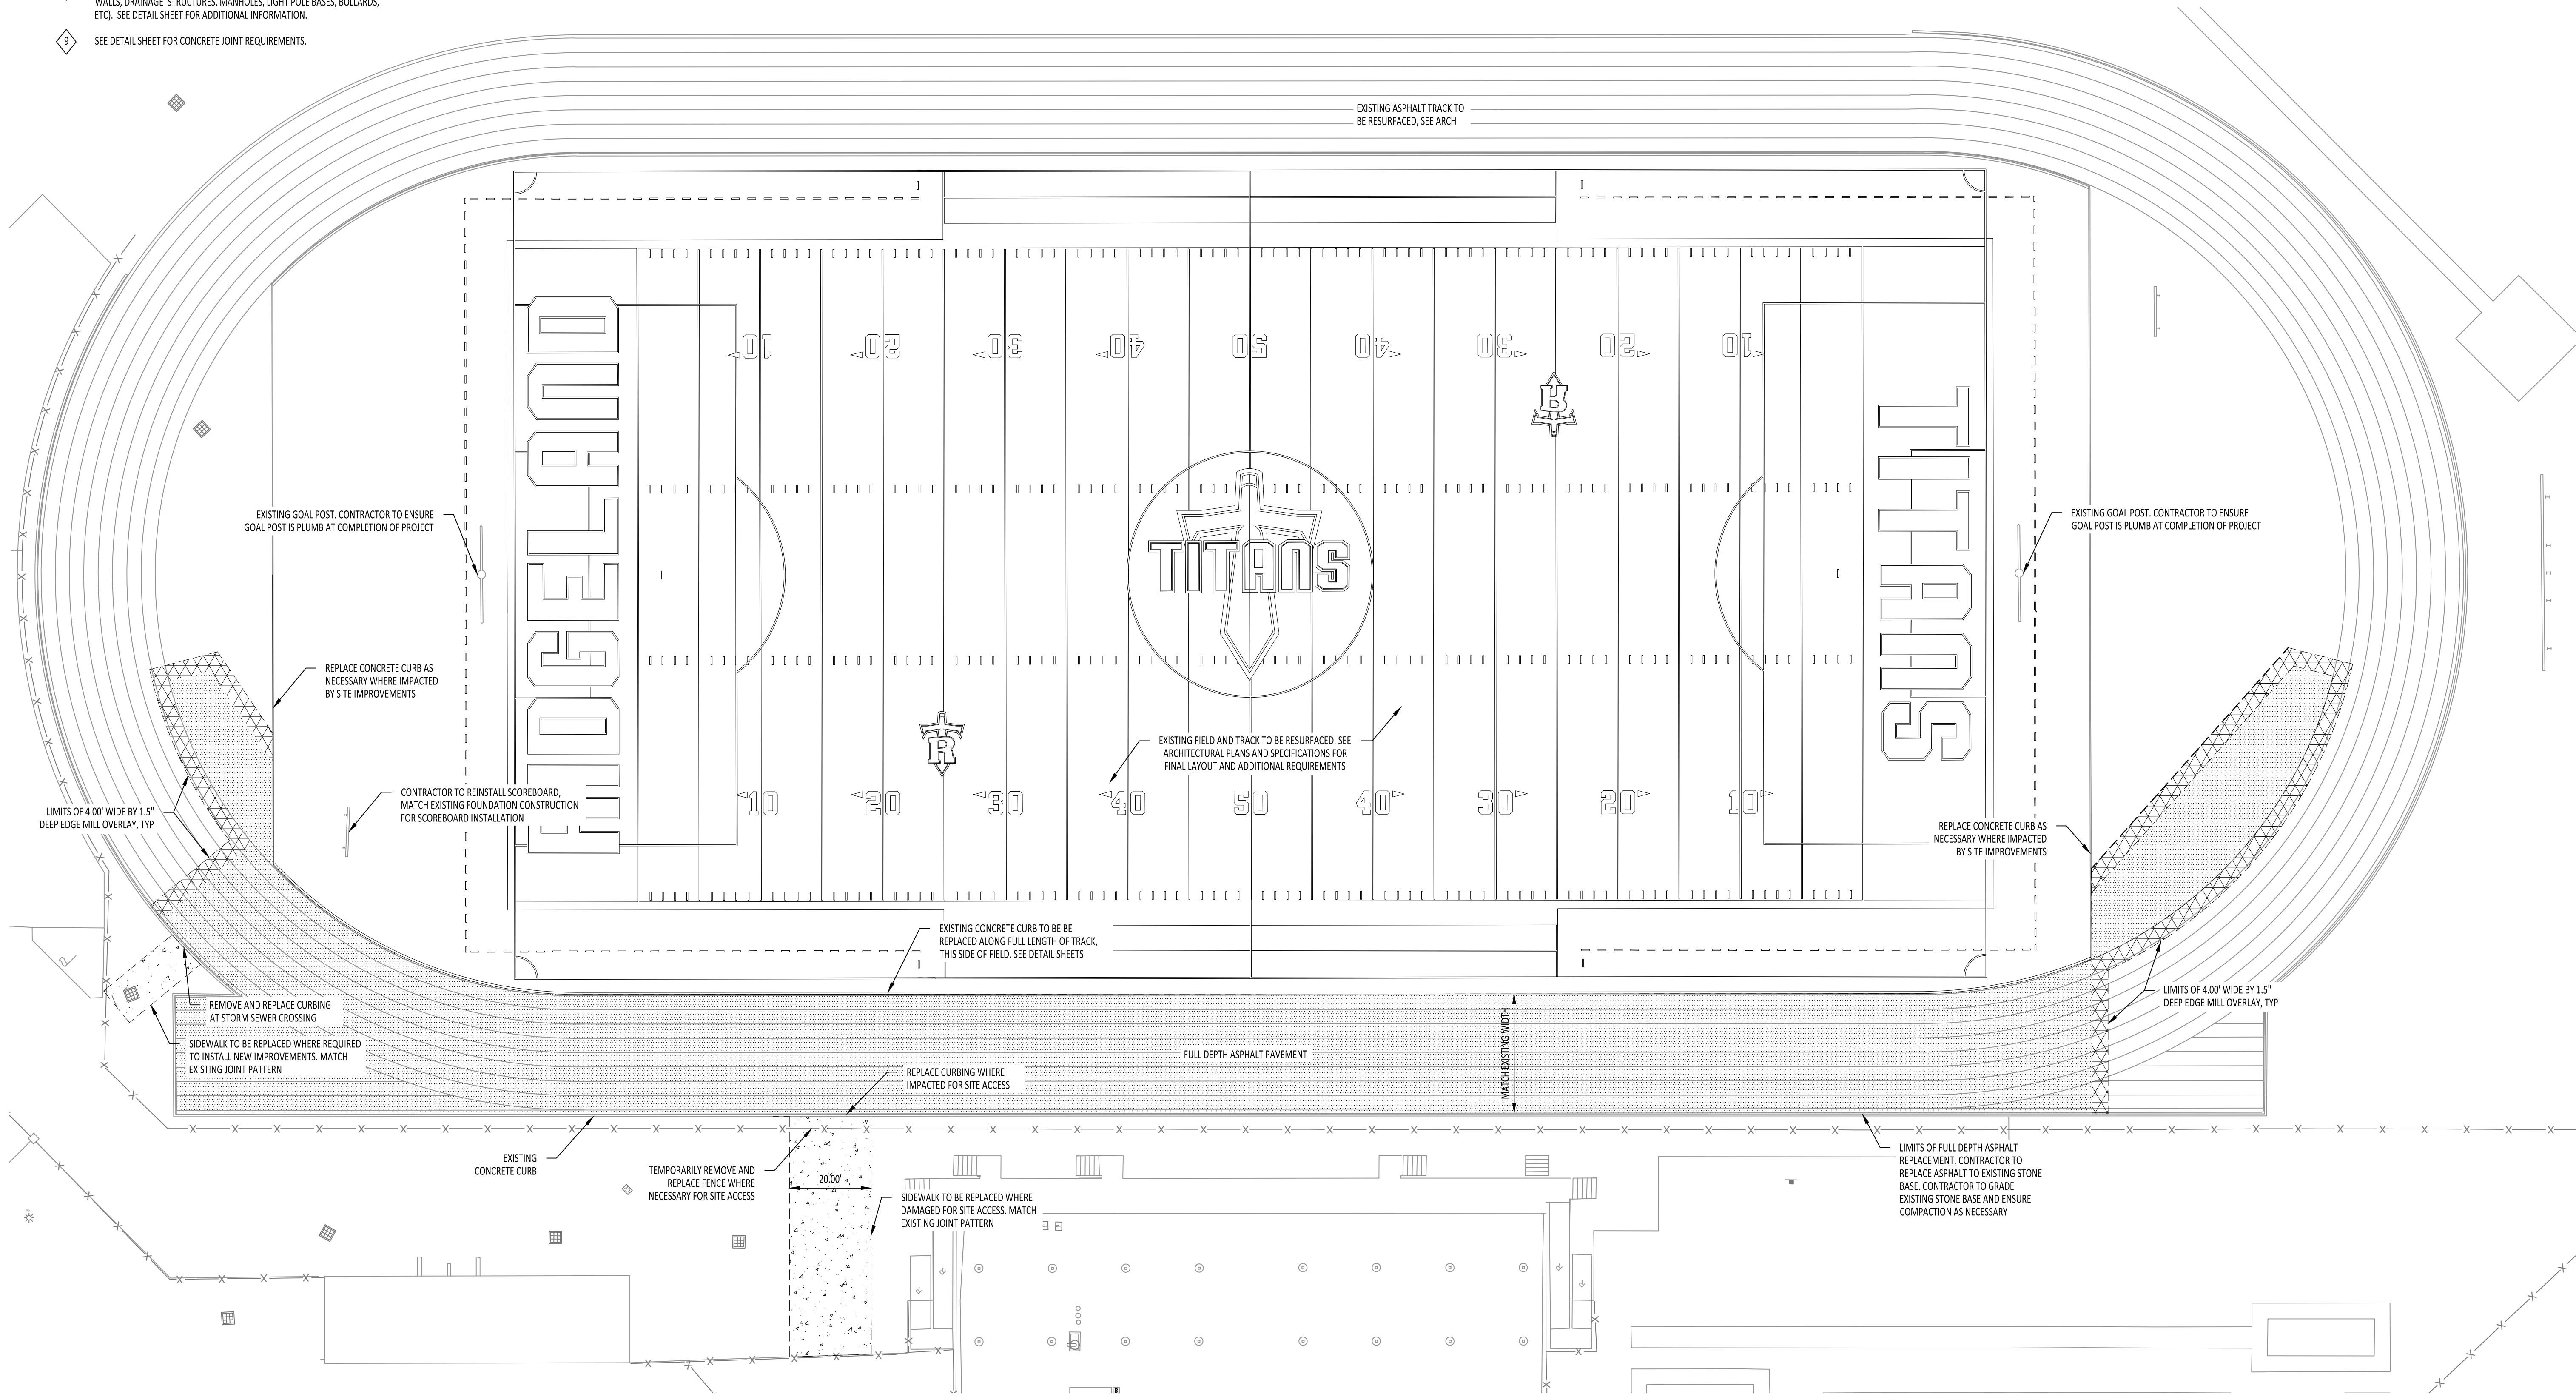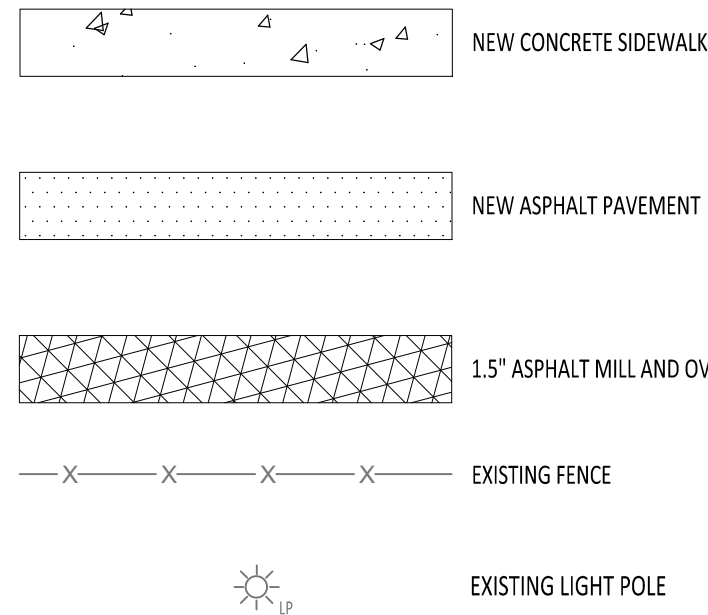

SITE PLAN
SCALE: 1"=20'-0"

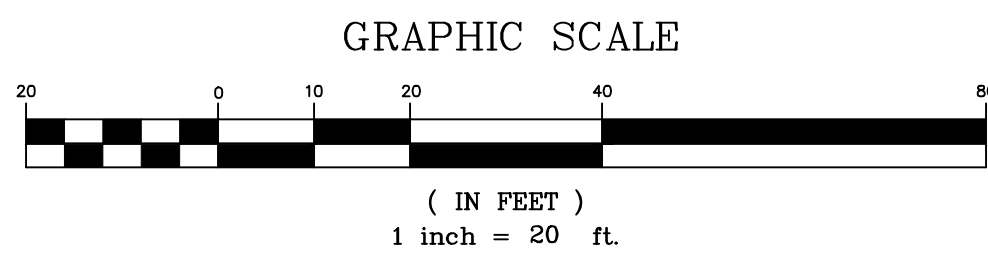

SMITHERS
ENGINEERS +
CONSULTANTS



APRIL 8, 2021

CONSTRUCTION
DOCUMENTS
WBA # 5620

REVISIONS


NO.	DESCRIPTION	DATE
-----	-------------	------

GRADING NOTES:

- 1 CONTRACTOR SHALL GRADE AREA AROUND NEW CATCH BASINS TO ENSURE POSITIVE STORM WATER DISCHARGE FROM THE DRAINAGE AREA UPSTREAM OF THE CATCH BASIN.
- 2 ALL STORM SEWER (ST S) PIPE SHALL BE CORRUGATED POLYETHYLENE (HP STORM), UNLESS NOTED OTHERWISE. ALL STORM PIPE NOTED AS PVC SHALL BE SDR 26 PVC MIN. SEE SPECIFICATIONS FOR ADDITIONAL INFORMATION.
- 3 ELEVATION OF NEW EDGE OF PAVEMENT OR SIDEWALK SHALL MATCH EXISTING.
- 4 EXISTING SLOPES GREATER THAN 6:1 SHALL BE BENCHED PRIOR TO PLACING FILL.
- 5 CONTRACTOR SHALL BE RESPONSIBLE FOR ALL NECESSARY INSPECTIONS, APPROVALS AND/OR CERTIFICATIONS REQUIRED BY CODES AND AUTHORITIES.
- 6 CATCH BASINS SHALL BE NYLOPLAST OR APPROVED EQUAL. REFER TO DETAIL SHEETS FOR ADDITIONAL INFORMATION, DRAINAGE STRUCTURE, SIZE AND PIPE CONNECTION SHALL BE SIZED TO ACCOUNT FOR SKEW OF PIPE.
- 7 CONTRACTOR SHALL ENSURE POSITIVE DRAINAGE AS SHOWN ON THIS SHEET. ANY WATER TRAPS WILL REQUIRE REMOVING AND REPLACING BY THE CONTRACTOR AT NO ADDITIONAL COST TO THE OWNER.
- 8 CONTRACTOR SHALL REFERENCE THE GEOTECHNICAL REPORT FOR ALL SUBGRADE PREPARATION AND PAVEMENT CONSTRUCTION. THE CONTRACTOR SHALL NOTIFY THE OWNER AND ENGINEER OF ANY DISCREPANCY BETWEEN THE GEOTECHNICAL REPORT AND CONSTRUCTION DOCUMENTS PRIOR TO COMMENCING CONSTRUCTION ACTIVITIES.

GRADING PLAN LEGEND:

- 206 EXISTING MINOR CONTOUR
- 200 EXISTING MAJOR CONTOUR
- S SANITARY SEWER MANHOLE
- NEW CATCH BASIN/ AREA INLET
- STORM DRAIN PIPE, NEW (ST S)
- EXSD EXSD EXISTING STORM DRAIN
- EXOHE EXOHE EXISTING OVERHEAD ELECTRIC
- EXUC EXUC EXISTING UNDERGROUND COMMUNICATIONS LINE
- EXUE EXUE EXISTING UNDERGROUND ELECTRIC
- EXSS EXSS EXISTING SANITARY SEWER LINE
- EXW EXW EXISTING WATER LINE



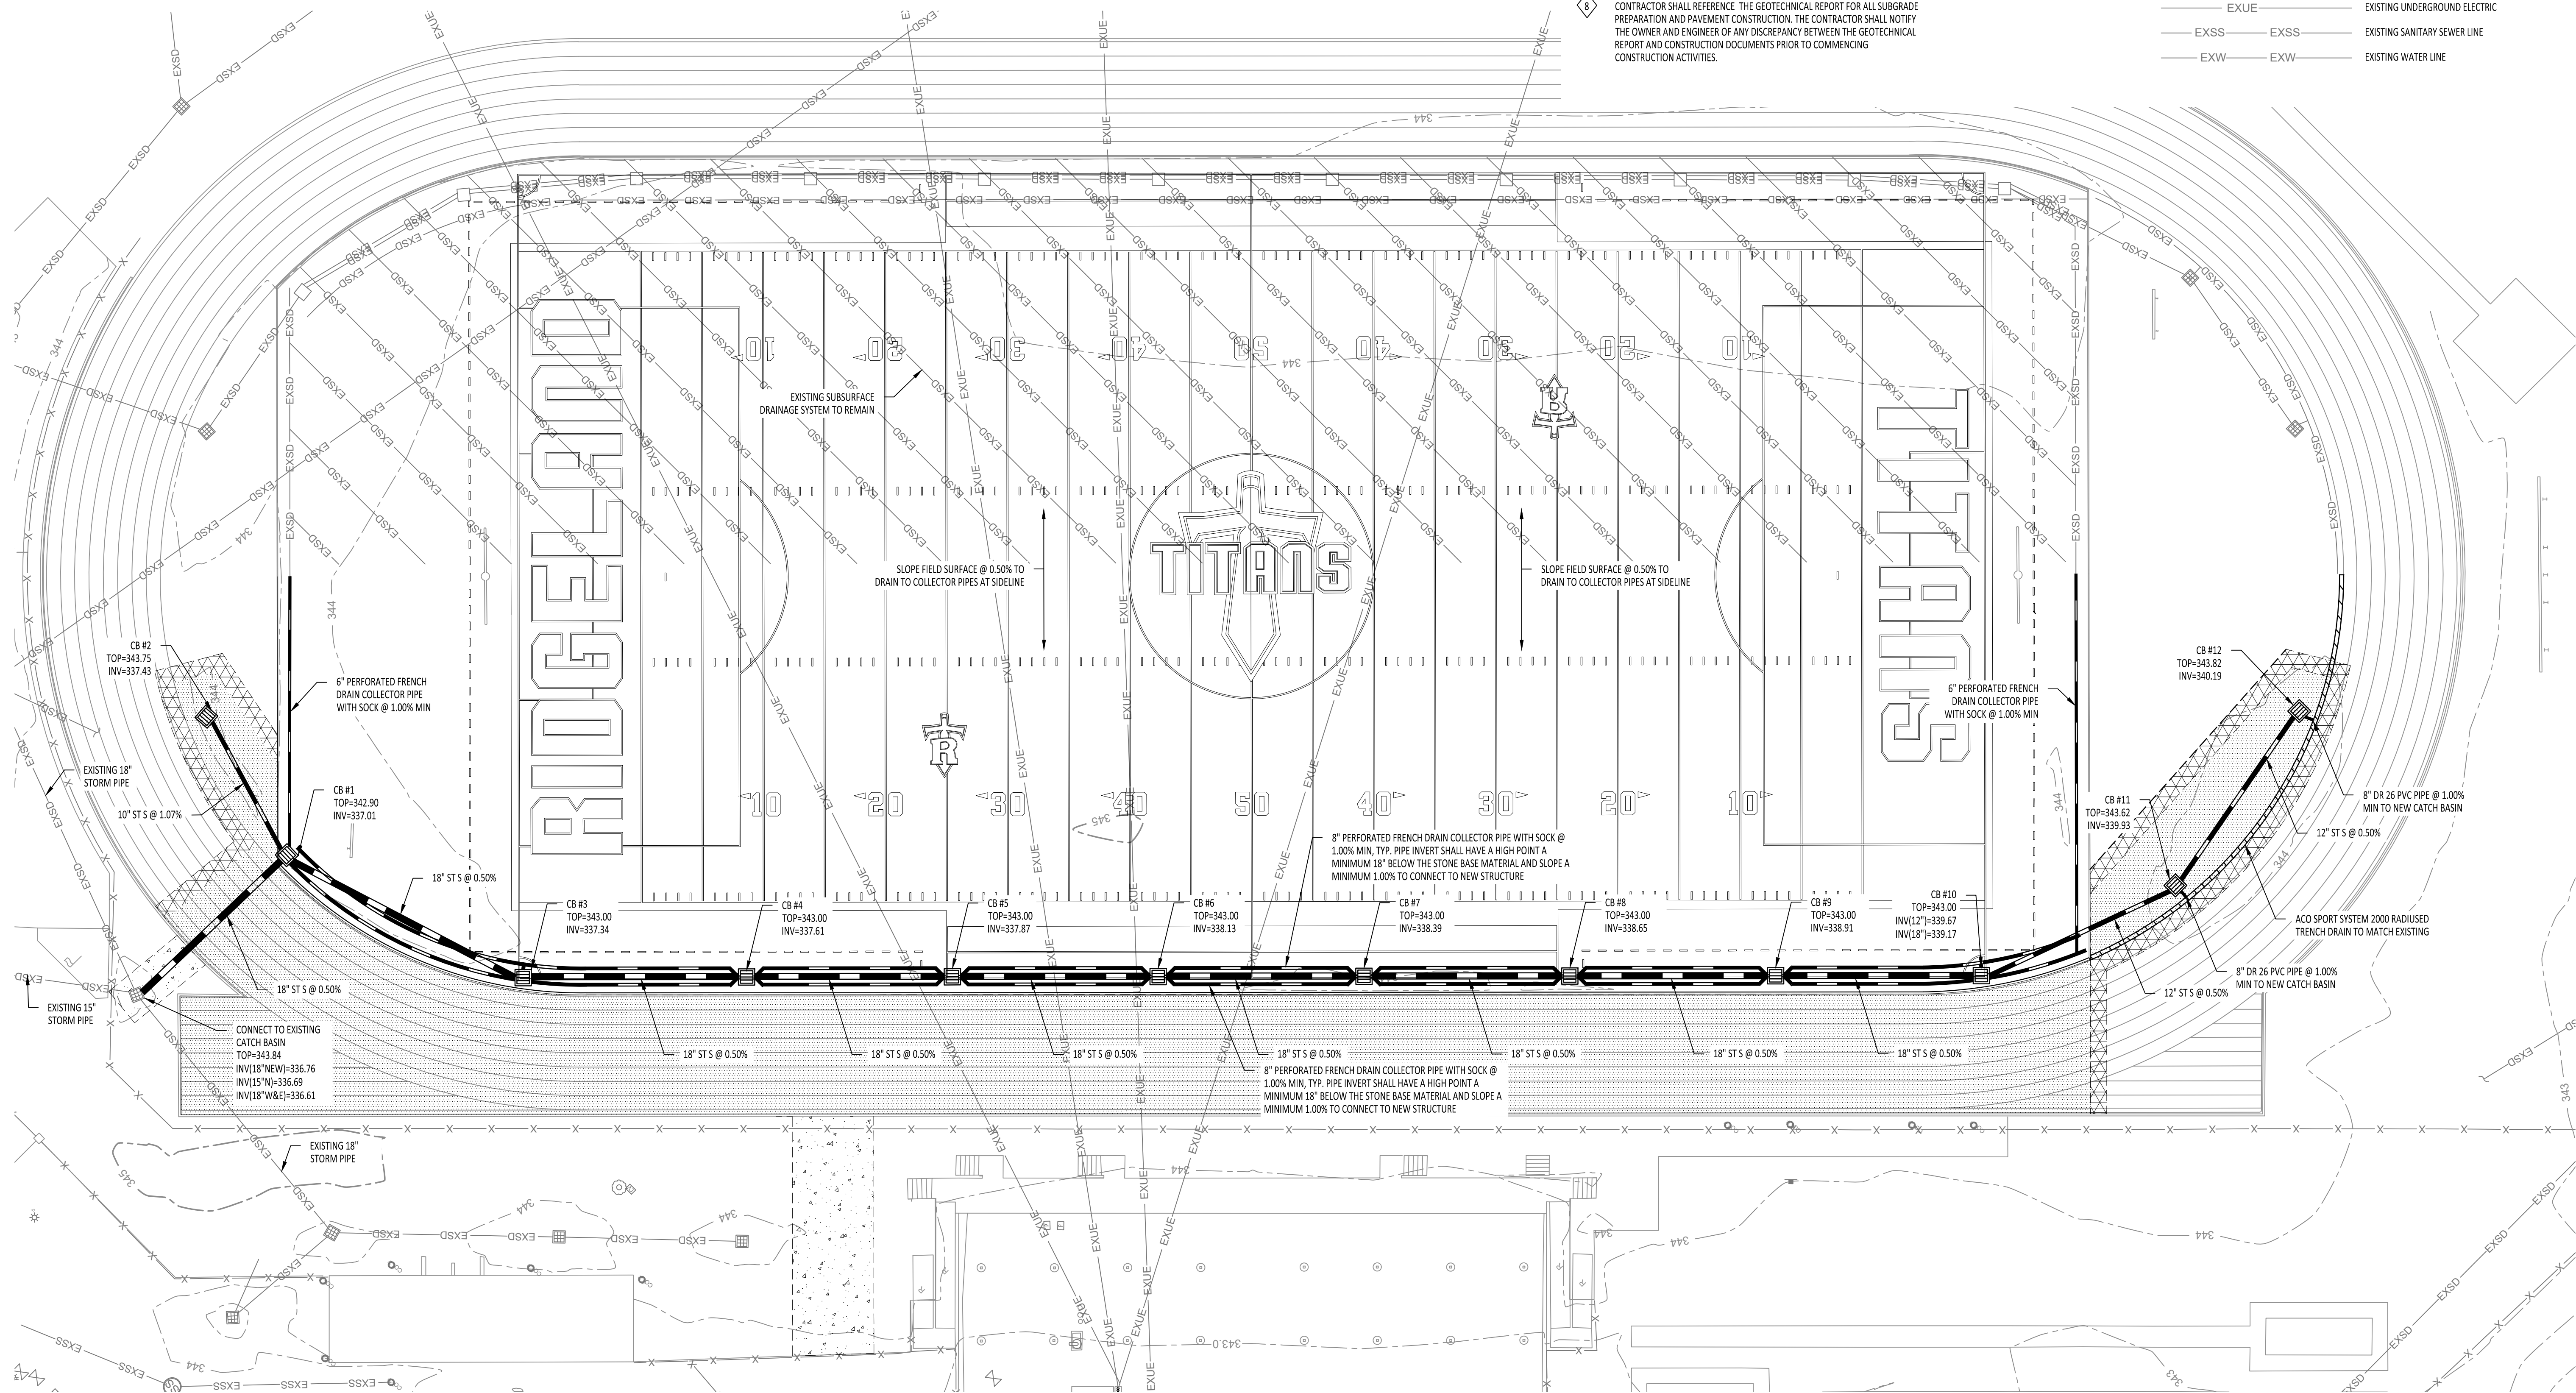



APRIL 8, 2021

CONSTRUCTION
DOCUMENTS
WBA # 5620

REVISIONS


NO. DESCRIPTION DATE



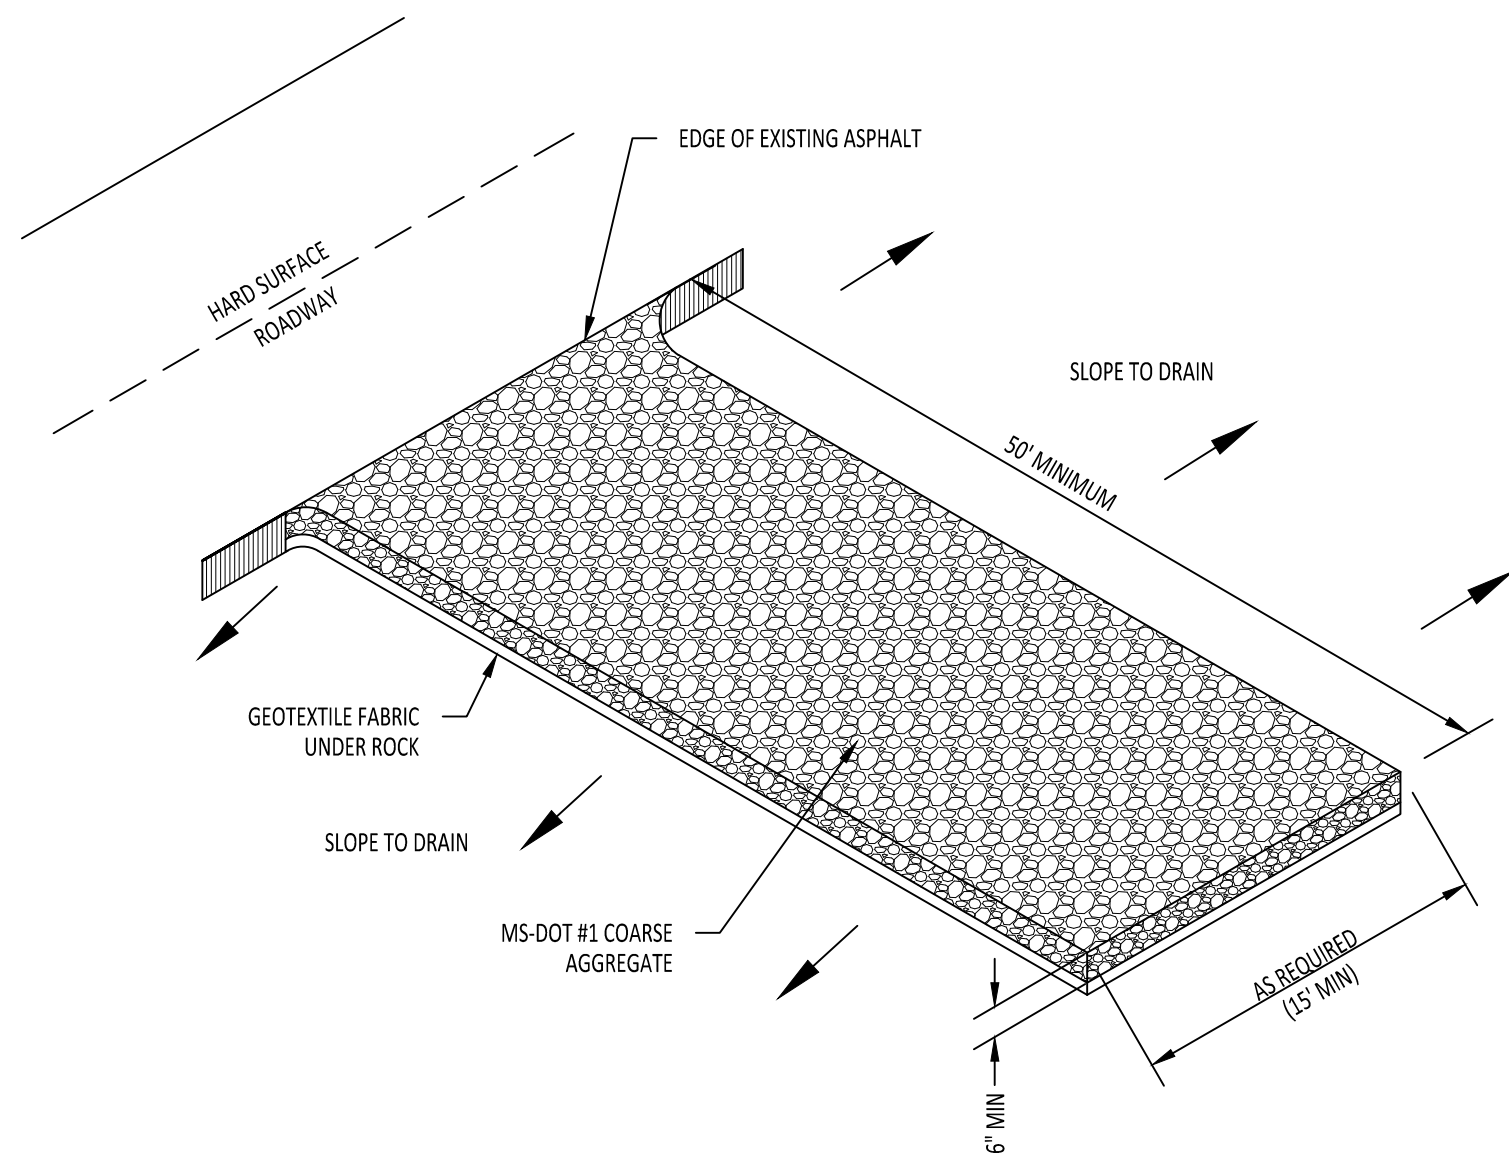



- NOTES:
1. THE AREA OF THE CONSTRUCTION EXIT SHALL BE EXCAVATED 6 INCHES DEEP, 50 FEET LONG AND SHALL EXTEND THE FULL WIDTH OF ANY VEHICULAR INGRESS AND EGRESS (MINIMUM 15 FEET) LOCATED ON THE SITE.
 2. THE EXIT SHALL BE PROPERLY MAINTAINED FOR THE DURATION OF THE PROJECT TO PREVENT THE TRACKING OF SEDIMENT ONTO PUBLIC RIGHT-OF-WAY. ALL MAINTENANCE AND REPAIRS SHALL BE THE RESPONSIBILITY OF THE CONTRACTOR.
 3. THE EXIT SHALL BE CHECKED ON A DAILY BASIS AND BEFORE AND AFTER ANY RAINFALL EVENT FOR ANY DAMAGES. ANY DAMAGES FOUND SHALL BE REMEDIATED BEFORE THE DAYS END AT NO ADDITIONAL COST TO THE OWNER.
 4. THE EXIT SHALL BE PROPERLY GRADED TO PREVENT THE FLOW OF SEDIMENT ONTO PUBLIC RIGHT-OF-WAY. ALL MATERIALS SPILLED, DROPPED, WASHED OR TRACKED FROM VEHICLES ONTO ROADWAYS OR INTO STORM DRAINS SHALL BE REMOVED IMMEDIATELY.
 5. CONSTRUCTION EQUIPMENT WHEELS MUST BE CLEANED TO REMOVE MUD PRIOR TO EGRESS FROM PROJECT SITE AND ONTO PUBLIC RIGHT-OF-WAY. WHEN WASHING IS REQUIRED, IT SHALL BE DONE ON AN AREA WITH CRUSHED STONE WHICH DRAINS INTO AN APPROVED SEDIMENT TRAP OR SEDIMENT BASIN.
 6. MEASURES SHALL BE TAKEN TO PREVENT VEHICULAR TRAFFIC FROM BYPASSING THE CONSTRUCTION EXIT DURING INGRESS AND EGRESS.
 7. REMOVE TEMPORARY CONSTRUCTION EXIT AFTER FINAL PROJECT APPROVAL BY ARCHITECT. AREA SHALL BE GRADED AND SOODED.

1
C201 **TEMPORARY CONSTRUCTION EXIT**
SCALE: NOT TO SCALE

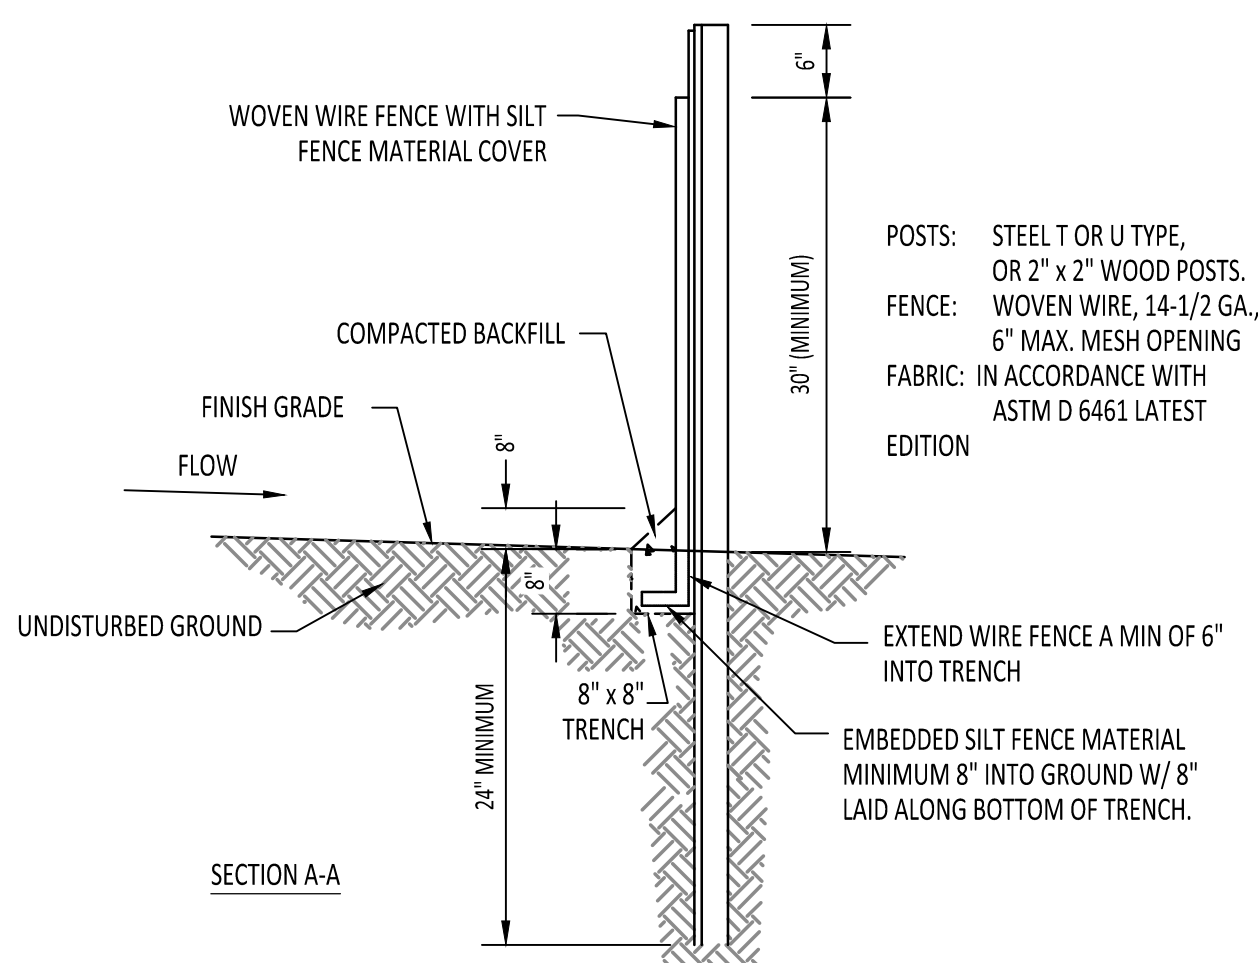

2
C201 **SEDIMENTATION/SILT FENCE WITH WIRE SUPPORT**
SCALE: NOT TO SCALE

- NOTES:
1. INSTALLATION SHALL COMPLY WITH ASTM D 6462 LATEST EDITION.
 2. ATTACH THE WOVEN WIRE FENCE TO EACH POST AND THE GEOTEXTILE TO THE WOVEN WIRE FENCE (SPACED EVERY 30") WITH THREE WIRE TIES OR OTHER FASTENERS. ALL SPACED WITHIN THE TOP 8" OF THE FABRIC. ATTACH EACH TIE DIAGONALLY 45 DEGREES THROUGH THE FABRIC, WITH EACH PUNCTURE AT LEAST 1" VERTICALLY APART. ALSO, EACH TIE PLACED ON A POST SHOULD BE POSITIONED TO HANG ON A POST NIPPLE WHEN TIGHTENED TO PREVENT SAGGING.
 3. WHEN TWO SECTIONS OF SILT FENCE MATERIAL ADJOIN EACH OTHER, THEY SHALL BE OVERLAPPED A MINIMUM OF 72" ACROSS TWO POSTS, AS SHOWN.
 4. MAINTENANCE SHALL BE PERFORMED AS NOTED IN THE SPECIFICATIONS. DEPTH OF ACCUMULATED SEDIMENTS MAY NOT EXCEED ONE-THIRD THE HEIGHT OF THE FENCE. MAINTENANCE CLEANOUT MUST BE CONDUCTED REGULARLY TO PREVENT ACCUMULATED SEDIMENTS FROM REACHING ONE-HALF THE HEIGHT OF THE SILT FENCE MATERIAL ABOVE GRADE.
 5. ALL SILT FENCE SHALL INCLUDE WIRE SUPPORT.
 6. WRAP APPROXIMATELY 6" OF FABRIC AROUND THE END POSTS AND SECURE WITH 3 TIES.
 7. COMPACT THE SOIL IMMEDIATELY NEXT TO THE SILT FENCE FABRIC WITH THE FRONT WHEEL OF THE TRACTOR, SKID STEER, OR ROLLER EXERTING AT LEAST 60 POUNDS PER SQ. INCH. COMPACT THE UPSTREAM SIDE FIRST. COMPACT EACH SIDE TWICE FOR A TOTAL OF FOUR TRIPS.
 8. ADD POST CAPS AS NEEDED BASED ON SITE CONDITIONS AND APPLICABLE AGENCY REQUIREMENTS.

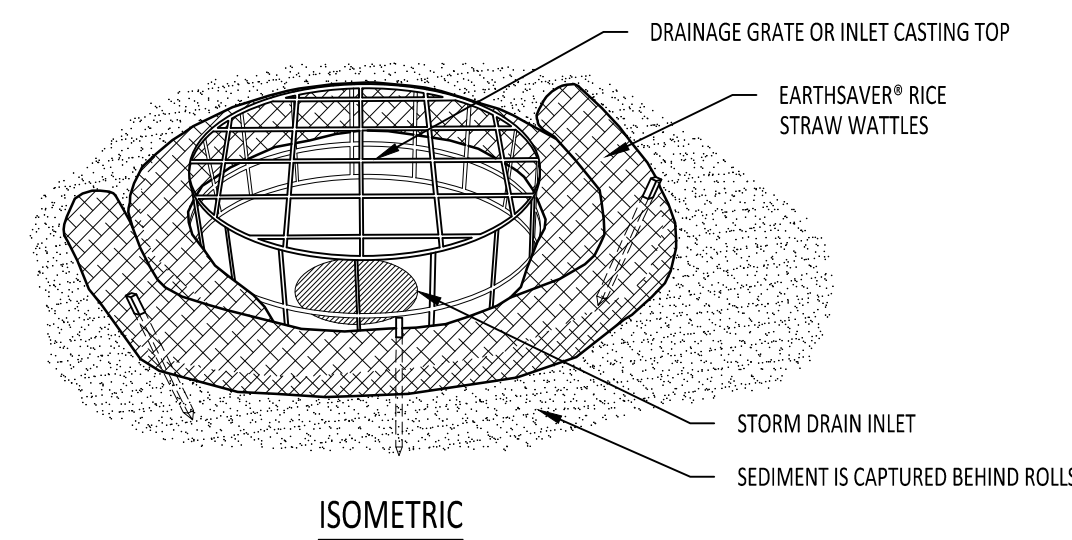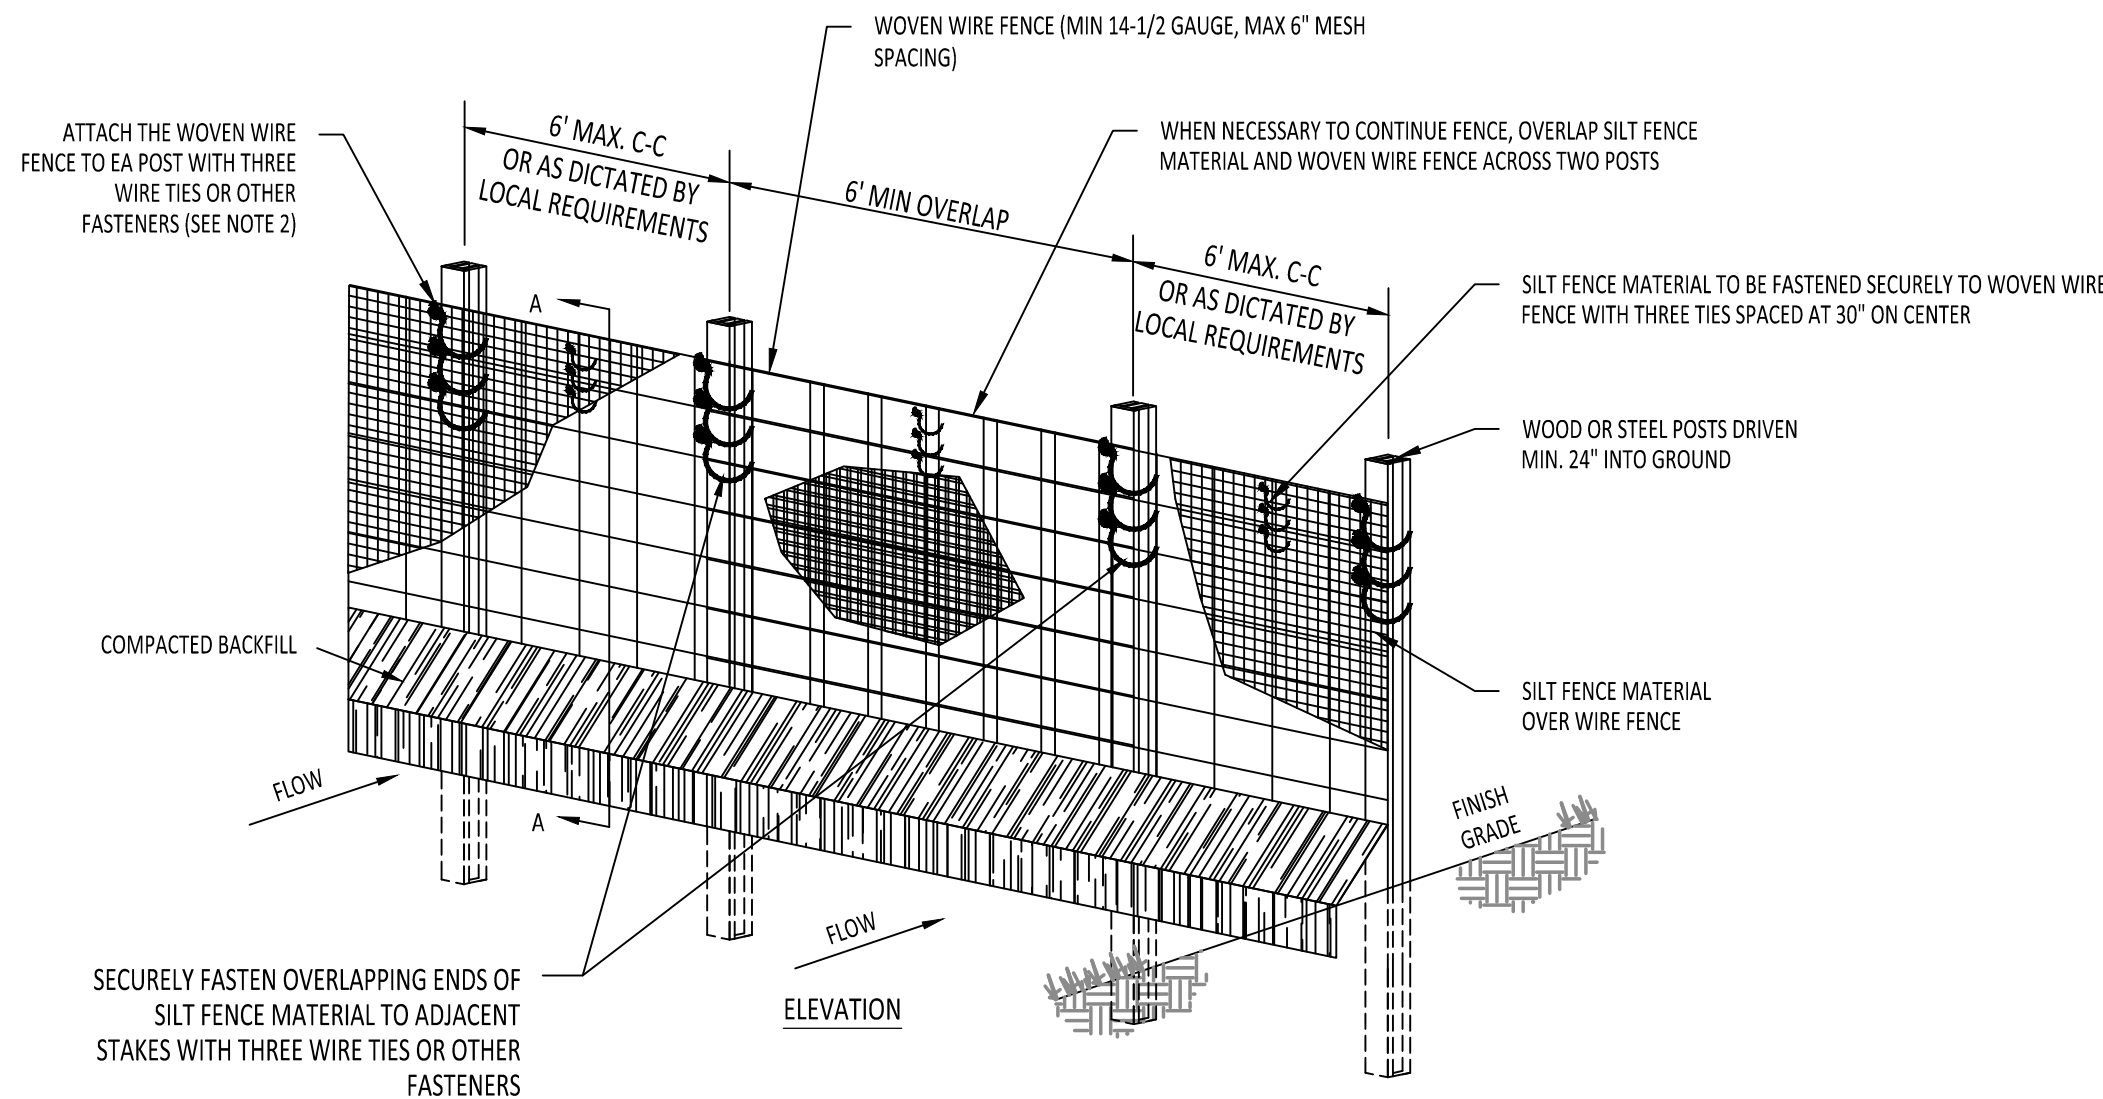

- NOTES:
1. INSTALLATION TO BE COMPLETED WITH MANUFACTURER'S SPECIFICATIONS.
 2. DO NOT SCALE DRAWINGS.
 3. FIBER ROLLS SHOULD BE INSPECTED AFTER EVERY SIGNIFICANT STORM EVENT TO CLEAR AND DISPOSE OF SEDIMENT AND DEBRIS.


3
C201 **STRAW WATTLES AT STRUCTURE**
SCALE: NOT TO SCALE



APRIL 8, 2021

**CONSTRUCTION
DOCUMENTS**
WBA # 5620


REVISIONS
NO. DESCRIPTION DATE

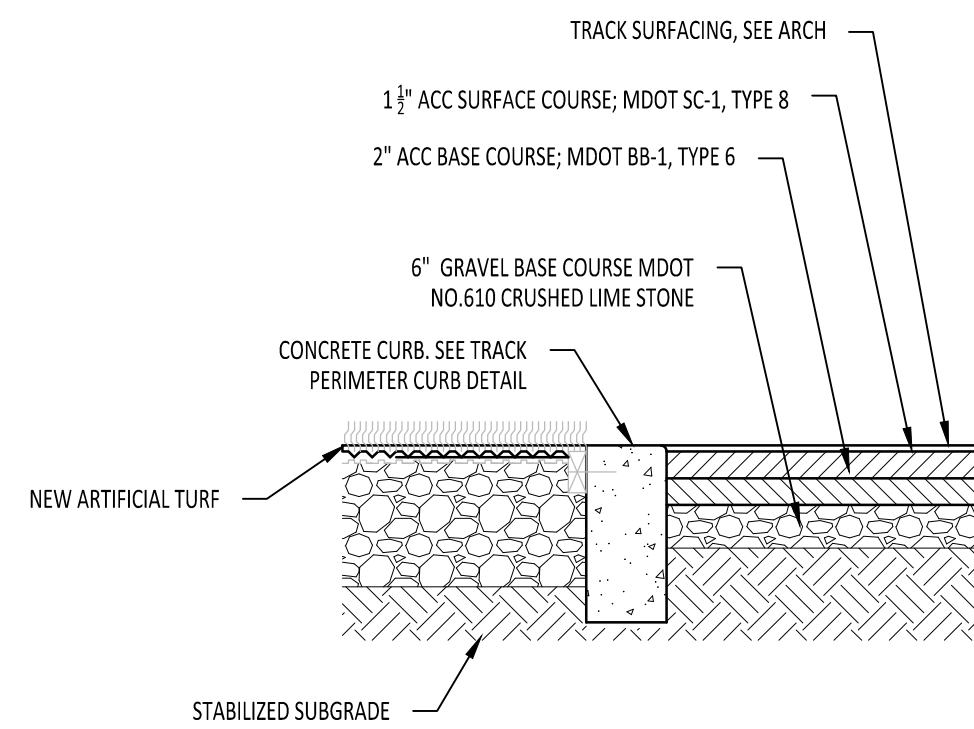


TRACK PAVING

1. FOR PREPARATION OF PAVEMENT SUBGRADE, FILL PLACED IN 9 INCH LIFTS TO WITHIN 9 INCHES OF FINISHED SUBGRADE ELEVATION IN FILL AREAS AND AT LEAST THE UPPER 9 INCHES OF SUBGRADE IN ALL AREAS TO BE PAVED SHALL BE COMPACTED TO AT LEAST 95% OF THE MATERIAL'S MAXIMUM STANDARD PROCTOR DRY DENSITY (ASTM D-698). FILL PLACED BELOW THIS LEVEL SHALL BE COMPACTED TO AT LEAST 95% OF THE MATERIAL'S MAXIMUM DRY DENSITY. THE SOIL'S WATER CONTENT SHALL BE AT -3% TO +3% OF THE SOIL'S OPTIMUM MOISTURE VALUE AT TIME OF COMPACTION. WHERE HAND OPERATED MECHANICAL TAMPERS ARE USED, THE LOOSE LIFT THICKNESS SHALL NOT EXCEED 5".
2. AFTER PROOFROLLING WITH A LOADED TANDEM AXLE DUMP TRUCK AND REPAIRING DEEP SUBGRADE DEFICIENCIES, THE ENTIRE SUBGRADE SHALL BE SCARIFIED TO A DEPTH OF 6 INCHES AND UNIFORMLY COMPACTED TO AT LEAST 95% OF STANDARD PROCTOR.
3. AGGREGATE GRAVEL BASE COURSE MIXTURES SHALL BE MDOT SIZE NO. 610 CRUSHED LIMESTONE, COMPACTED TO 100% OF THE MAXIMUM DRY DENSITY IN ACCORDANCE WITH ASTM D-698(STANDARD PROCTOR) AT -2% TO +2% OF THE SOILS OPTIMUM MOISTURE CONTENT AT THE TIME OF COMPACTION.
4. ASPHALT CONCRETE SURFACE COURSE SHALL BE MDOT SC-1, TYPE 8 AND ASPHALT CONCRETE BASE COURSE SHALL BE MDOT BB-1, TYPE 6 IN ACCORDANCE WITH THE 1990 EDITION OF THE MISSISSIPPI STANDARD SPECIFICATION FOR ROAD AND BRIDGE CONSTRUCTION.
5. THE PORTLAND CEMENT CONCRETE PAVEMENT MIXTURE SHALL BE IN ACCORDANCE WITH AIR-ENTRAINED CONCRETE FOR PAVEMENT AS PER ASTM C-31. PORTLAND CEMENT CONCRETE SHALL BE CONSTRUCTED IN ACCORDANCE WITH THE LATEST ACI, ASTM, AND PCA STANDARDS, INCLUDING THICKENED EXTERIOR EDGES AND CORNERS, AND LOAD TRANSFER DEVICES. THE MIXTURE SHALL BE DESIGNED TO DEVELOP A MINIMUM COMPRESSIVE STRENGTH OF 4000 PSI AT 28 DAYS.
6. CONTRACTOR SHALL PROVIDE A PRIME COAT AND TACK COAT. SEE PROJECT SPECIFICATIONS FOR ADDITIONAL INFORMATION.
7. PAVEMENT PREPARATION AND CONSTRUCTION SHALL BE IN CONFORMANCE WITH ALL GEOTECHNICAL RECOMMENDATIONS. THE ENGINEER SHALL BE NOTIFIED OF ANY DISCREPANCY BETWEEN THE PLANS AND GEOTECHNICAL REPORT PRIOR TO COMMENCING CONSTRUCTION ACTIVITIES.


1 TRACK PAVEMENT SECTION
SCALE: NOT TO SCALE

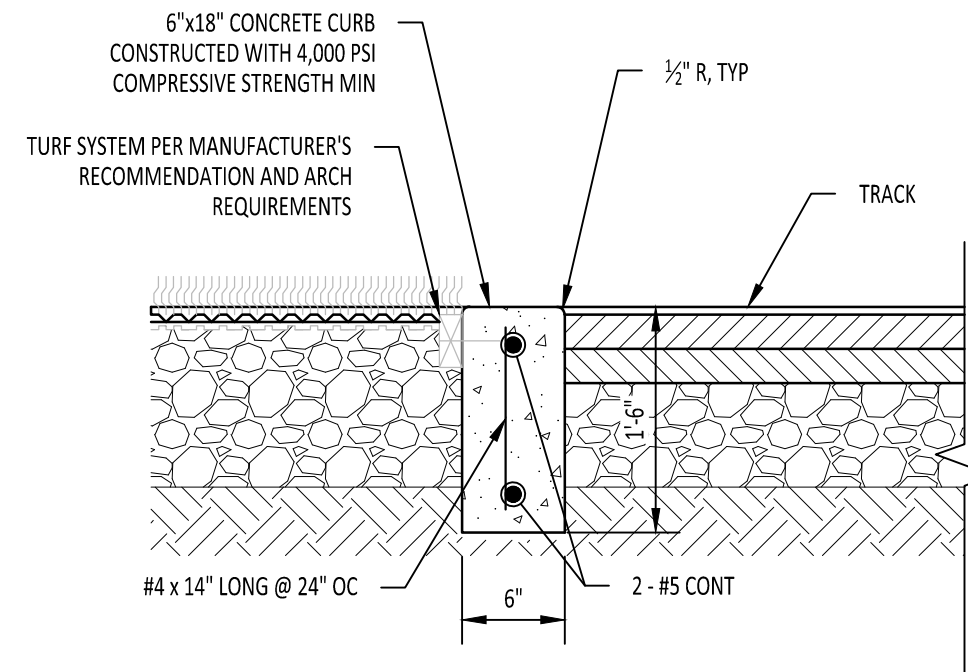

2 TRACK PERIMETER CURB
SCALE: NOT TO SCALE

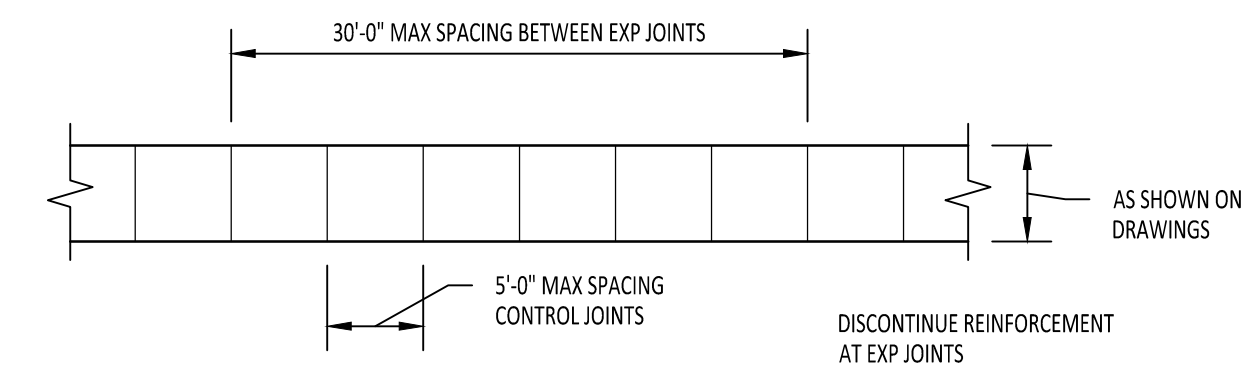


TYPICAL PLAN

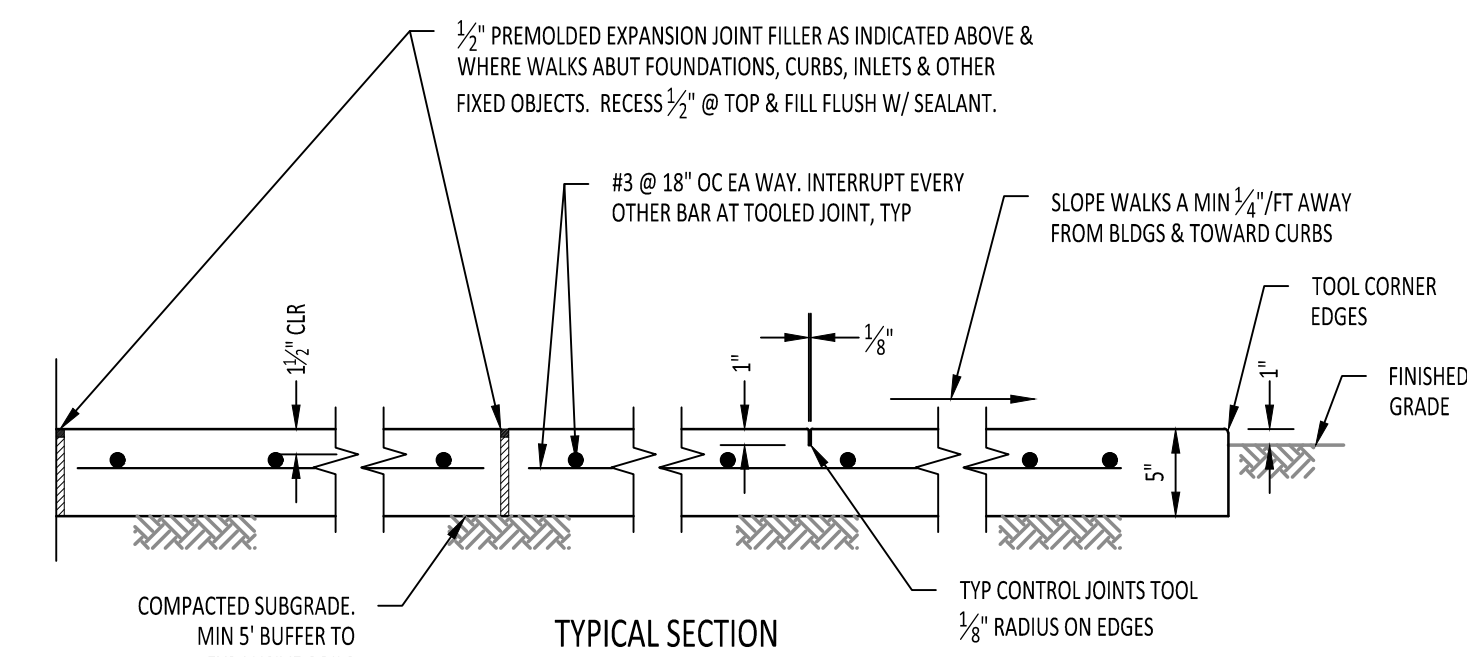


TYPICAL SECTION

3 CONCRETE SIDEWALK
SCALE: NOT TO SCALE

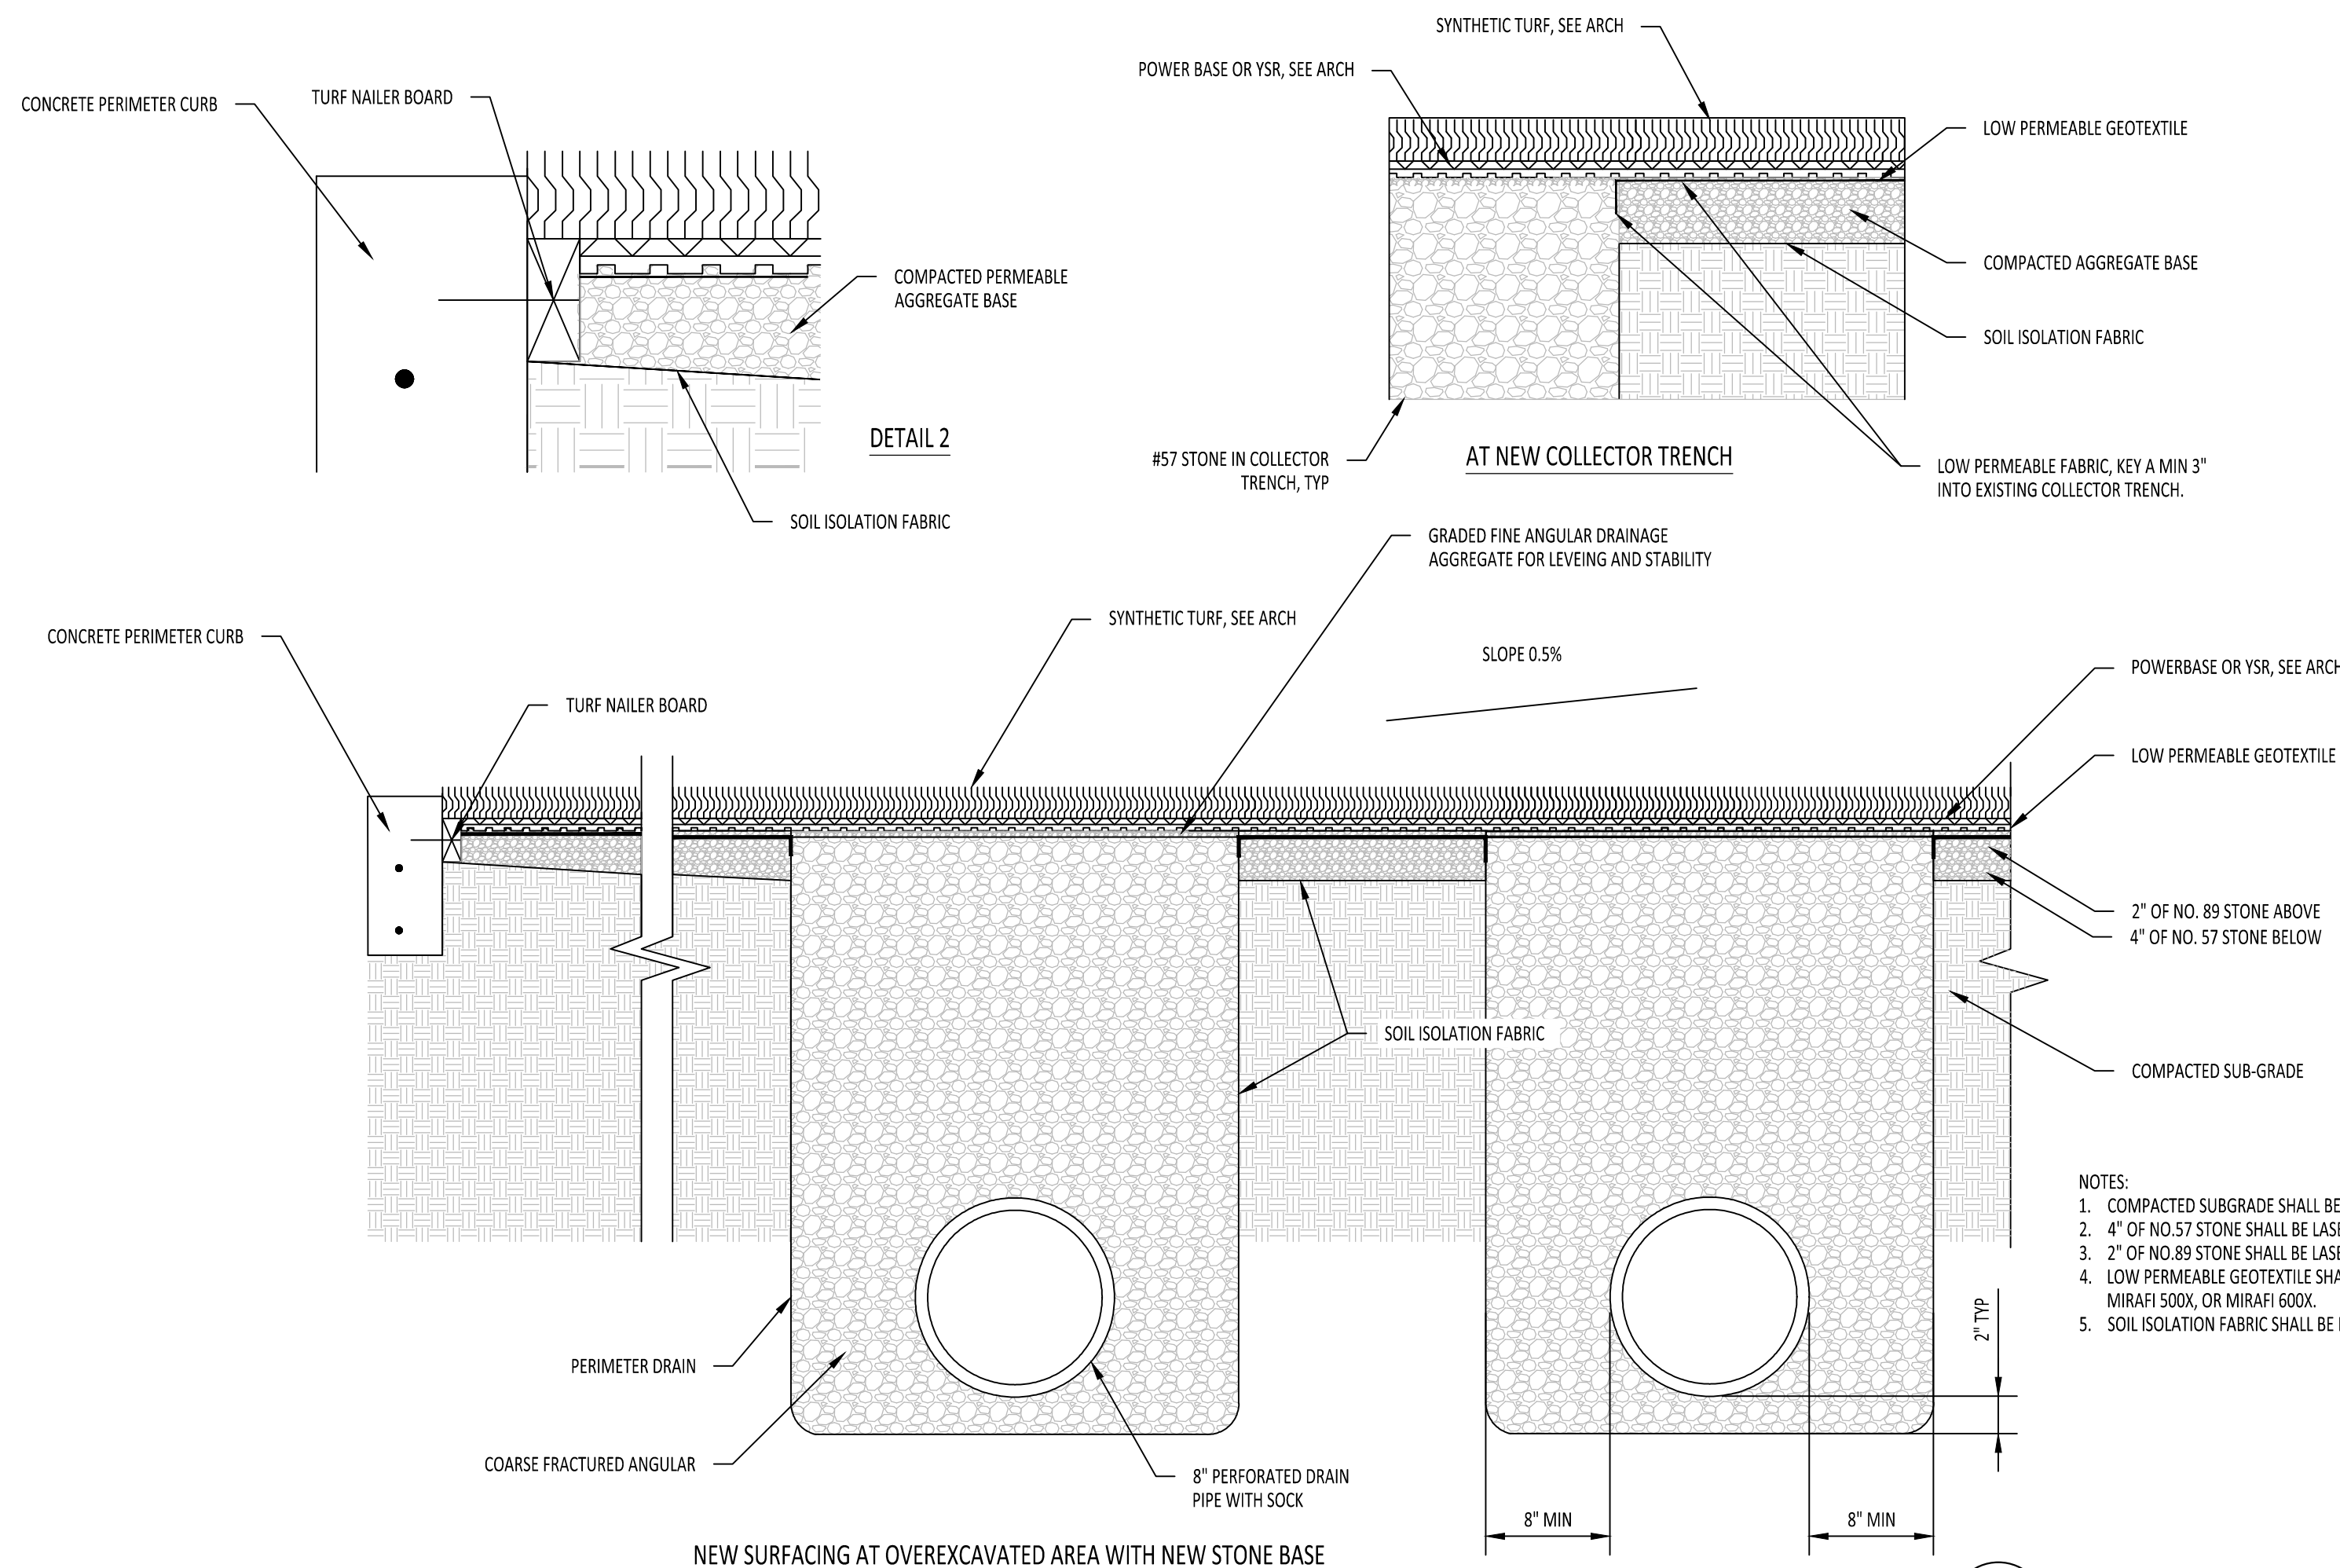

- NOTES:
1. COMPACTED SUBGRADE SHALL BE LASER GRADED
 2. 4" OF NO.57 STONE SHALL BE LASER GRADED
 3. 2" OF NO.89 STONE SHALL BE LASER GRADED
 4. LOW PERMEABLE GEOTEXTILE SHALL BE DUPONT SF65, MIRAFI 500X, OR MIRAFI 600X.
 5. SOIL ISOLATION FABRIC SHALL BE MIRAFI 140N, OR EQUAL

4 FIELD SECTIONS AND COLLECTOR PIPE DETAILS
SCALE: NOT TO SCALE

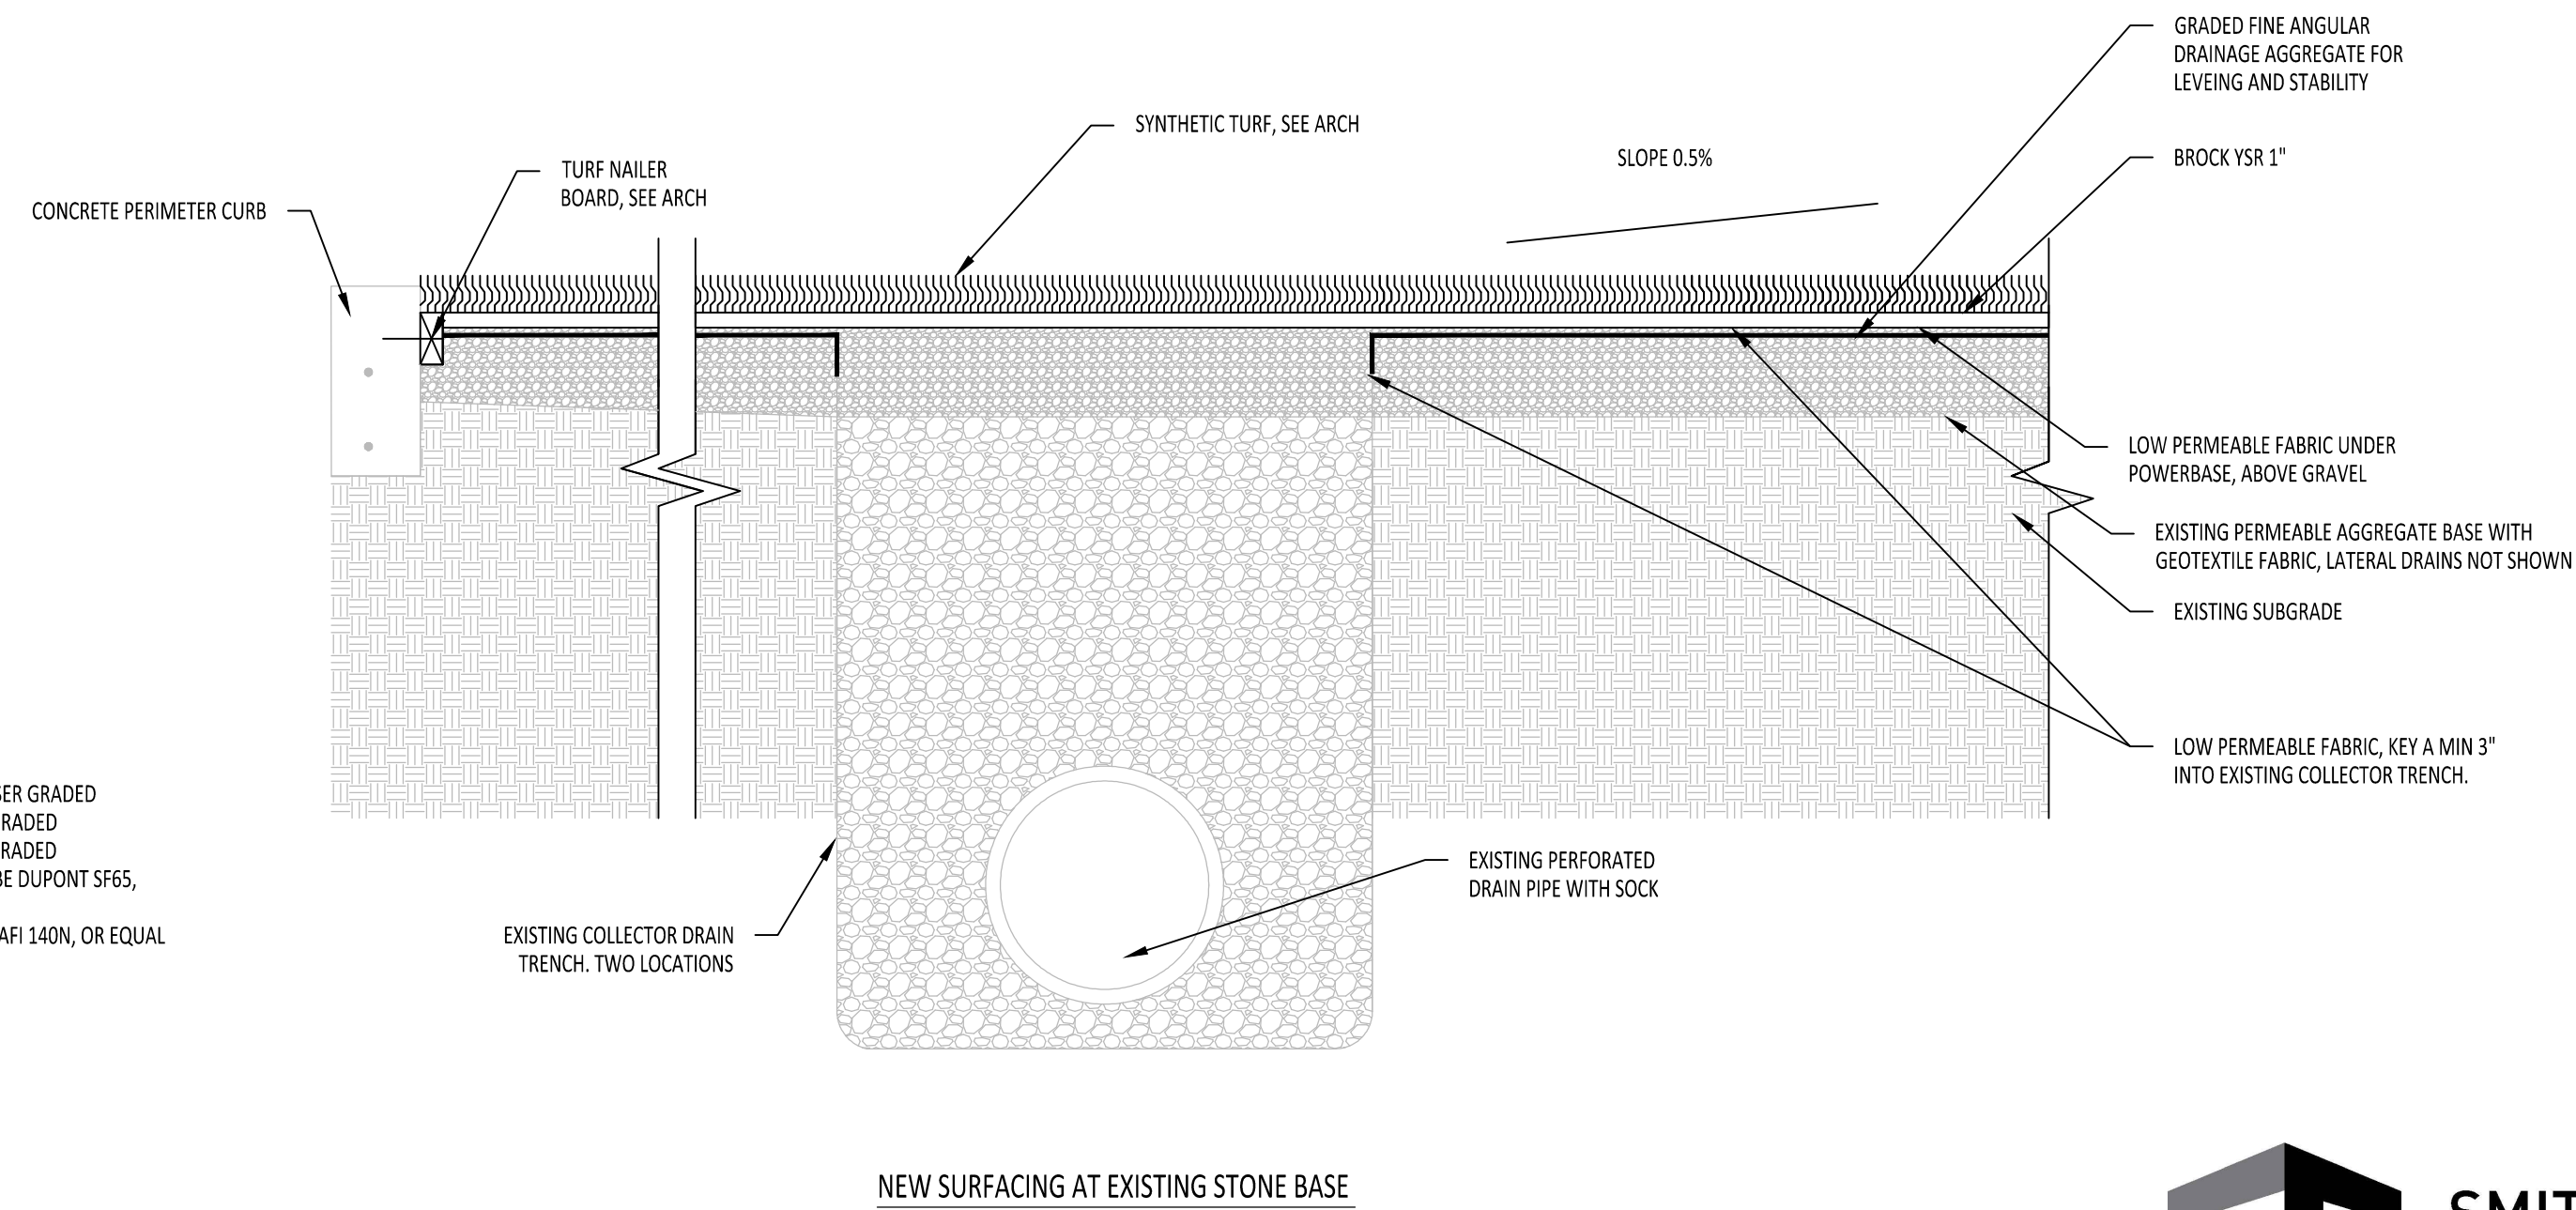


NEW SURFACING AT EXISTING STONE BASE




APRIL 8, 2021

CONSTRUCTION
DOCUMENTS
WBA # 5620


REVISIONS
NO. DESCRIPTION DATE

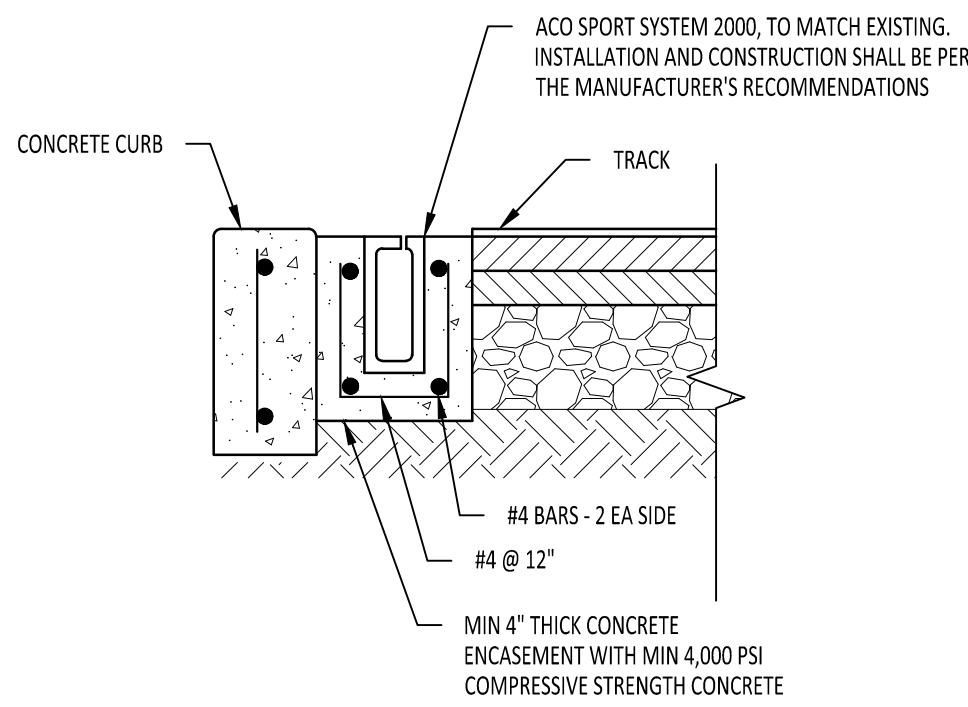


1
C203 TRENCH DRAIN DETAIL
SCALE: NOT TO SCALE

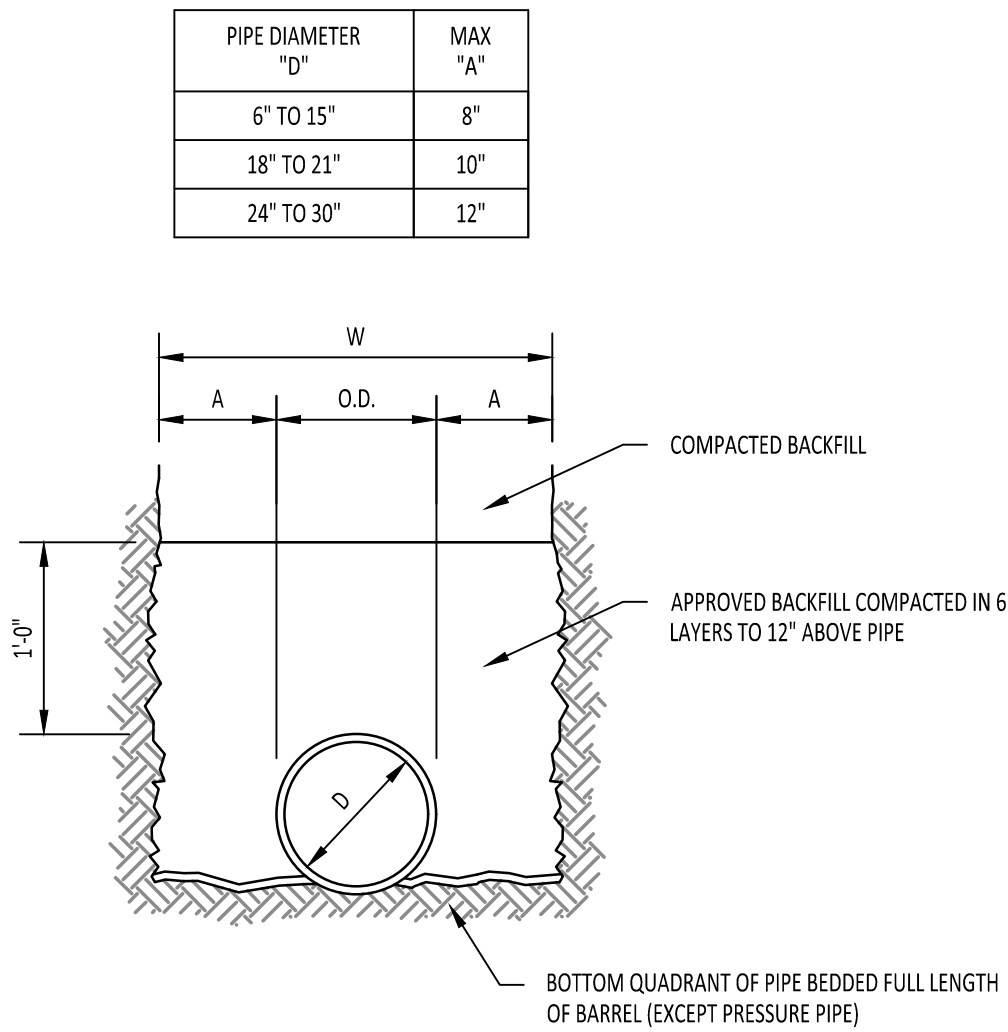

2
C203 UTILITY CONDUIT
SCALE: NOT TO SCALE

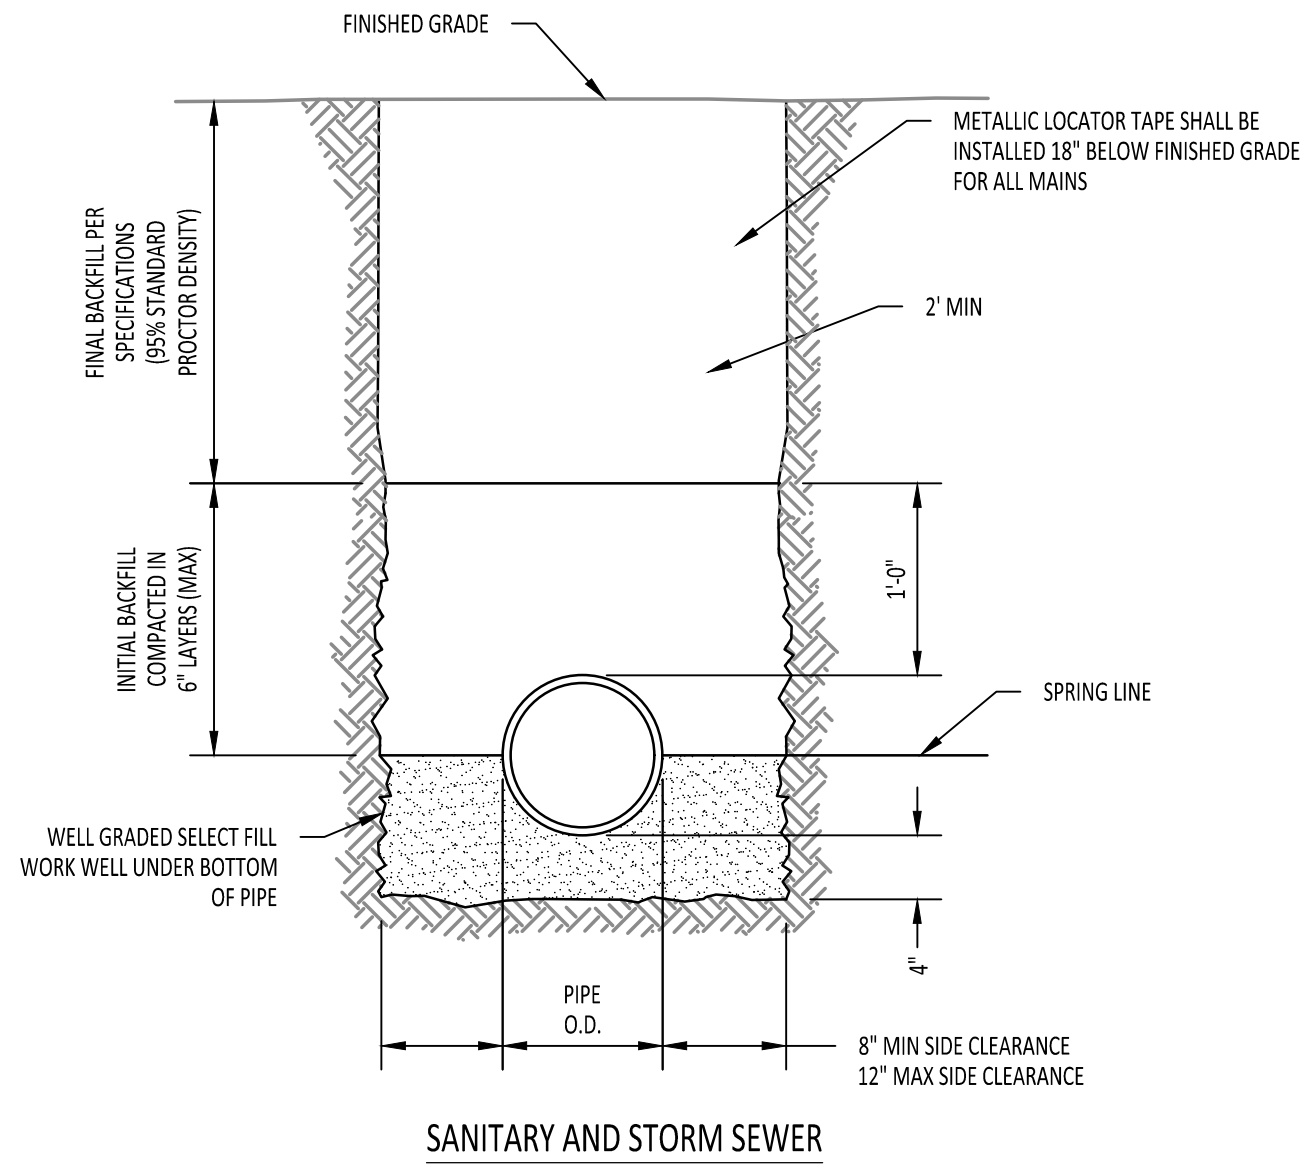


SANITARY AND STORM SEWER

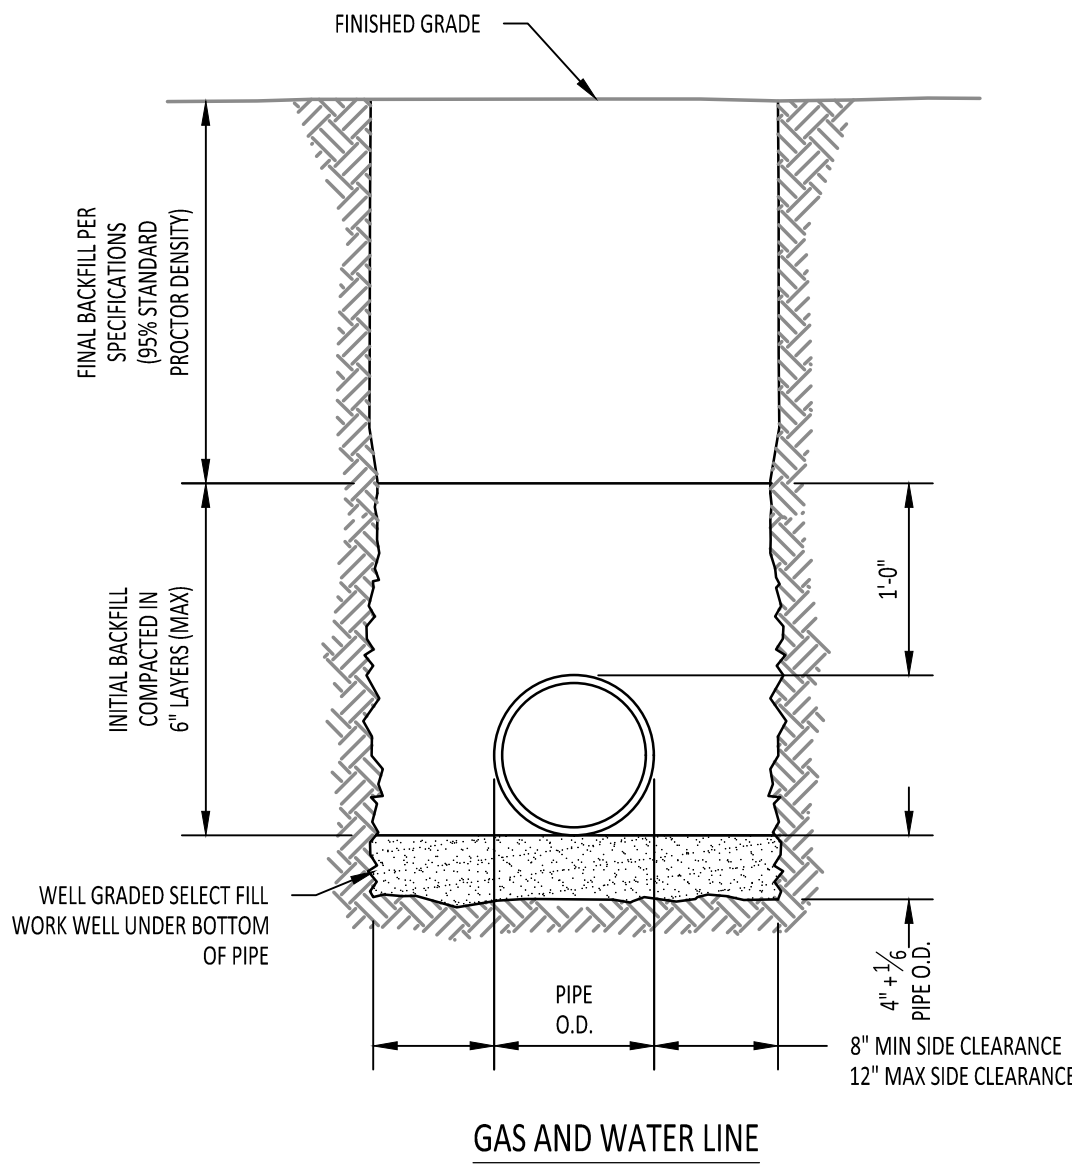


GAS AND WATER LINE

NOTE: FOR TRENCHES REQUIRING SHORING & BRACING, DIMENSIONS SHALL BE TAKEN FROM THE INSIDE FACE OF THE SHORING & BRACING.

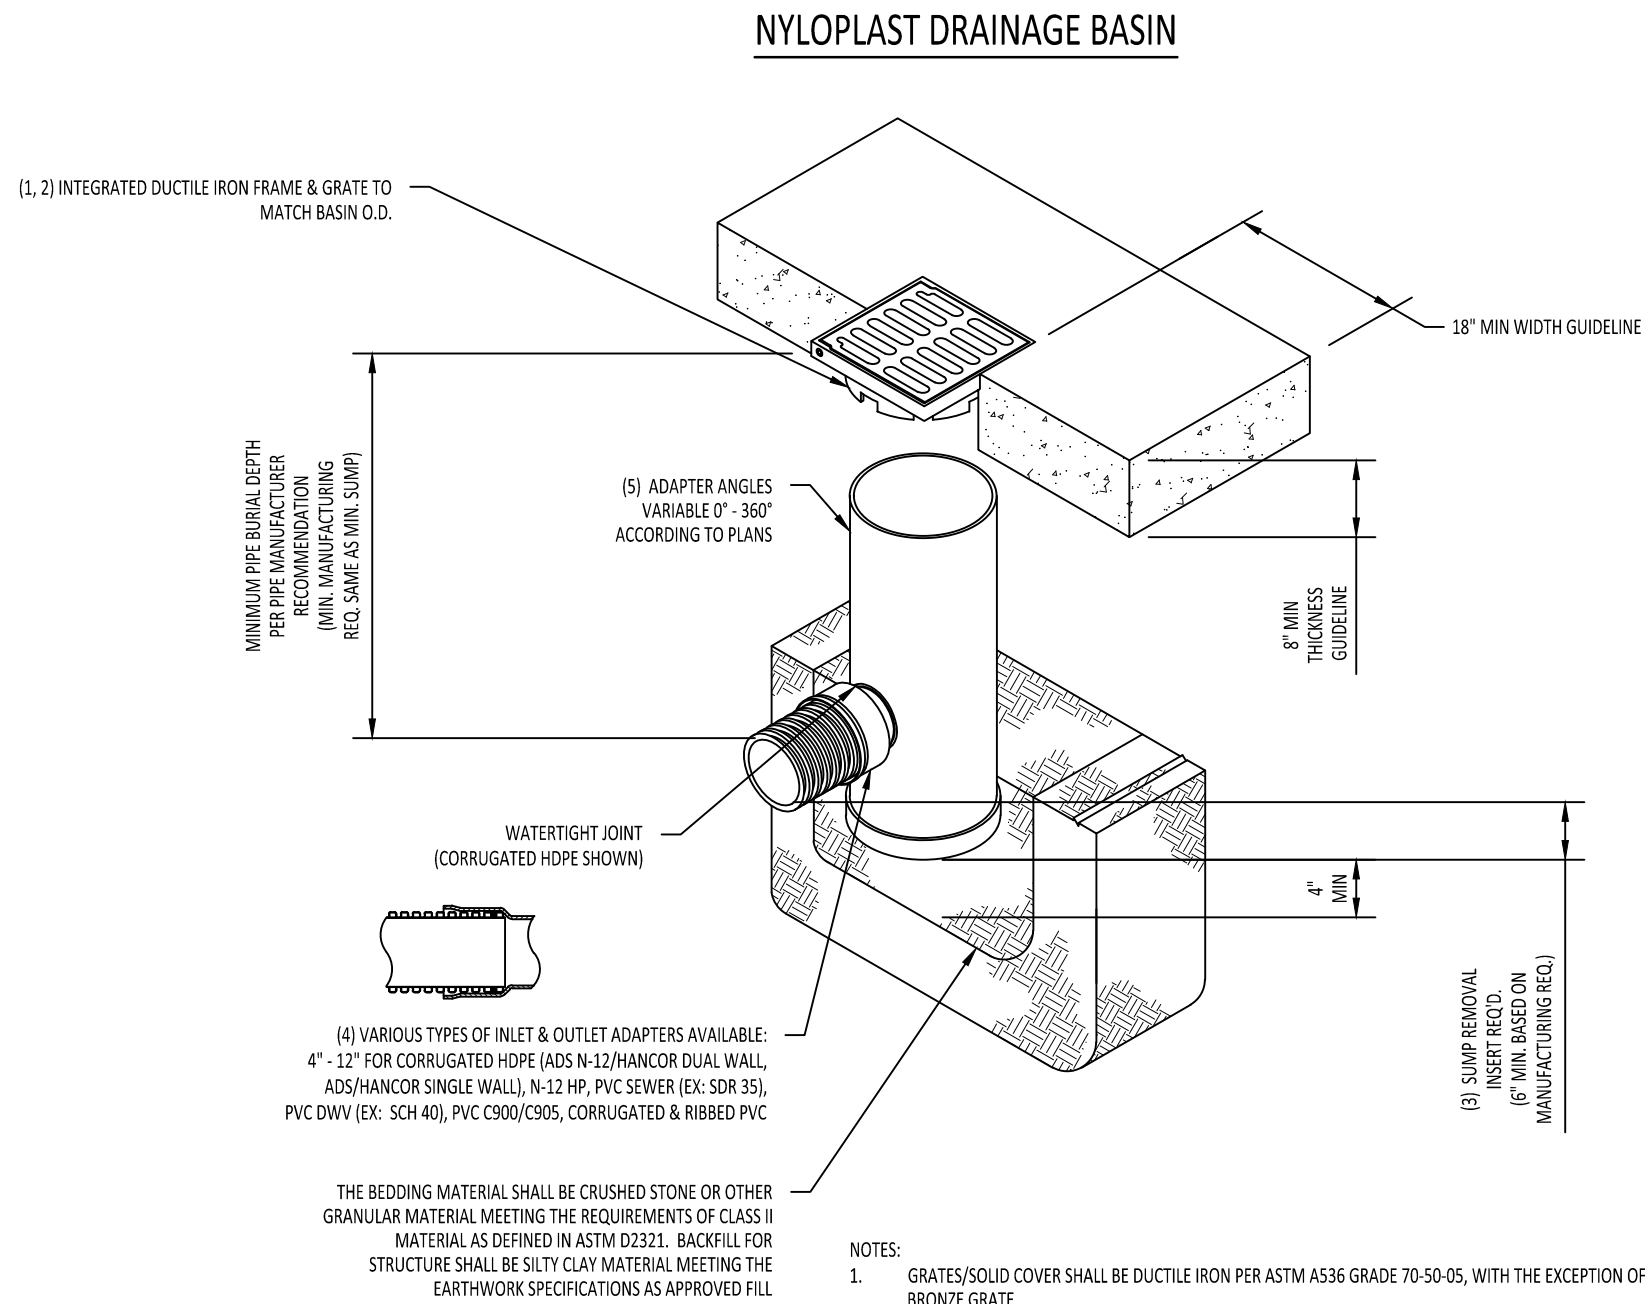

GRATE OPTIONS	LOAD RATING
PEDESTRIAN	MEETS H-10
STANDARD	MEETS H-20
SOLID COVER	MEETS H-20

- NOTES:
- GRATES/SOLID COVER SHALL BE DUCTILE IRON PER ASTM A536 GRADE 70-50-05, WITH THE EXCEPTION OF THE BRONZE GRATE.
 - FRAMES SHALL BE DUCTILE IRON PER ASTM A536 GRADE 70-50-05.
 - DRAIN BASIN TO BE CUSTOM MANUFACTURED ACCORDING TO PLAN DETAILS.
 - DRAINAGE CONNECTION STUB JOINT TIGHTNESS SHALL CONFORM TO ASTM D3212 FOR CORRUGATED HOPE (ADS N-12/HANCOR DUAL WALL), N-12 HP, & PVC SEWER AND SHALL BE WATERTIGHT.
 - ADAPTERS CAN BE MOUNTED ON ANY ANGLE 0° TO 360°.
 - ALL INLETS SHALL RECEIVE SLUMP REMOVAL INSERTS.

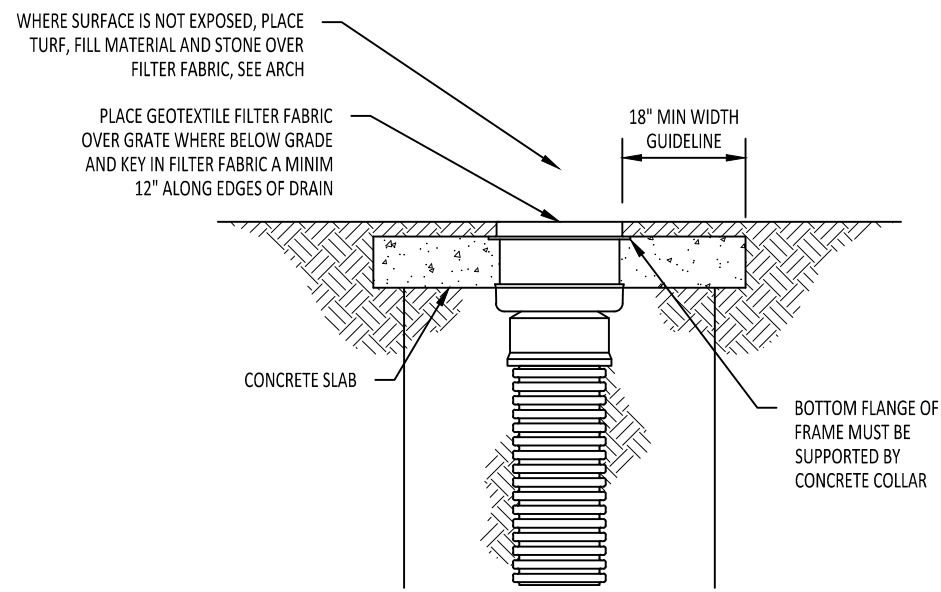

INLINE DRAIN

3
C203 NYLOPLAST DRAINAGE STRUCTURE
SCALE: NOT TO SCALE
